



Construction Monitoring Services, Inc.

Stow Pompositicut/Center Elementary School

OPM Monthly Status Report November 2010

Owner's Representatives

Project Managers

Construction Managers

*Submitted by: Paul Griffin, OPM
December, 2010*

270 Main Street
Marlboro, Massachusetts 01752
Tel: (508) 786-0600
Fax: (508) 786-0608
Email: cms@cms-ma.com

Monthly Status Report

Pompositticut / Center Elementary School

Stow, MA

November, 2010

Size: 98,050 SF
Enrollment: 660 Students
Reimbursement Rate: 52.11%

Project Team:

Owner's Project Manager: Construction Monitoring Services, Inc.
Paul Griffin (617) 429-5100
Neil Joyce (508) 808-1601

Architect: Symmes, Maini & McKee
Phil Poinelli – (617) 547-5400
Lorraine Finnigan – (617) 547-5400
Henry Ricciutti – (617) 547-5700

Project Budget: \$37,829,870

Status: Construction – 16% Complete

Project Status Overview – Work Completed through October, 2010 (OPM 8.1.3.01)

Project activities previously completed included commencement of building foundations and on-going sitework and related infrastructure activity.

Project Status Summary – Work Complete through November 30, 2010 (OPM 8.1.3.02)

During the month of November, major construction activities completed by PJ Stella and their subcontractors included:

- Extensive sitework, including completion of on-site processing of materials to produce gravel fill, crushed stone and other reusable materials. Infiltration System #2 was installed. Binder course of pavement was installed at parking area and the site access from Hartley Road.
- Installation of processed gravel, under-slab insulation and vapor barrier has been progressing, following under-slab utility installation.

- Completion of footing, frost wall and grade beam construction on the proposed addition. Slab on grade construction is progressing in an easterly direction. Retaining wall construction at Hartley Road is progressing.
- Continuation of under-slab utilities (plumbing, electrical) within the building footprint
- Commencement of application of waterproofing materials to foundation walls

Administrative Oversight: The following is a summary of non-construction related progress (work performed by the OPM / Architect & Design Team) during the month of November, 2010, as well as a forecast of the current administrative schedule through the anticipated end date of the project:

Contract Administration: The management team has been continuously involved in project and contract administration including but not limited to submittal review, RFI response and investigation, controlled construction oversight, change order review and overall project controls.

Future Work Forecast: A preliminary construction schedule prepared by the contractor has been provided for information. It is anticipated the following major construction items will be completed during the forthcoming three-month period (November, 2010 – January, 2011):

- Completion of site work activities for this season, including rough grading and restoration of the areas surrounding the building addition.
- Mock-up panel construction, including all major building elements.
- Progression of under-slab utilities, and subsequent placement of slabs on grade
- Steel erection has been revised to begin in early December, 2010.

Schedule Update (OPM 8.1.3.03)

PJ Stella Construction Company has presented a preliminary construction schedule for the project. Progress is largely consistent with activities forecasted on the schedule. The project team is currently working with PJ Stella to complete the review and approval of the overall construction schedule.

Financial Update (OPM 8.1.3.04 / 8.1.3.05 / 8.1.3.06)

The base contract amount for this project is \$23,640,900. Change Orders #1 through #5, amounting to \$65,401 have been issued by the Project. Change Order #6, in the estimated amount of \$32,000, is currently being finalized for execution by the Project. Pending Changes in the estimated amount of \$132,000 have been submitted to the project for consideration, and are under review and negotiation with the Project Team (SMMA, CMS and PJ Stella). The total amount of changes enumerated to date (both pending and approved) is estimated at \$229,000 or approximately 1% of the overall project budget.

Contractor's Safety Performance (OPM 8.1.3.07)

With regard to the construction operations underway at the site, CMS is not aware of any lost-time accidents or incidents occurring at the site. CMS will provide updates on these items as soon as they are available.

Designer's QA/QC (OPM 8.1.3.08)

Construction Monitoring Services has maintained a constructive working relationship with Symmes Maini & McKee throughout the duration of our involvement with the project. We will continue to work in cooperation with SMMA to identify potential issues in the construction documents, and address them prior to their impacting construction operations or progress.

Contractor's Environmental Compliance (OPM 8.1.3.09)

With regard to environmental compliance of the current construction operations, no report of any environmental abnormalities has been received. Minor site infractions (damaged hay bales, groundwater pumping, etc.) have been remedied by PJ Stella and their site contractor without delay.

Community Issues (OPM 8.1.3.10)

CMS has been made aware of the following issues regarding project abutters:

- The project has received notification from a small number of abutters, regarding claims of minor damage resulting from vibration associated with blasting and site activity. The information included in this claim has been forwarded to the contractor for action.
- The project has received notification of concerns regarding a perceived an increase in rodent (mice) activity in properties abutting the site. Pest control measures (bait stations) have been employed along the site perimeter to address these concerns.

CMS has been responsive to the abutter's questions and concerns regarding these matters . No other community issues are known at this time.

Designer & Contractor MBE/WBE Activity (OPM 8.1.3.11)

CMS has provided updated SOMWBA Participation Reports from PJ Stella.

Project Issues and Concerns (OPM 8.1.3.10 / 8.1.3.11)

The Project Team (SMMA and CMS) had previously identified concerns in the performance of PJ Stella and the concrete subcontractor on the project to date. In response to these concerns, PJ Stella has provided a replacement superintendent, whom started work at the site in late November. Further, they have removed the concrete subcontractor from further formwork responsibility on the project, and are limiting his responsibility to the concrete flatwork. Further, PJ Stella has completed the survey on the

deficient work items, developed acceptable solutions to the foundation elements, and commenced with corrective work as approved.

The impact of the deficiencies and associated repairs has impacted the progress of the work by an estimated 3-4 weeks. The Project Team (CMS, SMMA and PJ Stella) is currently working toward constructive solutions to these deficiencies, and a swift resolution to these matters is anticipated. The project team will continue to look at schedule mitigation measures to minimize these impacts. Should any further issues arise, CMS will notify the client and the MSBA as soon as practical.

Total Project Budget
Stow Pompositticut/Center School

Stow Pompositticut/Center School		12/04/2010						Stow Pompositticut/Center School		
		Pre Pay Cost Category	Budget	Reallocation	Adjusted Budget	Anticipated	Paid to Date	Balance	% Expended	Ineligible
Administration					40,000	11,281	11,281	-	100.0%	11,281
Legal Fees		0101-00000	40,000							
Owner's Project Manager										
OPM Feasibility Study		0001-00000	40,000		40,000	40,000	40,000	-	100.0%	
Design Development		0102-0400	33,750		33,750	33,750	33,750	-	100.0%	
Construction Contract Documents		0102-0500	55,800		55,800	55,800	55,800	-	100.0%	
Bidding		0102-0600	52,875		52,875	52,875	40,000	12,875	75.7%	
Construction Contract Administration		0102-0700	583,393		583,393	583,393	114,142	469,251	19.6%	
Closeout		0102-0800	83,057		83,057	83,057	83,057	83,057	0.0%	
Extra Services		0102-0900						-		
Reimbursable & Other Services		0102-1000	70,000		70,000	70,000	59,200	10,800	84.6%	
Cost Estimates		0102-1100						-		
Other Project Manager Costs		0102-9900		70,000		70,000	47,996	47,996	100.0%	
Advertising		0103-00000	2,000			2,000	2,000	122	1,878	6.1%
Permitting		0104-00000						-		
Owner's Insurance		0105-00000								
Other Administrative Costs		0199-00000	20,000		20,000	20,000	60	19,940	0.3%	
Administration Subtotal			940,875	70,000	1,010,875	988,871	39,070	597,801	153%	
Architecture and Engineering										
Basic Services										
Prior Studies		0004-00000	55,200		55,200	55,200			0.0%	
A&E Feasibility Study		0002-00000	490,000		490,000	490,000	582,500	(92,500)	118.9%	37,300
Design Development		0201-0400	506,300		506,300	506,300	562,000	(55,700)	111.0%	
Construction Contract Documents		0201-0500	1,054,000		1,054,000	1,054,000	1,094,000	(40,000)	103.8%	
Bidding		0201-0600	85,000		85,000	85,000	85,000	-	100.0%	
Construction Contract Administration		0201-0700	798,000		798,000	798,000	112,000	686,000	14.0%	
Closeout		0201-0800						-		
Other Basic Services		0201-9900		21,391	21,391	21,391		-	100.0%	
Reimbursable Services										
Construction testing		0203-0100	50,000		50,000	50,000	50,000	50,000		
Printing (over minimum)		0203-0200	70,000		(70,000)	-	-	-		
Other Reimbursable Costs		0203-9900	82,700		98,282	98,282	85,554	12,728	87.0%	20,280
Hazardous Materials		0204-0200	40,000		40,000	40,000	40,000	40,000	0.0%	
Geotech & Geo-Env.		0204-0300	115,000		(21,391)	93,609	93,609	93,609	0.0%	
Site Survey		0204-0400								
Wetlands		0204-0500								
Traffic Studies		0204-1200								
Architectural/Engineering Subtotal			3,346,200	(54,418)	3,291,782	3,291,782	2,542,445	694,377	77.2%	57,560

Total Project Budget
Stow Pompositicut/Center School

Stow Pompositicut/Center School										
12/04/2010		Pre-Pay Cost Category	Budget	Reallocation	Adjusted Budget	Anticipated	Paid to Date	Balance	% Expended	Ineligible
Construction										
Construction Contract		25,253,789			23,640,900	\$23,640,900				
Contingencies (Design and Pricing)		2,214,856							-	
Escalation to Mid-Point of Construction		1,373,211							-	
Change Orders					65,401	65,401			65,401	
Outstanding Liabilities					219,629	219,629			219,629	
Construction Subtotal	0502-0001	28,841,856	(5,200,956)	23,925,930	23,925,930				65,401	-
Const. Contingency		0507-0000	2,163,139	285,030	1,878,109					67,739
Construction Total			31,004,985		25,804,039	24,210,959		- 130,802	-	67,739
Miscellaneous Project Costs										
Utility company Fees		0601-0000							-	
Testing Services		0602-0000							-	
Swing Space/Modular's		0603-0000							-	
Other Project Costs (Mailing & Moving)		0699-0000	50,000.0		50,000.0	3,514.0	3,514.0		100.0%	
Misc. Project Costs Subtotal			50,000.0		50,000.0	3,514.0	3,514.0		100.0%	-
Furnishings and Equipment										
Furnishings		0701-0000	720,000		720,000		720,000		0.0%	
Equipment		0702-0000	20,000		20,000		20,000		0.0%	
Computer Equipment		0703-0000	1,047,700		1,047,700		1,047,700		0.0%	
FF&E Subtotal			1,787,700		1,787,700		1,787,700		0.0%	-
Owner's Contingency		0801-0000	\$620,100		\$644,518					
Total Project Budget			37,789,870	15,582	32,628,914	30,294,107	2,948,310	3,210,110	9.7%	136,580

Item	Amount	Balance	Comments	
Starting Balance				
CO 2	14,085	2,149,054		
CO 3	3,766	2,145,288		
CO 4	6,476	2,138,812		
CO 5	41,074	2,097,738		
Total	65,401			

Owner's Contingency				
Item	Vendor	Amount	Balance	Comments
Starting Balance				
PFA Adjustment	(40,000.00)		15,581.66	
MHC Support	SMMA			
Fees				
620,100	660,100		644,518	Stone Building
Total			15,581.66	

Item	Transfers	Amount	From Line	To Line	Comments	Printng	Reimburseable
		70,000.00	0203-0200	0102-9900	ReallocatIon		
		15,582.00	0801-0000	0203-9900	Owner's Contingency		
		85,582.00				Total	

Item	Amount	Comments	Outstanding - Liability
Anchors Electric Service Pipe	14,216.54		
Stella Open Rock	99,776.00		
Concrete admixture	800.00		
Asbestos Tile/carpet	3,000.00		
Fire Dumbster	1,000.00		
Asbestos Pipe	40,413.00		
Root Opener	1,061.00		
Root Drain Pipe	3,079.00		
Transformer Pad	1,000.00		
Door/Frame changes	9,000.00		
Gas Pit	2,000.00		
Motorized Shades	4,000.00		
Site Entrance sign	2,000.00		
Turf & Grass Revisions	4,771.00		
Structural Changes	1,000.00		
Pumbing Changes SKP 06	274.00		
Celling Changes SKA66	3,000.00		
Fireproofing Changes	27,000.00		
Fire doors	1,061.00		
Roof openings	1,177.00		
Fencing Gate			Total 219,628.54

CMS Amendments	Paid From	Amount	Structural Peer Review	ProjectDog Printing	T8L Floor Testing	Cost Estimates
Reimbursable 0102-1000	4,400.00	47,996.25	Printng 0203-0200	2,058.10	Reimbursable 0102-1000	Reimbursable 0102-1000
Reimbursable 0102-1000	59,200.00	59,200.00	Printng 0203-0200	59,200.00	Reimbursable 0102-1000	Reimbursable 0102-1000

Change Order Detail Log
Stow Center Elementary School

C M S

Proposed Change Order Log

Stow Center Elementary School

<u>PCO</u>	<u>Description</u>	<u>Date</u>	<u>CCD</u>	<u>PR</u>	<u>Proposed</u>	<u>Approved</u>	<u>CO#</u>
00001	Wetland Flagging - Hay Bales	7/15/2010			\$985.00	\$985.00	2
00001.2	Wetland Flagging - Hay Bales	7/16/2010		1			
00002	Primary electric riser conduit	8/9/2010		4			3
00002.2	Primary electric riser conduit	9/23/2010		4	\$1,772.00		
00003	Existing fire dumpster	8/20/2010					
00003.2	Existing fire dumpster	8/27/2010	002R1		\$13,100.00	\$13,100.00	2
00004	Architectural/structural modifications	8/22/2010		2	\$4,771.00		
00005	Builders risk insurance	8/23/2010				\$5,299.00	
00006	Wetland Mitigation	8/25/2010				\$53,424.00	
00006.2	Wetland Mitigation	8/28/2010					
00006.3	Wetland Mitigation	9/13/2010					
00006.4	Wetland Mitigation	9/28/2010		6	\$41,074.00		3
00007	Rock removal	8/30/2010			\$99,776.00		
00008	Ceiling revisions	9/7/2010				\$1,083.00	
00009	Electric panel at existing building	9/17/2010	001R1			\$1,994.00	
00010	Concrete for fire pump pit	10/11/2010				\$2,050.00	
000011	Asbestos cement pipe	10/19/2010				\$11,002.00	
000012	Temporary construction gate	11/1/2010					
000013	Roof opening revisions	11/1/2010					
000014	Asbestos cement pipe	11/3/2010	3			\$29,411.00	
000015	Roof drain piping	11/12/2010				\$3,079.00	
000016	Doors C264 & EX302	11/18/2010				\$274.00	
000017	Stair C122 opening	11/19/2010				\$25,899.50	
000017.2	Stair C122 opening	11/22/2010				\$26,855.00	

C M S

Construction Change Directive Log

Stow Center Elementary School

No.	Description	Amount	Date	COR	CO	PR	PCO
1	Disconnect & relocate existing panel P2 as indicated in sketch SKE-05		7/15/2010				
1R1	Signed partial field T&M slips regarding electric panel existing building		8/17/2010				
2R1	Remove & dispose existing asbestos containing floor tile material	\$13,100.00	7/30/2010	2			3.2
3	Removal of tranite pipe		8/24/2010				
4	Dispose at dumpster		8/30/2010				
5	Provide site work modifications	\$41,074.00	10/6/2010				

C M S

Proposal Request Log
Stow Center Elementary School Project

<u>P.R.</u>	<u>Description</u>	<u>Date</u>
001	Add temporary erosion control as indicated in SKC-08	7/12/2010
002	Furnish and install revisions to architectural and structural components of building exterior	7/22/2010
003	Provide costs to furnish and install plumbing piping as indicated SKP-06	7/27/2010
004	Provide riser pole conduits as indicated SKE-06	7/30/2010
005	Provide cost proposal to delete work associated with transformer pad	8/6/2010
006	Wetland mitigation	9/13/2010
007	Doors C264 and EX302	8/31/2010
010	Cost for interior doors frames & deluge sprinkler system	10/1/2010
011	Provide cost for fireproofing revisions	10/1/2010
012	Cost revise gas service pit	10/7/2010
013	Provide cost proposal for electrical work with circuiting for motorized shades	10/14/2010
014	Provide cost to revise site entry sign	10/18/2010
015	Provide cost to add, delete, and revise site work items regarding topsoil placement & seeding applications	10/22/2010
016	Provide revisions to Door B 132	11/19/2010

Nashoba Pompo/Center School Project
Cash Flow Projections

12/7/2010

Prior Year	Jan-10	Feb-10	Mar-10	Apr-10	May-10	Jun-10	Jul-10	Aug-10	Sep-10	Oct-10	Nov-10	Dec-10	Total
Total													
1,119,941	234,012	239,000	282,000	289,000	282,000	297,600	283,850	498,850	476,850	826,850	1,026,850	1,126,850	6,983,653
782,924	317,362	235,288	391,929	557,300	129,415	83,410	408,024	408,476	103,122	1,214,725	0	0	4,631,975
337,017	-83,350	3,712	-109,929	-268,300	152,585	214,190	-124,174	90,374	373,728	-387,875	1,026,850	0	1,224,828
Total													
6,983,653	1,234,850	1,734,850	1,756,850	1,734,850	1,734,850	2,234,850	2,234,850	1,934,850	1,734,850	1,755,850	1,234,850	1,084,850	27,394,853
6,983,653	1,234,850	1,734,850	1,756,850	1,734,850	1,734,850	2,234,850	2,234,850	1,934,850	1,734,850	1,755,850	1,234,850	1,084,850	27,394,853
Total													
27,394,853	971,989	886,850	608,850	568,850	490,850	974,892	464,725	220,549	67,000	10,000	10,000	5,160,462	37,829,870
27,394,853	971,989	886,850	608,850	568,850	490,850	974,892	464,725	220,549	67,000	10,000	10,000	5,160,462	37,829,870

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 1A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Contract Changes									
Contract Changes									
CCCIC1A	CIC #1 Issued - Wetlands	0	12JUL10 A		12JUL10 A				100
CCCIC2A	CIC #2 Issued - Electric Panel at Exst	0	12JUL10 A		12JUL10 A				100
CCCIC2B	CCD #1R Issued - Electric Panel at Exst	0	12JUL10 A	26JUL10 A	12JUL10 A	26JUL10 A			100
CCCIC1B	PR #6 Issued - Wetlands	0	12JUL10 A	11AUG10 A	12JUL10 A	11AUG10 A			100
CCCIC2C	Procure and Complete CCD #1R Work	0	27JUL10 A	10AUG10 A	27JUL10 A	10AUG10 A			100
CCNOC3A	NOC #3 Issued - Topsoil Removal	0	11AUG10 A		11AUG10 A				100
CCCIC2D	Remobilize Demolition	0	11AUG10 A	12AUG10 A	11AUG10 A	12AUG10 A			100
CCNOC3B	NOC #3 - Topsoil Removal Direction Issued	0	11AUG10 A	17AUG10 A	11AUG10 A	17AUG10 A			100
CCCIC1C	PCO #6 Issued - Wetlands	0	11AUG10 A	25AUG10 A	11AUG10 A	25AUG10 A			100
CCCIC6A	CIC #6 Issued - Rock Removal	0	12AUG10 A		12AUG10 A				100
CCCIC7A	CIC #7 Issued - ACM Pipe	0	12AUG10 A		12AUG10 A				100
CCCIC7B	CCD #3 Issued - ACM Pipe	0	12AUG10 A	26AUG10 A	12AUG10 A	26AUG10 A			100
CCCIC6B	CIC #6 - Additional Rock Removal	0	16AUG10 A	06OCT10 A	16AUG10 A	06OCT10 A			100
CCCIC1D	PCO #6 Reviewed, CCD #5 Issued - Wetlands	0	25AUG10 A	07OCT10 A	25AUG10 A	07OCT10 A			100
CCCIC7C	CCD #3 - Remove ACM Pipe	0	26AUG10 A	14SEP10 A	26AUG10 A	14SEP10 A			100
CCNOC3C	NOC #7 Issued - Topsoil Removal Site	0	21SEP10 A		21SEP10 A				100
CCNOC3D	NOC #7 - Topsoil Removal Direction Issued	0	21SEP10 A	24SEP10 A	21SEP10 A	24SEP10 A			100
CCCIC1E	PCO #6 Prep Work - Wetlands	0	11OCT10 A	22OCT10 A	11OCT10 A	22OCT10 A			100
CCCIC1F	Complete Access at Building	0		22OCT10 A		22OCT10 A			100
General Conditions/Start-up/Owner/AE									
General Conditions/Start-up/Owner/AE									
GC100	Bid - Award - NTP	0	07JUN10 A	15JUN10 A	07JUN10 A	15JUN10 A			100
GC110	Commence Construction	0	15JUN10 A		15JUN10 A				100
GC120	Obtain CADD Files, Prepare Layout	0	16JUN10 A	23JUN10 A	16JUN10 A	23JUN10 A			100
GC140	Procure Abatement, Demo, Sitenwork Subs	0	16JUN10 A	25JUN10 A	16JUN10 A	25JUN10 A			100
GC130	Obtain Building Permit	0	16JUN10 A	02JUL10 A	16JUN10 A	02JUL10 A			100
GC150	Mobilize, Set-up	0	16JUN10 A	23JUL10 A	16JUN10 A	23JUL10 A			100
GC160	Commence Submittals	0	21JUN10 A		21JUN10 A				100
GC180	Initial Site Layout, Engineering	0	29JUN10 A	19JUL10 A	29JUN10 A	19JUL10 A			100
GC170	File Abatement Notices	0	30JUN10 A	12JUL10 A	30JUN10 A	12JUL10 A			100
GC400	Exterior Building Mock-up Panel	5	29NOV10	03DEC10	06DEC10	10DEC10	5d	0	
GC410	Exterior Building Mock-up Commissioning	15	06DEC10	24DEC10	13DEC10	31DEC10	5d	0	
GC500	School Out for 2011 Summer	0	22JUN11 *		22JUN11			0	0
GC510	School Summer Break 2011	48	22JUN11	26AUG11	22JUN11	26AUG11	0	0	
GC520	School Summer Break 2011 Ends	0		26AUG11		26AUG11 *	0	0	

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 2A of 20A

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
General Conditions/Start-up/Owner/AE								
GC190	Set Office Trailers (Temporary)	0	01JUL10 A	01JUL10 A	01JUL10 A	01JUL10 A		100
GC200	Meeting with Conservation Commission	0	02JUL10 A	02JUL10 A	02JUL10 A	02JUL10 A		100
GC210	Temporary Construction Fencing	0	02AUG10 A	27AUG10 A	02AUG10 A	27AUG10 A		100
GC220	Prepare Trailer, Staging Areas	0	16AUG10 A	16AUG10 A	16AUG10 A	16AUG10 A		100
Initial Sitework - Phase 1A								
General Conditions/Start-up/Owner/AE								
GC300	Owner Relocate Blacksmith Shop	0	28JUL10 A	10AUG10 A	28JUL10 A	10AUG10 A		100
GC250	Relocate Office Trailers	0	17AUG10 A	19AUG10 A	17AUG10 A	19AUG10 A		100
GC240	Vacate Existing School Area	0	20AUG10 A	23AUG10 A	20AUG10 A	23AUG10 A		100
Existing Building - Phase 1A								
General Conditions/Start-up/Owner/AE								
GC230	Secure Existing Building	0	23AUG10 A	23AUG10 A	23AUG10 A	23AUG10 A		100
Existing Building								
Existing Building - Phase 1A								
Abatement, Demolition								
DM100	Asbestos-Abatement	0	20JUL10 A	30JUL10 A	20JUL10 A	30JUL10 A		100
HV101A	Cut/Cap MEP	0	30JUL10 A	30JUL10 A	30JUL10 A	30JUL10 A		100
DM120	Building Demolition	0	12AUG10 A	19AUG10 A	12AUG10 A	19AUG10 A		100
Sitework								
Initial Sitework Prep - Phase 1								
Sitework: Preparation								
SW1120	Erosion Control, Protections	0	06JUL10 A	13JUL10 A	06JUL10 A	13JUL10 A		100
SW1130	Clear and Grub	0	12JUL10 A	19JUL10 A	12JUL10 A	19JUL10 A		100
SW1140	Strip, Stockpile Topsoil	0	12JUL10 A	28JUL10 A	12JUL10 A	28JUL10 A		100
SW1110	Cut-In Initial Site Access	0	12JUL10 A	30JUL10 A	12JUL10 A	30JUL10 A		100
SW1160	Haul Out Excess Topsoil (Partial)	0	19AUG10 A	21SEP10 A	19AUG10 A	21SEP10 A		100
SW1150	Existing Utility Relocations	0	24AUG10 A	27AUG10 A	24AUG10 A	27AUG10 A		100
SW1160A	Haul Out Excess Topsoil (Complete)	10	27SEP10 A	12NOV10	27SEP10 A	29OCT10	-10d	0
Initial Sitework - Phase 1A								
Sitework: Preparation								
SW1210	Cut/Prep Utility Trenching	0	16AUG10 A	19AUG10 A	16AUG10 A	19AUG10 A		100
EL101A	Power & Communications Service to Phase 1	0	19AUG10 A	26AUG10 A	19AUG10 A	26AUG10 A		100
SW1220	Patch Utility Trenching	0	27AUG10 A	27AUG10 A	27AUG10 A	27AUG10 A		100
Sitework: Utilities, Roadways, Paving								
SW2210	Gas Service to Phase 1	0	23AUG10 A	24AUG10 A	23AUG10 A	24AUG10 A		100
Sitework - Building Area								
Sitework: Preparation								
SW1310	Building Cuts & Fills, West	0	28JUL10 A	13AUG10 A	28JUL10 A	13AUG10 A		100
SW1320	New 30" Drain Line at West	0	02AUG10 A	13AUG10 A	02AUG10 A	13AUG10 A		100
SW1340	Building Cuts & Fills, East	0	18AUG10 A	27AUG10 A	18AUG10 A	27AUG10 A		100
SW1330	Remove Existing Drainage	0	26AUG10 A	14SEP10 A	26AUG10 A	14SEP10 A		100
SW1350	Sewer Temporary Force Main	0	30AUG10 A	31AUG10 A	30AUG10 A	31AUG10 A		100

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 3A of 20A

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
EL10SW	UG Site Electric to Bldg	3	17NOV10	19NOV10	27OCT10	29OCT10	-15d	0
SW1360	Rough Grade Around Building	5	22NOV10	26NOV10	01NOV10	05NOV10	-15d	0
FN500	Concrete Bench Wall	5	26MAY11	01JUN11	09JUN11	15JUN11	10d	0
EL50SW	Set Transformer	5	06JUN11	10JUN11	16JUL11	22JUL11	30d	0
EL51SW	Set Emergency Generator	5	06JUN11	10JUN11	03OCT11	07OCT11	85d	0
EL90SW	Test and inspect Emergency Generator	5	04JUL11	08JUL11	10OCT11	14OCT11	70d	0
Sitework: Utilities, Roadways, Paving								
SW2310	Set DMH1-5, DMH1-6 at South, Building	0	06SEP10 A	07SEP10 A	06SEP10 A	07SEP10 A		100
SW2312	New Drain Line at South, Building	0	07SEP10 A	13SEP10 A	07SEP10 A	13SEP10 A		100
SW2316	Drainage at Building Area	5	14SEP10 A	05NOV10	14SEP10 A	15OCT10	-15d	75
SW2314	Temporary Drain Line at South, Building	0	27SEP10 A	27SEP10 A	27SEP10 A	27SEP10 A		100
SW2318	Infiltration Area 1	0	27SEP10 A	26OCT10 A	27SEP10 A	26OCT10 A		100
SW2328	Infiltration Area 2	8	29OCT10 A	10NOV10	29OCT10 A	05NOV10	-3d	20
SW2322	Water Mains at Building Area, Partial	10	08NOV10	19NOV10	18OCT10	29OCT10	-15d	0
SW2326	Excavate Site UG Electric to Building	2	15NOV10	16NOV10	25OCT10	26OCT10	-15d	0
SW2320	Site Roof Drain Piping	5	15NOV10	19NOV10	25OCT10	29OCT10	-15d	0
SW2330	Backfill UG Site Electric to Building	2	18NOV10	19NOV10	28OCT10	29OCT10	-15d	0
SW2332	Ex/Set/Bckfl Fire Suppression Tanks	5	27DEC10	31DEC10	07FEB11	11FEB11	30d	0
SW2334	Water/Fire Piping at Fire Supp Tanks	5	03JAN11	07JAN11	14FEB11	18FEB11	30d	0
SW2336	Well Water Piping	5	10JAN11	14JAN11	18APR11	22APR11	70d	0
SW2338	Test & Chlorinate Water System	5	17JAN11	21JAN11	25APR11	29APR11	70d	0
SW2340	Complete Gas Service to Building	5	09MAY11	13MAY11	23MAY11	27MAY11	10d	0
SW2342	Excavate/Prep Transf, Gen, Gas Pads	5	16MAY11	20MAY11	30MAY11	03JUN11	10d	0
SW2344	Form/Pour/Strip Conc Tranf, Gen, Gas Pads	5	23MAY11	27MAY11	06JUN11	10JUN11	10d	0
SW2346	Backfill Tranf, Gen, Gas Pads	5	30MAY11	03JUN11	13JUN11	17JUN11	10d	0
SW2348	Grade Fire Lane/Service, Building	10	06JUN11	17JUN11	20JUN11	01JUL11	10d	0
SW2350	E/B Site Lighting, Building	10	06JUN11	17JUN11	11JUL11	22JUL11	25d	0
EL13SW	UG Site Lighting, Building	10	06JUN11	17JUN11	18JUL11	29JUL11	30d	0
SW2352	Under Drain at Fire Lane, Building	5	20JUN11	24JUN11	25JUL11	29JUL11	25d	0
SW2354	Complete Rims, Inverts, Misc. Utilities, Bldg	10	20JUN11	01JUL11	15AUG11	26AUG11	40d	0
SW2324	Infiltration Area 3	10	04JUL11	15JUL11	08AUG11	19AUG11	26d	0
SW2356	Prep and FG Fire Lane/Service at Building	10	08AUG11	19AUG11	01AUG11	12AUG11	-5d	0
SW2358	Finish Pave Fire Lane/Service at Building	5	05SEP11	09SEP11	29AUG11	02SEP11	-5d	0
Sitework: Walks, Finishes, Landscaping								
SW4310	Excavate Concrete Bench Wall	3	23MAY11	25MAY11	06JUN11	08JUN11	10d	0
SW4312	Backfill Bench Wall	2	02JUN11	03JUN11	16JUN11	17JUN11	10d	0
SW5310	Granite Top & Edging at Bench Wall	5	06JUN11	10JUN11	04JUL11	06JUL11	20d	0
SW4314	Segmental Retaining Wall, Building	5	20JUN11	24JUN11	20JUN11	24JUN11	0	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 4A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	SW4316	Prep/Grade Concrete Walkways, Building	20	11JUL11	05AUG11	27JUN11	22JUL11	-10d	0
	SW4318	Traffic Signage, Building	5	18JUL11	22JUL11	25JUL11	29JUL11	5d	0
	SL400	Concrete Walkways, Building	20	25JUL11	19AUG11	11JUL11	05AUG11	-10d	0
	MM400	Site Bollards	5	08AUG11	12AUG11	25JUL11	29JUL11	-10d	0
	SW5312	Barricade Gates, Building	5	08AUG11	12AUG11	15AUG11	19AUG11	5d	0
	SW4320	Paving Binder at Service, Building	5	22AUG11	26AUG11	15AUG11	19AUG11	-5d	0
	SW4324	Mow Strip, Stone Pit, Building	10	22AUG11	02SEP11	08AUG11	19AUG11	-10d	0
	SW4322	Bit Berm, Building	5	29AUG11	02SEP11	22AUG11	26AUG11	-5d	0
	SW4326	Spread Topsoil, Building	15	05SEP11	23SEP11	22AUG11	09SEP11	-10d	0
	SW5314	Plantings, Building	10	12SEP11	23SEP11	12SEP11	23SEP11	0	0
	SW5316	Waste Receptacles, Wood Benches, Building	10	26SEP11	07OCT11	17OCT11	28OCT11	15d	0
	SW5318	FG and Lawns, Building	10	10OCT11	21OCT11	26SEP11	07OCT11	-10d	0
	SW4328	Pavement Markings	5	07NOV11	11NOV11	24OCT11	28OCT11	-10d	0

Sitework - Entry/Roadway/Parking

Sitework: Preparation

SW1410	Initial Rough Grade Entry Road	0	16AUG10 A	17AUG10 A	16AUG10 A	17AUG10 A		100
SW1420	Cuts and Fills Roadway	0	22SEP10 A	24SEP10 A	22SEP10 A	24SEP10 A		100
SW1430	Cuts and Fills, Northeast Parking	0	07OCT10 A	28OCT10 A	07OCT10 A	28OCT10 A		100
EL11SW	Electric UG under Roadway	5	15NOV10	19NOV10	25OCT10	29OCT10	-15d	0
SW1440	Prepare Storage Staging Area	5	13DEC10	17DEC10	20DEC10	24DEC10	5d	0

Sitework: Utilities, Roadways, Paving

SW2410	Drainage at Roadway	4	19OCT10 A	04NOV10	19OCT10 A	14OCT10	-15d	60
SW2412	Grade Northeast Parking	0	25OCT10 A	29OCT10 A	25OCT10 A	29OCT10 A		100
SW2418	Water Mains at Roadway	5	29OCT10 A	05NOV10	29OCT10 A	22OCT10	-10d	50
SW2416	Under Drain at Northeast Parking	5	01NOV10	05NOV10	11OCT10	15OCT10	-15d	0
SW2414	Force Main at Roadway	10	01NOV10	12NOV10	11OCT10	22OCT10	-15d	0
SW2430	New Sanitary System	25	05NOV10	09DEC10	15NOV10	17DEC10	6d	0

SW2420	Gravel and Finish Grade, NE Parking	5	08NOV10	12NOV10	18OCT10	22OCT10	-15d	0
SW2424	Excavate Electric under Roadway	3	15NOV10	17NOV10	25OCT10	27OCT10	-15d	0
SW2422	Rough Grade Roadway - Partial	5	15NOV10	19NOV10	25OCT10	29OCT10	-15d	0
SW2426	Backfill Electric under Roadway	2	18NOV10	19NOV10	28OCT10	29OCT10	-15d	0
SW2428	Gravel and Finish Grade Roadway - Partial	3	22NOV10	24NOV10	01NOV10	03NOV10	-15d	0
SW2432	Paving Binder, NE Parking and Partial Road	2	25NOV10	26NOV10	04NOV10	05NOV10	-15d	0
SW2434	Rough Grade Roadway - Complete	5	10DEC10	16DEC10	20DEC10	24DEC10	6d	0
SW2436	Test, Inspect, Approve New Sanitary	5	10DEC10	16DEC10	29JUN11	05JUL11	143d	0
SW2440	Gravel and FG Roadway - Complete	5	20JUN11	24JUN11	04JUL11	08JUL11	10d	0
SW2438	Remove Existing Sanitary System	8	22JUN11	01JUL11	06JUL11	15JUL11	10d	0
SW2442	Paving Binder Complete, Roadway	5	27JUN11	01JUL11	11JUL11	16JUL11	10d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 5A of 20A

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
SW2444	Light Pole Bases	10	04JUL11	15JUL11	18JUL11	29JUL11	10d	0
EL14SW	UG Site Lighting, Parking and Roadway	10	11JUL11	22JUL11	25JUL11	05AUG11	10d	0
SW2446	E/B Site Lighting, Parking and Roadway	10	11JUL11	22JUL11	25JUL11	05AUG11	10d	0
SW2448	Curbings, Parking and Roadway	15	25JUL11	12AUG11	08AUG11	26AUG11	10d	0
SW2450	Complete Rims, Inverts, Misc. Utilities, Roadway	10	15AUG11	26AUG11	03OCT11	14OCT11	35d	0
SW2452	Prep and Finish Paving, Roadway/Parking	5	31OCT11	04NOV11	17OCT11	21OCT11	-10d	0
Sitework: Walks, Finishes, Landscaping								
SW4410	Prep/Grade Concrete Walkways, Roadway	10	15AUG11	26AUG11	29AUG11	09SEP11	10d	0
SW4412	Traffic Signage, Roadway	5	22AUG11	26AUG11	05SEP11	09SEP11	10d	0
MS20S	Site School Sign	5	29AUG11	02SEP11	17OCT11	21OCT11	35d	0
SL500	Concrete Walkways, Roadway	10	12SEP11	23SEP11	05SEP11	16SEP11	-5d	0
SW4414	Spread Topsoil, Roadway	10	26SEP11	07OCT11	19SEP11	30SEP11	-5d	0
EL15SW	Site Lighting	10	26SEP11	07OCT11	03OCT11	14OCT11	5d	0
SW5410	Plantings, Roadway	5	10OCT11	14OCT11	03OCT11	07OCT11	-5d	0
SW5412	Chain Link Fence at Turnaround, Roadway	5	10OCT11	14OCT11	10OCT11	14OCT11	0	0
SW5414	FG and Lawns, Roadway	5	24OCT11	28OCT11	10OCT11	14OCT11 *	-10d	0
Storage Building								
Foundations and Structure								
SW331SB	Excavate Found, Storage Bldg	0	27SEP10 A	28SEP10 A	27SEP10 A	28SEP10 A		100
FN10SB	Foundations, Storage Bldg	0	12OCT10 A	25OCT10 A	12OCT10 A	25OCT10 A		100
SW332SB	Backfill, Grade, Storage Bldg	5	01NOV10	05NOV10	27DEC10	31DEC10	40d	0
SL10SB	Prep, Pour SOG, Storage Bldg	5	08NOV10	12NOV10	03JAN11	07JAN11	40d	0
MC10SB	CMU at Storage Bldg	10	15NOV10	26NOV10	10JAN11	21JAN11	40d	0
RC10SB	Ro Carpentry/Trusses/Framing, Storage Bldg	5	03JAN11	07JAN11	24JAN11	28JAN11	15d	0
Exterior/Closing-in								
RC20SB	Windows, Storage Bldg	2	10JAN11	11JAN11	03FEB11	04FEB11	18d	0
RF10SB	Roofing, Storage Bldg	5	10JAN11	14JAN11	31JAN11	04FEB11	15d	0
RC30SB	Siding and Trim, Storage Bldg	10	17JAN11	28JAN11	07FEB11	18FEB11	15d	0
OH10SB	OH Door, Storage Bldg	5	01FEB11	07FEB11	21FEB11	25FEB11	14d	0
Roughing-in								
EL12SB	Electric Rough, Storage Bldg	5	25NOV10	01DEC10	17JAN11	21JAN11	37d	0
Interior Finishes								
MM10SB	Bollards, Storage Bldg	5	08FEB11	14FEB11	26SEP11	30SEP11	164d	0
PA10SB	Painting, Storage Bldg	5	18JUL11	22JUL11	03OCT11	07OCT11	55d	0
EL20SB	Electric Finish, Inspect, Storage Bldg	5	25JUL11	29JUL11	10OCT11	14OCT11	55d	0
Completion								
ENDSB	Complete Storage Building	5	01AUG11	05AUG11	17OCT11	21OCT11	55d	0
Sitework - Leaching Field Area								
Sitework: Preparation								
SW1510	Excavate Site Conc. Retaining Wall	0	04OCT10 A	29OCT10 A	04OCT10 A	29OCT10 A		100

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 6A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	FN60S	Site Concrete Retaining Wall	10	01NOV10	12NOV10	08NOV10	19NOV10	5d	0
	SW1520	Backfill Site Conc. Retaining Wall	5	15NOV10	19NOV10	22NOV10	26NOV10	5d	0
Sitework: Utilities, Roadways, Paving									
	SW2510	Leaching Field - Partial	10	22NOV10	03DEC10	29NOV10	10DEC10	5d	0
	SW2512	Grade Leaching Area - Partial	5	06DEC10	10DEC10	13DEC10	17DEC10	5d	0
	SW2514	Remove Existing Leaching Field	10	04JUL11	15JUL11	18JUL11	29JUL11	10d	0
	SW2516	Leaching Field - Complete	15	18JUL11	05AUG11	01AUG11	19AUG11	10d	0
Sitework: Walks, Finishes, Landscaping									
	SW4510	Complete Grading at Leaching	5	08AUG11	12AUG11	22AUG11	26AUG11	10d	0
	SW5510	Chain Link Fence, Leaching	10	29AUG11	09SEP11	29AUG11	09SEP11	0	0
	SW4512	Spread Topsoil, Leaching	5	12SEP11	16SEP11	12SEP11	16SEP11	0	0
	SW5512	FG and Lawns, Leaching	5	19SEP11	23SEP11	19SEP11	23SEP11	0	0
Sitework - Playfields Area									
Sitework: Walks, Finishes, Landscaping									
	SW4610	Prep and Rough Grade, Field	10	30MAY11	10JUN11	23MAY11	03JUN11	-5d	0
	SW4616	Remove/Distribute Loam Pile	5	13JUN11	17JUN11	06JUN11	10JUN11	-5d	0
	SW4618	Prep and Grade Playground/BB	5	20JUN11	24JUN11	13JUN11	17JUN11	-5d	0
	SW4620	Curbing at Playground/BB	5	27JUN11	01JUL11	20JUN11	24JUN11	-5d	0
	SW4622	Prep/Fine Grade BB/Walk	5	04JUL11	08JUL11	04JUL11	08JUL11	0	0
	SW4516	1-5 Playground Equipment	15	04JUL11	22JUL11	27JUN11	15JUL11	-5d	0
	SW4624	Pave Basketball Court and Walk	5	11JUL11	15JUL11	11JUL11	15JUL11	0	0
	SW5616	Basketball Court Striping	5	18JUL11	22JUL11	24OCT11	28OCT11	70d	0
	SW5618	Resilient Play Surface	10	25JUL11	06AUG11	18JUL11	29JUL11	-5d	0
	SW5620	Chain Link Fencing, Field	15	08AUG11	26AUG11	08AUG11	26AUG11	0	0
	SW5610	Players Benches, Field	5	29AUG11	02SEP11	05SEP11	09SEP11	5d	0
	SW4614	Stone Dust Path, Field	5	05SEP11	09SEP11	12SEP11	16SEP11	5d	0
	SW4612	Spread Topsoil, Field	10	12SEP11	23SEP11	29AUG11	09SEP11	-10d	0
	SW5612	Skinned Infield, Field	5	26SEP11	30SEP11	12SEP11	16SEP11	-10d	0
	SW5614	FG and Lawns, Field	5	03OCT11	07OCT11	19SEP11	23SEP11	-10d	0
	SW5624	Playfield Equipment (Bases, etc.)	5	03OCT11	07OCT11	24OCT11	28OCT11	15d	0
Phase 1									
Completion									
	ENDSW	Complete Finish Sitework	10	14NOV11	25NOV11	31OCT11	11NOV11*	-10d	0

New Addition - Area B and C

New Addition - Area B and C

Foundations and Structure							
SW3310C	Excavate Foundations, Area B/C	0	16AUG10 A	07SEP10 A	16AUG10 A	07SEP10 A	100
FN10C	Foundations Area B/C	0	26AUG10 A	08OCT10 A	26AUG10 A	08OCT10 A	100
FN20C	Interior Footings, Piers, Area B/C	0	08SEP10 A	08OCT10 A	08SEP10 A	08OCT10 A	100
PL10C	Plumbing Underslab Storm Drain at B	0	13SEP10 A	14SEP10 A	13SEP10 A	14SEP10 A	100

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 7A of 20A

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
SW3320C	Perim Insul/Backfill Foundations, Area B/C	0	20SEP10 A	08OCT10 A	20SEP10 A	08OCT10 A		100
SW3330C	E/B for US Utilities, Area B/C	4	29SEP10 A	04NOV10	29SEP10 A	18OCT10	-13d	75
PL11C	Underslab Plumbing, Area B/C	4	05OCT10 A	04NOV10	05OCT10 A	18OCT10	-13d	75
FN30C	Grout Baseplates, Area B/C	4	05OCT10 A	04NOV10	05OCT10 A	22OCT10	-9d	60
WP10C	Waterproofing, Area B/C	2	18OCT10 A	02NOV10	18OCT10 A	20OCT10	-9d	90
EL10C	Underslab Electric, Area B/C	8	26OCT10 A	10NOV10	26OCT10 A	22OCT10	-13d	25
SW3340C	BF, Grade SOG, Area B/C	5	27OCT10 A	11NOV10	27OCT10 A	27OCT10	-11d	50
SL10C	Prep & Pour Slab-on-Grade, Area B/C	10	11NOV10	24NOV10	25OCT10	05NOV10	-13d	0
ST10C	Steel Erection - Area B/C	40	29NOV10	21JAN11	08NOV10	31DEC10	-15d	0
MM30C	Tube Steel Supoort, Area B/C	5	24JAN11	28JAN11	17JAN11	21JAN11	-5d	0
MM20C	Angle at Roof Overhang, Area B/C	10	24JAN11	04FEB11	31JAN11	11FEB11	5d	0
MM10C	Deliver Loose Lintels	10	24JAN11	04FEB11	21FEB11	04MAR11	20d	0
RC605	Set HM Frames at CMU, Area B/C	20	14MAR11	08APR11	28FEB11	25MAR11	-10d	0
MC10C	CMU Back-up, Area B/C	15	21MAR11	08APR11	07MAR11	25MAR11	-10d	0
MC207	CMU at Boiler/Mech/Receiving Area	20	11APR11	06MAY11	28MAR11	22APR11	-10d	0
MM107	Seismic Clips at CMU, Area B/C	15	09MAY11	27MAY11	25APR11	13MAY11	-10d	0
MC205	CMU at Art Area, Area B/C	10	16MAY11	27MAY11	02MAY11	13MAY11	-10d	0
MC306	CMU at B, Near Existing, Area B/C	10	16MAY11	27MAY11	02MAY11	13MAY11	-10d	0
Exterior/Closing-in								
PL20C	Roof Drains, Area B/C	10	10JAN11	21JAN11	17JAN11	28JAN11	5d	0
RC10C	Roof Blocking at High Roofs, Area B/C	10	10JAN11	21JAN11	17JAN11	28JAN11	5d	0
RF10C	High Roof System, Area B/C	10	24JAN11	04FEB11	31JAN11	11FEB11	5d	0
DW10C	Ext. Studs/Sheath/Blkg Above Roofs, Area B/C	20	24JAN11	18FEB11	03JAN11	28JAN11	-15d	0
RF20C	Deliver Thru-Wall Flashings, Area B/C	5	31JAN11	04FEB11	31JAN11	04FEB11	0	0
RC20C	Roof Blocking at Low Roofs, Area B/C	10	07FEB11	18FEB11	14FEB11	25FEB11	5d	0
DW11C	Complete Ext Studs/Sheath/Blkg, Area B/C	25	14FEB11	18MAR11	24JAN11	25FEB11	-15d	0
HV10C	Set Roof Curbs, etc., Area B/C	5	27FEB11	28FEB11	28FEB11	04MAR11	5d	0
AB10C	Air Barrier at Walls Above Low Roofs, Area B/C	10	21FEB11	04MAR11	07FEB11	18FEB11	-10d	0
MV10C	Masonry Veneer at Roofs, Area B/C	15	07MAR11	25MAR11	21FEB11	11MAR11	-10d	0
RF11C	Low Roof above Lobby, Area B/C	10	14MAR11	25MAR11	07MAR11	18MAR11	-5d	0
RF12C	Low Roof above Mech/Kitch, Area B/C	10	21MAR11	01APR11	07MAR11	18MAR11	-10d	0
AB20C	Air Membrane Barriers, Area B/C	25	21MAR11	22APR11	26FEB11	01APR11	-15d	0
RC50C	Temp. Access Doors EX-C156, Area B/C	5	28MAR11	01APR11	02MAY11	06MAY11	25d	0
WN30C	Sloped Glazing Assembly, Area B/C	10	28MAR11	08APR11	21MAR11	01APR11	-5d	0
MV11C	Masonry Veneer, Area B/C	30	28MAR11	06MAY11	07MAR11	15APR11	-15d	0
RF30C	Roof Hatch, Area B/C	5	04APR11	08APR11	18APR11	22APR11	10d	0
MM50C	Roof Ladder, Area B/C	5	04APR11	08APR11	04JUL11	08JUL11	65d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 8A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	HV11C	Set Roof Top Equip., Area B/C	10	04APR11	15APR11	11APR11	22APR11	5d	0
	WN10C	Wind/CW/SF at Gym/Cafe, Area B/C	20	18APR11	13MAY11	28MAR11	22APR11	-15d	0
	MP10C	Composite Wall Panels, Area B/C	30	09MAY11	17JUN11	09MAY11	17JUN11	0	0
	WN11C	Wind/CW/SF at Media, Area B/C	10	16MAY11	27MAY11	25APR11	06MAY11	-15d	0
	WN12C	Wind/CW/SF at Lobby West, Area B/C	10	16MAY11	27MAY11	09MAY11	20MAY11	-5d	0
	WN13C	Wind/CW/SF at Admin/Lobb East, Area B/C	15	30MAY11	17JUN11	23MAY11	10JUN11	-5d	0
	MP11C	Comp. Wall Panel at Slope Glazing, Area B/C	10	20JUN11	01JUL11	27JUN11	08JUL11	5d	0
	MP20C	Acoustic Equip Screen (Roof), Area B/C	10	20JUN11	01JUL11	27JUN11	08JUL11	5d	0
	RF40C	Complete Fascia and Roof Metal, Area B/C	15	20JUN11	08JUL11	20JUN11	08JUL11	0	0
	WN20C	Complete Alum. Entrances, Area B/C	15	20JUN11	08JUL11	04JUL11	22JUL11	10d	0
	WP30C	Exterior Sealants, Area B/C	25	20JUN11	22JUL11	20JUN11	22JUL11	0	0
	RF50C	Misc. Roofing, Area B/C	10	11JUL11	22JUL11	11JUL11	22JUL11	0	0
	RC60C	Remove Temp Access - Door EX-C156, Area B/C	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0

Gymnasium - Cafeteria Area

Roughing-in:

HV203	Rough Ductwork Mains, Gym/Café	20	07FEB11	04MAR11	21FEB11	18MAR11	10d	0
PL303	Plumbing - Rough & Test, Gym/Café	20	07FEB11	04MAR11	07MAR11	01APR11	20d	0
EL203	Electric - Rough Mains, Risers, Gym/Café	25	07FEB11	11MAR11	14FEB11	18MAR11	5d	0
HV303	Rough HVAC Piping, Gym/Café	20	21FEB11	18MAR11	14MAR11	08APR11	15d	0
PL313	Plumbing - Rough Inspect, Gym/Café	5	07MAR11	11MAR11	04APR11	08APR11	20d	0
FP203	Fire Protection - Rough & Test, Gym/Café	25	07MAR11	08APR11	04APR11	06MAY11	20d	0
DW203	Interior Metal Stud Framing, Gym/Café	20	14MAR11	08APR11	21MAR11	15APR11	5d	0
EL303	Electric - Rough Plns & Complete, Gym/Café	20	21MAR11	15APR11	28MAR11	22APR11	5d	0
RC403	Interior Rough Carpentry, Gym/Café	20	28MAR11	22APR11	11APR11	06MAY11	10d	0
HV413	Controls - Roughing-in, Gym/Café	25	28MAR11	29APR11	04APR11	06MAY11	5d	0
TC303	Telecommunications Rough, Gym/Café	25	28MAR11	29APR11	04APR11	06MAY11	5d	0
HV213	Complete Rough Ductwork, Gym/Café	15	04APR11	22APR11	18APR11	06MAY11	10d	0
HV503	HVAC Pipe Insulation, Gym/Café	20	04APR11	29APR11	11APR11	06MAY11	5d	0
PL403	Plumbing - Pipe Covering, Gym/Café	20	04APR11	29APR11	11APR11	06MAY11	5d	0
EL403	Electric - Inspect Rough-in, Gym/Café	10	18APR11	29APR11	25APR11	06MAY11	5d	0

Interior Finishes:

DW303	Drywall, Tape & Sand, Gym/Café	25	16MAY11	17JUN11	09MAY11	10JUN11	-5d	0
PA103	Prime Paint, Gym/Café	15	06JUN11	24JUN11	30MAY11	17JUN11	-5d	0
AP103	Sound Wall Panels, Gym/Cafe	10	20JUN11	01JUL11	13JUN11	24JUN11	-5d	0
FS103	Firestopping, Gym/Café	10	20JUN11	01JUL11	25JUL11	05AUG11	25d	0
MM103	Unistrut Proj. Support, Gym/Cafe	5	27JUN11	01JUL11	18JUL11	22JUL11	15d	0
DW403	Touch-up Drywall, Gym/Café	10	27JUN11	08JUL11	20JUN11	01JUL11	-5d	0
WP203	Interior Caulking, Gym/Café	10	27JUN11	08JUL11	25JUL11	05AUG11	20d	0

P.J. Stelia Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 9A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	CL103	Ceiling Grid, Gym/Café	15	27JUN11	15JUL11	04JUL11	22JUL11	5d	0
	HV703	HVAC Radiation, Gym/Café	15	27JUN11	15JUL11	04JUL11	22JUL11	5d	0
	FC103	Finish Millwork, Panelling, Gym/Café	30	04JUL11	12AUG11	27JUN11	05AUG11	-5d	0
	PA303	Finish Paint Exposed Struct, Gym	10	11JUL11	22JUL11	04JUL11	15JUL11	-5d	0
	FC203	Hang Interior Doors, Gym/Café	5	18JUL11	22JUL11	26SEP11	30SEP11	50d	0
	HV803	ATC Controls - Finish, Gym/Café	10	18JUL11	29JUL11	25JUL11	05AUG11	5d	0
	FP403	Fire Protection - Finish Heads, Gym/Café	15	18JUL11	05AUG11	05SEP11	23SEP11	35d	0
	HV723	Reg, Grilles, Fans, Finishes, Gym/Café	15	18JUL11	05AUG11	05SEP11	23SEP11	35d	0
	EL703	Lighting Fixtures, Gym/Café	20	18JUL11	12AUG11	29AUG11	23SEP11	30d	0
	MS503	Projection Screens, Gym/Café	5	25JUL11	29JUL11	01AUG11	05AUG11	5d	0
	GE103	Gym Backboards, Gym/Café	10	25JUL11	05AUG11	18JUL11	29JUL11	-5d	0
	DW503	Misc. Interior Drywall, Gym/Café	10	25JUL11	05AUG11	25JUL11	05AUG11	0	0
	EL803	Scoreboard, Gym/Café	5	08AUG11	12AUG11	01AUG11	05AUG11	-5d	0
	PA203	Complete Finish Paint Walls & Ceilings, Gym/Café	15	08AUG11	26AUG11	08AUG11	26AUG11	0	0
	MM203	Metal Rails, Gym/Café	10	15AUG11	26AUG11	19SEP11	30SEP11	25d	0
	WF103	Wood Floor & Base, Gym/Café	20	15AUG11	09SEP11	08AUG11	02SEP11	-5d	0
	EL813	Electric Finishes, Gym/Café	15	29AUG11	16SEP11	29AUG11	16SEP11	0	0
	MS103	Miscellaneous Specialties, Gym/Café	15	29AUG11	16SEP11	26SEP11	14OCT11	20d	0
	TC803	Telecommunications Finish, Gym/Café	15	05SEP11	23SEP11	05SEP11	23SEP11	0	0
	FC113	Complete Finish Millwork, Gym/Café	10	12SEP11	23SEP11	19SEP11	30SEP11	5d	0
	OP103	Operable Partition, Gym/Café	10	12SEP11	23SEP11	19SEP11	30SEP11	5d	0
	WF203	Wood Floor at Stage, Gym/Café	10	12SEP11	23SEP11	19SEP11	30SEP11	5d	0
	CT103	Porcelain Tile, Gym/Café	15	12SEP11	30SEP11	05SEP11	23SEP11	-5d	0
	BL103	Gym Bleachers & Equipment	15	12SEP11	30SEP11	26SEP11	14OCT11	10d	0
	GE113	Gym Wall Pads, Divider, & Equipment	20	12SEP11	07OCT11	19SEP11	14OCT11	5d	0
	EP103	Resinous Floor, Gym/Café	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	RS103	VCT, Gym/Café	5	26SEP11	30SEP11	03OCT11	07OCT11	5d	0
	CL203	Ceiling Tile, Gym/Café	15	26SEP11	14OCT11	26SEP11	14OCT11	0	0
	PL703	Plumbing Finish, Gym/Café	5	03OCT11	07OCT11	26SEP11	30SEP11	-5d	0
	FC213	Complete Finish Hardware, Gym/Café	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	PA503	Paint at Corridors, Gym/Café	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	RS403	Vinyl Base, Gym/Café	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	PA603	Misc. Painting, Gym/Café	10	10OCT11	21OCT11	03OCT11	14OCT11	-5d	0
Completion									
	ENDG	Complete Gym/Café	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0
Kitchen									
Foundations and Structure									
	MC104	CMU at Kitchen	5	09MAY11	13MAY11	25APR11	29APR11	-10d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 10A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Roughing-in									
	HV204	Rough Ductwork, Kitch	15	04APR11	22APR11	21MAR11	08APR11	-10d	0
	EL204	Electric - Rough Mains, Risers; Kitch	15	04APR11	22APR11	25APR11	13MAY11	15d	0
	HV304	Rough HVAC Piping, Kitch	15	18APR11	06MAY11	04APR11	22APR11	-10d	0
	FP204	Fire Protection - Rough & Test, Kitch	15	18APR11	06MAY11	23MAY11	10JUN11	25d	0
	HV504	HVAC Pipe Insulation, Kitch	15	09MAY11	27MAY11	23MAY11	10JUN11	10d	0
	PL304	Plumbing - Rough & Test, Kitch	20	09MAY11	03JUN11	25APR11	20MAY11	-10d	0
	DW204	Interior Metal Stud Framing, Kitch	15	16MAY11	03JUN11	09MAY11	27MAY11	-5d	0
	EL304	Electric - Rough Ptns & Complete, Kitch	15	23MAY11	10JUN11	16MAY11	03JUN11	-5d	0
	HV404	Controls - Roughing-in, Kitch	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
	RC404	Interior Rough Carpentry, Kitch	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
	TC304	Telecommunications Rough, Kitch	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
	PL314	Plumbing - Rough Inspect, Kitch	5	06JUN11	10JUN11	23MAY11	27MAY11	-10d	0
	EL404	Electric - Inspect Rough-in, Kitch	5	13JUN11	17JUN11	06JUN11	10JUN11	-5d	0
	PL404	Plumbing - Pipe Covering, Kitch	10	13JUN11	24JUN11	30MAY11	10JUN11	-10d	0
	PL324	Plumbing - Gas Piping, Kitch	5	01AUG11	05AUG11	01AUG11	05AUG11	0	0
Interior Finishes									
	KN104	Set Cooler/Freezer, Kitch	10	06JUN11	17JUN11	30MAY11	10JUN11	-5d	0
	DW304	Drywall, Tape & Sand, Kitch	10	27JUN11	08JUL11	13JUN11	24JUN11	-10d	0
	PA114	Prime Paint, Kitch	5	11JUL11	15JUL11	27JUN11	01JUL11	-10d	0
	FS104	Firestopping, Kitch	10	11JUL11	22JUL11	11JUL11	22JUL11	0	0
	CL104	Ceiling Grid, Kitch	10	18JUL11	29JUL11	04JUL11	15JUL11	-10d	0
	DW404	Touch-up Drywall, Kitch	10	18JUL11	29JUL11	04JUL11	15JUL11	-10d	0
	WP204	Interior Caulking, Kitch	10	18JUL11	29JUL11	11JUL11	22JUL11	-5d	0
	HV704	HVAC Radiation, Kitch	15	18JUL11	05AUG11	04JUL11	22JUL11	-10d	0
	DW504	Misc. Interior Drywall, Kitch	10	01AUG11	12AUG11	18JUL11	29JUL11	-10d	0
	CT104	Ceramic Tile, Kitch	10	01AUG11	12AUG11	25JUL11	05AUG11	-5d	0
	HV714	Set/Connect CUH's, misc., Kitch	10	01AUG11	12AUG11	12SEP11	23SEP11	30d	0
	MS104	FRP Walls, Kitch	15	01AUG11	19AUG11	18JUL11	05AUG11	-10d	0
	EL704	Lighting Fixtures, Kitch	15	01AUG11	19AUG11	25JUL11	12AUG11	-5d	0
	FP404	Fire Protection - Finish Heads, Kitch	15	01AUG11	19AUG11	25JUL11	12AUG11	-5d	0
	HV724	Reg, Grilles, Fans, Finishes, Kitch	15	01AUG11	19AUG11	25JUL11	12AUG11	-5d	0
	PA204	Finish Paint Walls & Ceilings, Kitch	10	08AUG11	19AUG11	25JUL11	05AUG11	-10d	0
	HV804	ATC Controls - Finish, Kitch	15	08AUG11	26AUG11	05SEP11	23SEP11	20d	0
	CT204	Porcelain Floor/Base, Kitch	5	22AUG11	26AUG11	08AUG11	12AUG11	-10d	0
	FC204	Hang Interior Doors, Kitch	10	22AUG11	02SEP11	26SEP11	07OCT11	25d	0
	RS104	VCT and Base, Kitch	10	22AUG11	02SEP11	03OCT11	14OCT11	30d	0
	EL814	Electric Finishes, Kitch	15	22AUG11	09SEP11	19SEP11	07OCT11	20d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 11A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	CL204	Ceiling Tile, Kitch	10	29AUG11	09SEP11	26SEP11	07OCT11	20d	0
	EP104	Resinous Floor at Kitchen	15	29AUG11	16SEP11	15AUG11	02SEP11	-10d	0
	TC804	Telecommunications Finish, Kitch	10	05SEP11	16SEP11	03OCT11	14OCT11	20d	0
	FC214	Complete Finish Hardware, Kitch	5	19SEP11	23SEP11	10OCT11	14OCT11	15d	0
	KN204	Set Kitchen Equipment, Kitch	10	19SEP11	30SEP11	05SEP11	16SEP11	-10d	0
	EL804	Kitchen Equipment - Electric Connections	20	26SEP11	21OCT11	12SEP11	07OCT11	-10d	0
	PL704	Kitchen Equipment - Plumbing Connections	20	26SEP11	21OCT11	12SEP11	07OCT11	-10d	0
	LK104	Lockers, Kitch	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	PA604	Misc. Painting, Kitch	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	KN304	Start-up at Kitchen	10	24OCT11	04NOV11	10OCT11	21OCT11	-10d	0
Completion									
	ENDK	Complete Kitchen	5	31OCT11	04NOV11	17OCT11	21OCT11	-10d	0

Media Center, Art Rooms

	Roughing-in								
	HV205	Rough-Ductwork-Mains, Media/Art	10	28MAR11	08APR11	21MAR11	01APR11	-5d	0
	PL305	Plumbing - Rough & Test, Media/Art	15	04APR11	22APR11	28MAR11	15APR11	-5d	0
	EL205	Electric - Rough Mains, Risers; Media/Art	15	11APR11	29APR11	04APR11	22APR11	-5d	0
	HV305	Rough HVAC Piping, Media/Art	15	11APR11	29APR11	04APR11	22APR11	-5d	0
	HV215	Complete Rough Ductwork, Media/Art	15	11APR11	29APR11	25APR11	13MAY11	10d	0
	DW205	Interior Metal Stud Framing, Media/Art	20	18APR11	13MAY11	11APR11	06MAY11	-5d	0
	FP205	Fire Protection - Rough & Test, Media/Art	20	18APR11	13MAY11	18APR11	13MAY11	0	0
	PL315	Plumbing - Rough Inspect, Media/Art	5	25APR11	29APR11	18APR11	22APR11	-5d	0
	EL305	Electric - Rough Ptns & Complete, Media/Art	15	25APR11	13MAY11	18APR11	06MAY11	-5d	0
	HV405	Controls - Roughing-in, Media/Art	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
	HV505	HVAC Pipe Insulation, Media/Art	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
	PL405	Plumbing - Pipe Covering, Media/Art	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
	RC415	Interior Rough Carpentry, Media/Art	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
	TC305	Telecommunications Rough, Media/Art	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
	EL405	Electric - Inspect Rough-in, Media/Art	5	16MAY11	20MAY11	09MAY11	13MAY11	-5d	0

Interior Finishes

DW305	Drywall, Tape & Sand, Media/Art	20	30MAY11	24JUN11	16MAY11	10JUN11	-10d	0
PA105	Prime Paint, Media/Art	15	20JUN11	08JUL11	13JUN11	01JUL11	-5d	0
FS105	Firestopping, Media/Art	15	27JUN11	15JUL11	01AUG11	19AUG11	25d	0
DW405	Touch-up Drywall, Media/Art	10	11JUL11	22JUL11	08AUG11	19AUG11	20d	0
CL105	Ceiling Grid, Media/Art	15	11JUL11	29JUL11	04JUL11	22JUL11	-5d	0
HV705	HVAC Radiation, Media/Art	15	11JUL11	29JUL11	18JUL11	05AUG11	5d	0
CT105	Ceramic Tile Toilets, Media/Art	15	11JUL11	29JUL11	01AUG11	19AUG11	15d	0
WP205	Interior Caulking, Media/Art	15	11JUL11	29JUL11	01AUG11	19AUG11	15d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 12A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	DW505	Misc. Interior Drywall, Media/Art	10	01AUG11	12AUG11	22AUG11	02SEP11	15d	0
	FC105	Finish Millwork, Media/Art	15	01AUG11	19AUG11	25JUL11	12AUG11	-5d	0
	FC205	Hang Interior Doors, Media/Art	15	01AUG11	19AUG11	08AUG11	26AUG11	5d	0
	HV805	ATC Controls - Finish, Media/Art	15	01AUG11	19AUG11	08AUG11	26AUG11	5d	0
	PL705	Plumbing Finish, Media/Art	15	01AUG11	19AUG11	22AUG11	09SEP11	15d	0
	CW105	Fixed Casing, Media/Art	15	01AUG11	19AUG11	05SEP11	23SEP11	25d	0
	EL705	Lighting Fixtures, Media/Art	15	01AUG11	19AUG11	05SEP11	23SEP11	25d	0
	FP405	Fire Protection - Finish Heads, Media/Art	15	01AUG11	19AUG11	05SEP11	23SEP11	25d	0
	HV715	Reg. Grilles, Finishes, Media/Art	15	01AUG11	19AUG11	05SEP11	23SEP11	25d	0
	CB105	MB/TB, Media/Art	5	22AUG11	26AUG11	15AUG11	19AUG11	-5d	0
	TP105	Toilet Compartments, Media/Art	10	22AUG11	02SEP11	12SEP11	23SEP11	15d	0
	CL205	Ceiling Tile, Media/Art	10	22AUG11	02SEP11	26SEP11	07OCT11	25d	0
	RS105	VCT, Media/Art	15	22AUG11	09SEP11	29AUG11	16SEP11	5d	0
	PA205	Finish Paint Walls & Ceilings, Media/Art	15	29AUG11	16SEP11	22AUG11	09SEP11	-5d	0
	TA105	Toilet Accessories, Media/Art	10	05SEP11	16SEP11	26SEP11	07OCT11	15d	0
	CP105	Carpet, Media/Art	5	12SEP11	16SEP11	19SEP11	23SEP11	5d	0
	FC215	Complete Finish Hardware, Media/Art	15	12SEP11	30SEP11	19SEP11	07OCT11	5d	0
	AP105	Sound Wall Panels, Media	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	MS105	Miscellaneous Specialties, Media/Art	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	PA605	Misc. Painting, Media/Art	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	RS405	Vinyl Base, Media/Art	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	EL805	Electric Finishes, Media/Art	15	19SEP11	07OCT11	12SEP11	30SEP11	-5d	0
	TC805	Telecommunications Finish, Media/Art	15	26SEP11	14OCT11	19SEP11	07OCT11	-5d	0
Completion									
	ENDM	Complete Media/Art	5	17OCT11	21OCT11	10OCT11	14OCT11	-5d	0

Main Entrance, Lobby, Administration

Roughing-in

HV206	Rough Ductwork, Lobby/Admin	15	11APR11	29APR11	04APR11	22APR11	-5d	0
HV306	Rough HVAC Piping, Lobby/Admin	15	18APR11	06MAY11	11APR11	29APR11	-5d	0
FP206	Fire Protection - Rough & Test, Lobby/Admin	15	18APR11	06MAY11	23MAY11	10JUN11	25d	0
EL206	Electric - Rough Mains, Risers, Lobby/Admin	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
PL306	Plumbing - Rough & Test, Lobby/Admin	15	09MAY11	27MAY11	02MAY11	20MAY11	-5d	0
HV506	HVAC Pipe Insulation, Lobby/Admin	15	09MAY11	27MAY11	23MAY11	10JUN11	10d	0
DW206	Interior Metal Stud Framing, Lobby/Admin	15	16MAY11	03JUN11	09MAY11	27MAY11	-5d	0
PL316	Plumbing - Rough Inspect, Lobby/Admin	5	30MAY11	03JUN11	23MAY11	27MAY11	-5d	0
HV406	Controls - Roughing-in, Lobby/Admin	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
RC406	Interior Rough Carpentry, Lobby/Admin	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
EL306	Electric - Rough PIns & Complete, Lobby/Admin	15	30MAY11	17JUN11	16MAY11	03JUN11	-10d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 13A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	TC306	Telecommunications Rough, Lobby/Admin	15	30MAY11	17JUN11	23MAY11	10JUN11	-5d	0
	PL406	Plumbing - Pipe Covering, Lobby/Admin	10	06JUN11	17JUN11	30MAY11	10JUN11	-5d	0
	EL406	Electric - Inspect Rough-in, Lobby/Admin	5	20JUN11	24JUN11	06JUN11	10JUN11	-10d	0
Interior Finishes									
	DW306	Drywall, Tape & Sand, Lobby/Admin	15	27JUN11	15JUL11	13JUN11	01JUL11	-10d	0
	PA106	Prime Paint, Lobby/Admin	10	18JUL11	29JUL11	04JUL11	15JUL11	-10d	0
	CW106	Fixed Casework, Lobby/Admin	5	01AUG11	05AUG11	08AUG11	12AUG11	5d	0
	CL106	Ceiling Grid, Lobby/Admin	10	01AUG11	12AUG11	25JUL11	05AUG11	-5d	0
	CT106	Wall Tile, Lobby/Admin	20	01AUG11	26AUG11	18JUL11	12AUG11	-10d	0
	FC106	Finish Millwork, Lobby/Admin	25	01AUG11	02SEP11	25JUL11	26AUG11	-5d	0
	CB106	MB/TB, Display Cases, Lobby/Admin	5	15AUG11	19AUG11	08AUG11	12AUG11	-5d	0
	EL606	Lighting Fixtures, Lobby/Admin	10	15AUG11	26AUG11	22AUG11	02SEP11	5d	0
	FP406	Fire Protection - Finish, Lobby/Admin	10	15AUG11	26AUG11	22AUG11	02SEP11	5d	0
	HV706	HVAC Finish, Lobby/Admin	15	15AUG11	02SEP11	15AUG11	02SEP11	0	0
	MM106	Metal Handrails, Lobby/Admin	10	29AUG11	09SEP11	05SEP11	16SEP11	5d	0
	CT206	Porcelain Floor, Lobby/Admin	15	29AUG11	16SEP11	15AUG11	02SEP11	-10d	0
	EL706	Electric Finish, Lobby/Admin	15	29AUG11	16SEP11	15AUG11	02SEP11	-10d	0
	TC806	Telecommunications Finish, Lobby/Admin	15	29AUG11	16SEP11	15AUG11	02SEP11	-10d	0
	CP106	Carpet, Lobby/Admin	10	19SEP11	30SEP11	05SEP11	16SEP11	-10d	0
	RS406	Vinyl Base, Lobby/Admin	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	PA206	Complete Finish Paint, Lobby/Admin	10	03OCT11	14OCT11	19SEP11	30SEP11	-10d	0
	CL206	Ceiling Tile, Lobby/Admin	10	17OCT11	28OCT11	03OCT11	14OCT11	-10d	0
Completion									
	ENDL	Complete Lobby/Admin	5	31OCT11	04NOV11	17OCT11	21OCT11	-10d	0
Mechanical and Electrical Rooms									
Foundations and Structure									
	SL107	Concrete Equipment Pads	5	09MAY11	13MAY11	02MAY11	06MAY11	-5d	0
Roughing-in									
	FP107	Fire Protection - Set Pump in Pit	5	09MAY11	13MAY11	02MAY11	06MAY11	-5d	0
	LV107	Louver, Mech/Elect.	5	09MAY11	13MAY11	11JUL11	15JUL11	45d	0
	EL507	Switchgear - Set & Connect	20	09MAY11	03JUN11	27JUN11	22JUL11	35d	0
	HV607	HVAC Boiler Room & Mechanical Room	40	09MAY11	01JUL11	25APR11	17JUN11	-10d	0
	PL507	Plumbing - at Fire Pump Pit	15	16MAY11	03JUN11	09MAY11	27MAY11	-5d	0
	FP217	Fire Protection - at Fire Pump Pit	15	16MAY11	03JUN11	30MAY11	17JUN11	10d	0
	PL607	Plumbing - Boiler Room Piping	25	13JUN11	15JUL11	30MAY11	01JUL11	-10d	0
	FP207	Fire Protection, Mech/Elect	20	20JUN11	15JUL11	20JUN11	15JUL11	0	0
	PL617	Plumbing - Set & Connect Water Heater	15	27JUN11	15JUL11	13JUN11	01JUL11	-10d	0
	HV617	Breaching and Chimney Flue	10	04JUL11	15JUL11	01AUG11	12AUG11	20d	0
	EL517	Electric Connections at Mech Equipment	15	04JUL11	22JUL11	27JUN11	15JUL11	-5d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 14A of 20A

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
PL627	Plumbing - Gas Piping, Mech/Elect	10	18JUL11	29JUL11	04JUL11	15JUL11	-10d	0
PL309	Plumbing - Gas Piping to Roof Units	5	01AUG11	05AUG11	01AUG11	05AUG11	0	0
HV627	Complete HVAC at Boiler & Mech Room	20	01AUG11	26AUG11	18JUL11	12AUG11	-10d	0
Interior Finishes								
MM207	Roof Access Treads, Mech	5	09MAY11	13MAY11	11JUL11	15JUL11	45d	0
EL907	Activate Permanent Power	15	13JUN11	01JUL11	25JUL11	12AUG11	30d	0
PA107	Prime Paint, Mech/Elect	10	11JUL11	22JUL11	04JUL11	15JUL11	-5d	0
FP507	Fire Protection - Compl, Test, Inspect Fire Pump	5	18JUL11	22JUL11	03OCT11	07OCT11	55d	0
PA207	Finish Paint, Mech/Elect	10	29AUG11	09SEP11	19SEP11	30SEP11	15d	0
HV907	HVAC Start-up & Test	20	29AUG11	23SEP11	15AUG11	09SEP11	-10d	0
PA507	Sealed Concrete Floor, Mech/Elect	5	12SEP11	16SEP11	03OCT11	07OCT11	15d	0
EL807	Electric Finishes, Mech/Elect	10	19SEP11	30SEP11	10OCT11	21OCT11	15d	0
HV917	Permanent Systems Operational	5	26SEP11	30SEP11	19SEP11	23SEP11	-5d	0
HV927	HVAC Balancing	20	10OCT11	04NOV11	26SEP11	21OCT11	-10d	0

New Addition - Area D

New Addition - Area D

Foundations and Structure

SW3310D	Excavate Foundations, Area D	0	08SEP10 A	16SEP10 A	08SEP10 A	16SEP10 A		100
FN10D	Foundations - Area D	0	08SEP10 A	15OCT10 A	08SEP10 A	15OCT10 A		100
SW3320D	Footing Drain, Area D	2	17SEP10 A	02NOV10	17SEP10 A	10NOV10	6d	85
FN20D	Interior Footings, Piers, Area D	0	23SEP10 A	15OCT10 A	23SEP10 A	15OCT10 A		100
SW3340D	Perim Insul/Backfill Foundations, Area D	4	04OCT10 A	04NOV10	04OCT10 A	12NOV10	6d	75
FN30D	Grout Baseplates, Area D	4	05OCT10 A	04NOV10	05OCT10 A	19NOV10	11d	60
WP10D	Waterproofing, Area D	2	19OCT10 A	02NOV10	19OCT10 A	12NOV10	8d	85
PL10D	Underslab Plumbing, Area D	10	01NOV10	12NOV10	11OCT10	22OCT10	-15d	0
SW3330D	E/B for US Utilities, Area D	10	01NOV10	12NOV10	11OCT10	22OCT10	-15d	0
EL10D	Underslab Electric, Area D	10	01NOV10	12NOV10	25OCT10	05NOV10	-5d	0
SW3350D	BF, Partial Grade SOG, Area D	10	16NOV10	26NOV10	08NOV10	19NOV10	-5d	0
SL10D	Prep & Pour Slab-on-Grade, Area D	10	29NOV10	10DEC10	22NOV10	03DEC10	-5d	0
ST10D	Steel Erection - Area D	30	17JAN11	25FEB11	27DEC10	04FEB11	-15d	0
SL20D	Slabs-on-Deck, Area D	15	14FEB11	04MAR11	31JAN11	18FEB11	-10d	0

Exterior/Closing-in

DW10D	Ext. Studs/Sheath/Bkg Above Roofs, Part D	10	28FEB11	11MAR11	07FEB11	18FEB11	-15d	0
PL20D	Roof Drains, Area D	10	28FEB11	11MAR11	14FEB11	25FEB11	-10d	0
RC10D	Roof Blocking at High Roofs, Area D	10	28FEB11	11MAR11	14FEB11	25FEB11	-10d	0
HV10D	Set Roof Curbs, etc., Area D	5	07MAR11	11MAR11	21FEB11	25FEB11	-10d	0
RF30D	Deliver Thru-Wall Flashings, Area D	5	07MAR11	11MAR11	07MAR11	11MAR11	0	0
AB10D	Air Barrier at Walls Above Low Roofs, Area D	10	14MAR11	25MAR11	28FEB11	11MAR11	-10d	0
RC20D	Roof Blocking at Low Roofs, Area D	10	14MAR11	25MAR11	28MAR11	08APR11	10d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 15A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	RF10D	High Roof System, Area D	15	14MAR11	01APR11	28FEB11	18MAR11	-10d	0
	DW11D	Complete Ext Studs/Sheath/Blkg, Area D	25	14MAR11	15APR11	21FEB11	25MAR11	-15d	0
	MV10D	Masonry Veneer at Roofs, Area D	10	28MAR11	08APR11	14MAR11	25MAR11	-10d	0
	RF20D	Roof Hatch, Area D	5	04APR11	08APR11	11APR11	15APR11	5d	0
	SK10D	Unit Skylight, Area D	5	04APR11	08APR11	11APR11	15APR11	5d	0
	RF22D	Elevator Vent, Area D	5	04APR11	08APR11	02MAY11	06MAY11	20d	0
	RF21D	Roof Davit, Area D	5	04APR11	08APR11	25JUL11	29JUL11	80d	0
	AB20D	Air Membrane Barriers, Area D	25	04APR11	06MAY11	14MAR11	15APR11	-15d	0
	RC50D	Temp Access Doors EX-D184, Area D	5	11APR11	15APR11	09MAY11	13MAY11	20d	0
	RF11D	Low Roof System, Area D	10	11APR11	22APR11	11APR11	22APR11	0	0
	MV11D	Masonry Veneer, Area D	30	18APR11	27MAY11	28MAR11	06MAY11	-15d	0
	HV11D	Set Roof Top Equip., Area D	10	25APR11	06MAY11	02MAY11	13MAY11	5d	0
	WN10D	Wind/CW/SF, Area D	20	09MAY11	03JUN11	18APR11	13MAY11	-15d	0
	WN11D	Wind/CW/SF at Stair C122, Area D	5	30MAY11	03JUN11	09MAY11	13MAY11	-15d	0
	MP10D	Composite Wall Panels, Area D	30	30MAY11	08JUL11	16MAY11	24JUN11	-10d	0
	MP30D	Metal Wall Panels (Roof), Area D	15	11JUL11	29JUL11	11JUL11	29JUL11	0	0
	RF40D	Complete Fascia and Roof Metal, Area D	15	11JUL11	29JUL11	11JUL11	29JUL11	0	0
	WP30D	Exterior Sealants, Area D	15	25JUL11	12AUG11	25JUL11	12AUG11	0	0
	RF50D	Misc. Roofing, Area D	10	01AUG11	12AUG11	01AUG11	12AUG11	0	0
	RC60D	Remove Temp Access - Door EX-D184, Area D	5	19SEP11	23SEP11	19SEP11	23SEP11	0	0
	WN20D	Complete Alum Entr D184, Area D	5	26SEP11	30SEP11	26SEP11	30SEP11	0	0

Classroom Wing - First Floor

Roughing-in

HV201	Rough Ductwork Mains, 1st Class	20	04APR11	29APR11	21MAR11	15APR11	-10d	0
EL201	Electric - Rough Mains, Risers; 1st Class	20	11APR11	06MAY11	28MAR11	22APR11	-10d	0
HV301	Rough HVAC Piping, 1st Class	20	11APR11	06MAY11	28MAR11	22APR11	-10d	0
PL301	Plumbing - Rough & Test, 1st Class	20	11APR11	06MAY11	28MAR11	22APR11	-10d	0
DW201	Interior Metal Stud Framing, 1st Class	20	18APR11	13MAY11	04APR11	29APR11	-10d	0
EL301	Electric - Rough Ptns & Complete, 1st Class	20	25APR11	20MAY11	11APR11	06MAY11	-10d	0
FP201	Fire Protection - Rough & Test, 1st Class	20	25APR11	20MAY11	18APR11	13MAY11	-5d	0
HV211	Complete Rough Ductwork, 1st Class	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
HV401	Controls - Roughing-in, 1st Class	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
RC401	Interior Rough Carpentry, 1st Class	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
TC301	Telecommunications Rough, 1st Class	20	02MAY11	27MAY11	18APR11	13MAY11	-10d	0
PL311	Plumbing - Rough Inspect, 1st Class	5	09MAY11	13MAY11	25APR11	29APR11	-10d	0
HV501	HVAC Pipe Insulation, 1st Class	15	09MAY11	27MAY11	25APR11	13MAY11	-10d	0
PL401	Plumbing - Pipe Covering, 1st Class	10	16MAY11	27MAY11	02MAY11	13MAY11	-10d	0
EL401	Electric - Inspect Rough-in, 1st Class	5	23MAY11	27MAY11	09MAY11	13MAY11	-10d	0

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 16A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Interior Finishes									
	DW301	Drywall, Tape & Sand, 1st Class	20	06JUN11	01JUL11	16MAY11	10JUN11	-15d	0
	FS101	Firestopping, 1st Class	15	20JUN11	08JUL11	04JUL11	22JUL11	10d	0
	PA101	Prime Paint, 1st Class	15	27JUN11	15JUL11	27JUN11	15JUL11	0	0
	CB101	MB/TB, 1st Class	10	18JUL11	29JUL11	01AUG11	12AUG11	10d	0
	DW401	Touch-up Drywall, 1st Class	10	18JUL11	29JUL11	01AUG11	12AUG11	10d	0
	FC101	Finish Millwork, 1st Class	10	18JUL11	29JUL11	01AUG11	12AUG11	10d	0
	CT101	Ceramic Tile Toilets, 1st Class	15	18JUL11	05AUG11	18JUL11	05AUG11	0	0
	WP201	Interior Caulking, 1st Class	15	18JUL11	05AUG11	25JUL11	12AUG11	5d	0
	CL101	Ceiling Grid, 1st Class	20	18JUL11	12AUG11	25JUL11	19AUG11	5d	0
	RS101	VCT Rooms, 1st Class	10	01AUG11	12AUG11	22AUG11	02SEP11	15d	0
	FC201	Hang Interior Doors, 1st Class	15	01AUG11	19AUG11	15AUG11	02SEP11	10d	0
	PL701	Plumbing Finish, 1st Class	15	08AUG11	26AUG11	22AUG11	09SEP11	10d	0
	CT201	Wall Tile at Corridors, 1st Class	20	08AUG11	02SEP11	08AUG11	02SEP11	0	0
	CP101	Carpet, 1st Class	5	15AUG11	19AUG11	12SEP11	16SEP11	20d	0
	PA201	Finish Paint Walls & Ceilings, 1st Class	15	15AUG11	02SEP11	15AUG11	02SEP11	0	0
	HV701	HVAC Radiation, 1st Class	15	15AUG11	02SEP11	22AUG11	09SEP11	5d	0
	HV711	Reg, Grilles, Fans, Finishes, 1st Class	15	15AUG11	02SEP11	05SEP11	23SEP11	15d	0
	FC211	Complete Finish Hardware, 1st Class	15	15AUG11	02SEP11	19SEP11	07OCT11	25d	0
	CW101	Fixed Casework, 1st Class	20	15AUG11	09SEP11	22AUG11	16SEP11	5d	0
	EL701	Lighting Fixtures, 1st Class	20	15AUG11	09SEP11	29AUG11	23SEP11	10d	0
	FP401	Fire Protection - Finish Heads, 1st Class	20	15AUG11	09SEP11	29AUG11	23SEP11	10d	0
	TP101	Toilet Compartments, 1st Class	10	29AUG11	09SEP11	12SEP11	23SEP11	10d	0
	FC111	Finish Millwork at Corridor, 1st Class	5	05SEP11	09SEP11	26SEP11	30SEP11	15d	0
	RS301	Linoleum Corridors, 1st Class	10	05SEP11	16SEP11	05SEP11	16SEP11	0	0
	HV801	ATC Controls - Finish, 1st Class	10	05SEP11	16SEP11	12SEP11	23SEP11	5d	0
	MS101	Miscellaneous Specialties, 1st Class	10	05SEP11	16SEP11	26SEP11	07OCT11	15d	0
	EL801	Electric Finishes, 1st Class	20	05SEP11	30SEP11	06SEP11	30SEP11	0	0
	DW501	Misc. Interior Drywall, 1st Class	10	12SEP11	23SEP11	19SEP11	30SEP11	5d	0
	TA101	Toilet Accessories, 1st Class	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
	PL711	Plumbing Fixtures Classrooms, 1st Class	15	12SEP11	30SEP11	19SEP11	07OCT11	5d	0
	CL201	Ceiling Tile, 1st Class	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	RS401	Vinyl Base, 1st Class	15	19SEP11	07OCT11	19SEP11	07OCT11	0	0
	TC801	Telecommunications Finish, 1st Class	15	19SEP11	07OCT11	19SEP11	07OCT11	0	0
	PA601	Misc. Painting, 1st Class	5	26SEP11	30SEP11	03OCT11	07OCT11	5d	0
	EM101	Entrance Mats, 1st Class	5	03OCT11	07OCT11	03OCT11	07OCT11	0	0
Completion									
	END1	Complete 1st Class	10	10OCT11	21OCT11	10OCT11	21OCT11	0	0

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 17A of 20A

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Classroom Wing - Second Floor								
Roughing-in								
HV202	Rough Ductwork Mains, 2nd Class	20	18APR11	13MAY11	04APR11	29APR11	-10d	0
EL202	Electric - Rough Mains, Riser, 2nd Class	20	25APR11	20MAY11	18APR11	13MAY11	-5d	0
HV302	Rough HVAC Piping, 2nd Class	20	25APR11	20MAY11	18APR11	13MAY11	-5d	0
PL302	Plumbing - Rough & Test, 2nd Class	20	25APR11	20MAY11	18APR11	13MAY11	-5d	0
DW202	Interior Metal Stud Framing, 2nd Class	20	02MAY11	27MAY11	18APR11	13MAY11	-10d	0
EL302	Electric - Rough Ptns & Complete, 2nd Class	20	09MAY11	03JUN11	02MAY11	27MAY11	-5d	0
FP202	Fire Protection - Rough & Test, 2nd Class	20	09MAY11	03JUN11	09MAY11	03JUN11	0	0
HV212	Complete Rough Ductwork, 2nd Class	15	16MAY11	03JUN11	16MAY11	03JUN11	0	0
HV402	Controls - Roughing-in, 2nd Class	15	16MAY11	03JUN11	16MAY11	03JUN11	0	0
RC402	Interior Rough Carpentry, 2nd Class	15	16MAY11	03JUN11	16MAY11	03JUN11	0	0
TC302	Telecommunications Rough, 2nd Class	20	16MAY11	10JUN11	09MAY11	03JUN11	-5d	0
PL312	Plumbing - Rough Inspect, 2nd Class	5	23MAY11	27MAY11	16MAY11	20MAY11	-5d	0
HV502	HVAC Pipe Insulation, 2nd Class	15	23MAY11	10JUN11	16MAY11	03JUN11	-5d	0
PL402	Plumbing - Pipe Covering, 2nd Class	10	30MAY11	10JUN11	23MAY11	03JUN11	-5d	0
EL402	Electric - Inspect Rough-in, 2nd Class	5	06JUN11	10JUN11	30MAY11	03JUN11	-5d	0
Interior Finishes								
DW302	Drywall, Tape & Sand, 2nd Class	20	27JUN11	22JUL11	06JUN11	01JUL11	-15d	0
FS102	Firestopping, 2nd Class	15	11JUL11	29JUL11	04JUL11	22JUL11	-5d	0
PA102	Prime Paint, 2nd Class	15	18JUL11	05AUG11	27JUN11	15JUL11	-15d	0
CB102	MB/TB, 2nd Class	10	08AUG11	19AUG11	01AUG11	12AUG11	-5d	0
DW402	Touch-up Drywall, 2nd Class	10	08AUG11	19AUG11	01AUG11	12AUG11	-5d	0
FC102	Finish Millwork, 2nd Class	10	08AUG11	19AUG11	01AUG11	12AUG11	-5d	0
CT102	Ceramic Tile Toilets, 2nd Class	15	08AUG11	26AUG11	18JUL11	05AUG11	-15d	0
WP202	Interior Caulking, 2nd Class	15	08AUG11	26AUG11	25JUL11	12AUG11	-10d	0
CL102	Ceiling Grid, 2nd Class	20	08AUG11	02SEP11	25JUL11	19AUG11	-10d	0
RS102	VCT Rooms, 2nd Class	10	22AUG11	02SEP11	22AUG11	02SEP11	0	0
FC202	Hang Interior Doors, 2nd Class	15	22AUG11	09SEP11	15AUG11	02SEP11	-5d	0
PA202	Finish Paint Walls & Ceilings, 2nd Class	15	29AUG11	16SEP11	15AUG11	02SEP11	-10d	0
PL702	Plumbing Finish, 2nd Class	15	29AUG11	16SEP11	22AUG11	09SEP11	-5d	0
CT202	Wall Tile at Corridors, 2nd Class	20	29AUG11	23SEP11	08AUG11	02SEP11	-15d	0
CP102	Carpet, 2nd Class	5	05SEP11	09SEP11	12SEP11	16SEP11	5d	0
HV702	HVAC Radiation, 2nd Class	15	05SEP11	23SEP11	22AUG11	09SEP11	-10d	0
HV712	Reg, Grilles, Fans, Finishes, 2nd Class	15	05SEP11	23SEP11	05SEP11	23SEP11	0	0
FC212	Complete Finish Hardware, 2nd Class	15	05SEP11	23SEP11	19SEP11	07OCT11	10d	0
CW102	Fixed Casework, 2nd Class	20	05SEP11	30SEP11	22AUG11	16SEP11	-10d	0
EL702	Lighting Fixtures, 2nd Class	20	05SEP11	30SEP11	29AUG11	23SEP11	-5d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 18A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	FP402	Fire Protection - Finish Heads, 2nd Class	20	05SEP11	30SEP11	29AUG11	23SEP11	-5d	0
	TP102	Toilet Compartments, 2nd Class	10	19SEP11	30SEP11	12SEP11	23SEP11	-5d	0
	MS102	Miscellaneous Specialties, 2nd Class	10	19SEP11	30SEP11	26SEP11	07OCT11	5d	0
	EL802	Electric Finishes, 2nd Class	20	19SEP11	14OCT11	05SEP11	30SEP11	-10d	0
	FC112	Finish Millwork at Corridor, 2nd Class	5	26SEP11	30SEP11	26SEP11	30SEP11	0	0
	RS302	Linoleum Corridors, 2nd Class	10	26SEP11	07OCT11	05SEP11	16SEP11	-15d	0
	HV802	ATC Controls - Finish, 2nd Class	10	26SEP11	07OCT11	12SEP11	23SEP11	-10d	0
	DW502	Misc. Interior Drywall, 2nd Class	10	03OCT11	14OCT11	19SEP11	30SEP11	-10d	0
	TA102	Toilet Accessories, 2nd Class	10	03OCT11	14OCT11	26SEP11	07OCT11	-5d	0
	PL712	Plumbing Fixtures Classrooms, 2nd Class	15	03OCT11	21OCT11	19SEP11	07OCT11	-10d	0
	TC802	Telecommunications Finish, 2nd Class	15	03OCT11	21OCT11	19SEP11	07OCT11	-10d	0
	CL202	Ceiling Tile, 2nd Class	10	10OCT11	21OCT11	26SEP11	07OCT11	-10d	0
	RS402	Vinyl Base, 2nd Class	15	10OCT11	28OCT11	19SEP11	07OCT11	-15d	0
	PA602	Misc. Painting, 2nd Class	5	17OCT11	21OCT11	03OCT11	07OCT11	-10d	0
Completion									
	END2	Complete 2nd Class	10	31OCT11	11NOV11	10OCT11	21OCT11	-15d	0
Stairs and Elevator									
Foundations and Structure									
	MM108	Stairs & Rails C122, Area D	10	28FEB11	11MAR11	14MAR11	25MAR11	10d	0
	SL108	Concrete Pan Stairs C122, Area D	5	14MAR11	18MAR11	28MAR11	01APR11	10d	0
	MM118	Stairs & Rails D178, Area D	10	14MAR11	25MAR11	04APR11	15APR11	15d	0
	SL118	Concrete Pan Stairs D178, Area D	5	28MAR11	01APR11	18APR11	22APR11	15d	0
	SF105	Spray FP, Stairs, Area D	10	25APR11	06MAY11	25APR11	06MAY11	0	0
Roughing-in									
	EL208	Electric Rough, Stairs, Area D	10	16MAY11	27MAY11	02MAY11	13MAY11	-10d	0
	FP118	Fire Protection Rough, Stairs, Area D	10	16MAY11	27MAY11	02MAY11	13MAY11	-10d	0
	HV118	HVAC Rough, Stairs, Area D	10	16MAY11	27MAY11	02MAY11	13MAY11	-10d	0
	DW208	Shaft Walls, Elevator & Stairs, Area D	10	23MAY11	03JUN11	09MAY11	20MAY11	-10d	0
Interior Finishes									
	MM128	Misc. Metals at Elevator	5	06JUN11	10JUN11	08AUG11	12AUG11	45d	0
	DW508	Complete Sheetrock, Stairs	10	25JUL11	05AUG11	18JUL11	29JUL11	-5d	0
	PA108	Prime Paint, Stairs	5	08AUG11	12AUG11	01AUG11	05AUG11	-5d	0
	EV108	Elevator	30	08AUG11	16SEP11	15AUG11	23SEP11	5d	0
	CL108	Ceiling Grid, Stairs	10	15AUG11	26AUG11	08AUG11	19AUG11	-5d	0
	EL808	Electric Finish, Stairs	10	29AUG11	09SEP11	22AUG11	02SEP11	-5d	0
	FP408	Fire Protection Finish, Stairs	10	29AUG11	09SEP11	22AUG11	02SEP11	-5d	0
	HV708	HVAC Equip & Finishes, Stairs	10	29AUG11	09SEP11	22AUG11	02SEP11	-5d	0
	CT208	Wall Tile, Stairs	15	29AUG11	16SEP11	22AUG11	09SEP11	-5d	0
	CL208	Ceiling Tile, Stairs	10	12SEP11	23SEP11	06SEP11	16SEP11	-5d	0

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 19A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	MM208	Complete Metal Rails, Stairs	10	12SEP11	23SEP11	05SEP11	16SEP11	-5d	0
	CT218	Porcelain Floor, Elevator	5	19SEP11	23SEP11	26SEP11	30SEP11	5d	0
	FC108	Finish Millwork, Stairs	5	19SEP11	23SEP11	26SEP11	30SEP11	5d	0
	MM308	Roof Access Treads, Stairs	5	19SEP11	23SEP11	26SEP11	30SEP11	5d	0
	PA508	Seal Concrete Floor, Machine Room	5	19SEP11	23SEP11	26SEP11	30SEP11	5d	0
	RS208	Resilient Treads/Flooring/Base, Stairs	10	26SEP11	07OCT11	19SEP11	30SEP11	-5d	0
	EM108	Foot Grilles, Stairs	5	10OCT11	14OCT11	03OCT11	07OCT11	-5d	0
	PA208	Finish Paint, Stairs	10	10OCT11	21OCT11	03OCT11	14OCT11	-5d	0
	EM208	Entrance Mats, Stairs	5	17OCT11	21OCT11	10OCT11	14OCT11	-5d	0
Completion									
	EL908	Fire Alarm Test, Elevator	5	26SEP11	30SEP11	03OCT11	07OCT11	5d	0
	EV208	Elevator Final Inspection	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
	ENDS	Complete Stairs, Elevator	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0

Miscellaneous

Miscellaneous

EN1994 Compliant

FN10M Complete MISC. Foundations ✓ ✓ ✓ ✓ ✓ ✓ ✓

Interior Finishes

Completion

PL807	Plumbing - Gas Inspection	5	08AUG11	12AUG11	08AUG11	12AUG11	0	0
EL909	Fire Alarm - Final Inspection	5	24OCT11	28OCT11	10OCT11	14OCT11	-10d	0
PL809	Plumbing - Final Inspection	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0
EL919	Electric - Final Inspection	5	31OCT11	04NOV11	17OCT11	21OCT11	-10d	0

Overall Project Completion

Initial Sitework - Phase 1A

Completion	END1A	Complete Phase 1A	0		27AUG10 A		27AUG10 A		100
-------------------	-------	-------------------	---	--	-----------	--	-----------	--	-----

1

Phase 1 Completion

P.J. Stella Construction Corp.
October 2010 Update
Data Date: 10/29/10

**Pompo/Center Elementary School
Stow, MA**

Forwarded to Architect/Owner:
November 11, 2010
Page 20A of 20A

	Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
	GC420	Building Commissioning - Phase 1	50	29AUG11	04NOV11	15AUG11	21OCT11	-10d	0
	ENDP1	Complete - Phase 1	15	14NOV11	02DEC11	24OCT11	11NOV11	-15d	0
	ENFP1	Owner's Float - Phase 1	15	05DEC11	23DEC11	14NOV11	02DEC11	-15d	0
	ENSP1	Substantial Completion - Phase 1	0		23DEC11		02DEC11 *	-15d	0
	GC600	Owner - Teachers/Staff Move-in Phase 1	16	26DEC11	16JAN12	05DEC11	26DEC11	-15d	0

Phase 2

Completion	
GC610	Owner Vacate Existing Building
GC700	Phase 2
ENDP2	Substantial Completion - Phase 2

Project Open Submittals


09020.00

Stow Pompositicut Elementary School

P.J. Stella

29-Nov-10


In	Submittal Number	Type	Date In	Date Due	Review	Description	Comments
25	333110. 8	Product Data	11/4/2010	11/19/2010	JW	(8R2) Resubmittal - Risers & Accessor	
11	85113. 1	Certifications	11/18/2010	12/3/2010	HSR	(8) Glazing Certifications	
11	85113. 2	Product Data	11/18/2010	12/3/2010	HSR	(14) Glass Types CA&CT; CP; CF; TA&	
11	85113. 3	Product Data	11/18/2010	12/3/2010	HSR	(3) Series 3006i - Product Data	
11	85113. 4	Test Results	11/18/2010	12/3/2010	HSR	(9) Series 3006i Thermal Test Data	
11	85113. 5	Test Results	11/18/2010	12/3/2010	HSR	(7) Product Test Reports	
11	85113. 6	Product Data	11/18/2010	12/3/2010	HSR	(10) Series 3006i Warranties Sample	
11	88000. 2	Product Data	11/18/2010	12/3/2010	HSR	(1) Storefront and Curtain Wall Frame	
11	88000. 3	Product Data	11/18/2010	12/3/2010	HSR	(2) Storefront & Curtain Wall Frames	
11	88000. 4	Certifications	11/18/2010	12/3/2010	HSR	(7) Oldcastle Product Certificates Sa	
11	88000. 5	Product Data	11/18/2010	12/3/2010	HSR	(9) Oldcastle Glass Sample of special	
10	233713. 3	Product Data	11/19/2010	12/4/2010	SES	(1R2) Resubmittal - RGD Data Sheets	
10	233713. 4	Product Data	11/19/2010	12/4/2010	SES	(2R2) Resubmittal - Diffuser, Register,	
11	265100. 1	Product Data	11/18/2010	12/3/2010	MJB	(1) Interior Lighting - MA-CHPS - Prod	
11	265100. 2	Product Data	11/18/2010	12/3/2010	MJB	(2) Interior Lighting - Fixtures - Produ	
11	265100. 3	Product Data	11/18/2010	12/3/2010	MJB	(3) Interior Lighting - Emergency Ligh	
11	265100. 4	Product Data	11/18/2010	12/3/2010	MJB	(4) Interior Lighting - Ballasts - Produ	
11	265100. 5	Product Data	11/18/2010	12/3/2010	MJB	(5) Interior Lighting - Energy-Efficienc	
11	265100. 6	Product Data	11/18/2010	12/3/2010	MJB	(6) Interior Lighting - Photometric Dat	
11	265100. 7	Product Data	11/18/2010	12/3/2010	MJB	(7) Interior Lighting - Shop Drawings	
11	237200. 4	Product Data	11/18/2010	12/3/2010	SES	(1R2) Resubmittal - Venmar Product	
11	237200. 5	Shop Drawings	11/18/2010	12/3/2010	SES	(2R2) Resubmittal - Shop Dwgs:Air-to	
11	237200. 6	Product Data	11/18/2010	12/3/2010	SES	(12R2) Resubmittal - Venmar Sample	
10	51200. 33	Product Data	11/19/2010	12/4/2010	CK	(26) Primers Mfg Data - Sturo Letter o	
7	86200. 10	Test Results	11/22/2010	12/7/2010	HSR	(1R4) Resubmittal - Acrylic Test Data	
7	61753. 4	Product Data	11/22/2010	12/7/2010	HSR	(2R2) Resubmittal - Connectors, Acce	
7	61753. 5	Shop Drawings	11/22/2010	12/7/2010	HSR	(3R2) Resubmittal - Reliable Truss Sh	
7	61753. 6	Product Data	11/22/2010	12/7/2010	HSR	(4R2) Resubmittal - Delegated-Desig	
7	22533. 24	Product Data	11/22/2010	12/7/2010	C @ CDV	(15) ACM Waste Removal Manifests # to KC @ CDW on 11/23/10	
7	12900. 15	Shop Drawings	11/22/2010	12/7/2010	HSR	(34R2) Resubmittal - Site Utilization P	
7	237200. 7	Samples	11/22/2010	12/7/2010	HSR	(7) Venmar Color Samples	
6	84113. 1	Samples	11/23/2010	12/8/2010	HSR	(5) EFCO D518 Door Fabrication Sam	
11	84133. 1	Product Data	11/18/2010	12/3/2010	HSR	(1) Glazed Aluminum Curtain Wall -	
11	84133. 2	Product Data	11/18/2010	12/3/2010	HSR	(2) EFCO Series 5500 & 5600 with 325	
11	84133. 3	Test Results	11/18/2010	12/3/2010	HSR	(9) EFCO Series 5500 & 5600 with 325	
11	84133. 4	Test Results	11/18/2010	12/3/2010	HSR	(10) EFCO Series 5500 & 5600 with 32	
11	84133. 5	Product Data	11/18/2010	12/3/2010	HSR	(11) EFCO Warranties: Sample	
11	84413. 1	Product Data	11/18/2010	12/3/2010	HSR	(084113-1) MA-CHPS Submittal	
11	84113. 1	Product Data	11/18/2010	12/3/2010	HSR	(1) MA-CHPS Submittal	
11	84113. 2	Product Data	11/18/2010	12/3/2010	HSR	(10) Warranties: Sample	
11	84113. 3	Product Data	11/18/2010	12/3/2010	HSR	(17) EFCO Series 403-1 & 402 Mfg Dat	
11	84113. 4	Test Results	11/18/2010	12/3/2010	HSR	(18) EFCO Series 403-1 & 402 Product	
11	84113. 5	Test Results	11/18/2010	12/3/2010	HSR	(19) EFCO Series 403-1 & 402 Therma	
6	81113. 2	Samples	11/23/2010	12/8/2010	HSR	Hollow Metal Frame Sample - Substit	
6	84413. 2	Samples	11/23/2010	12/8/2010	HSR	(19) EFCO Series 5600 - Fabrication S	
6	84113. 6	Samples	11/23/2010	12/8/2010	HSR	(5) EFCO Series 402 Fabrication Sam	
6	84413. 3	Samples	11/23/2010	12/8/2010	HSR	(19) EFCO Series 5500 Fabrication Sa	
6	84113. 7	Samples	11/23/2010	12/8/2010	HSR	(5) EFCO Series 403I Fabrication Sam	



RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional
 Job Name: Stow Pompositicut Elementary School
 Job Location:
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
001	OK	1	6/15/2010	PJ Stella	6/16/2010	6/16/2010	Grade Beam Reinforcing	RMC
002	OK	4	6/21/2010	PJ Stella	6/21/2010	6/25/2010	30" Drain Line Note	JW
003	OK	2	6/21/2010	PJ Stella	6/21/2010	6/23/2010	Enclosure Fence Windscreen	MSA
004	OK	31	6/22/2010	PJ Stella	6/25/2010	7/26/2010	Roof Drain Piping	HSR
005	OK	16	6/29/2010	PJ Stella	6/29/2010	7/15/2010	Part B Canopy/Foundation	JW
006	OK	6	7/16/2010	PJ Stella	7/16/2010	7/22/2010	Survey Information	HSR
007	OK	4	7/19/2010	PJ Stella	7/19/2010	7/23/2010	Materials Attributes Calculations	HSR
008	OK	3	7/23/2010	PJ Stella	7/23/2010	7/26/2010	Primary Electric Duct-Bank Conduit	HSR
009	OK	31	7/27/2010	PJ Stella	7/27/2010	8/27/2010	Electric Service Pole	HSR
010	OK	9	7/28/2010	PJ Stella	7/28/2010	8/6/2010	Electric Panel at Existing Building	RMC
011	OK	5	7/28/2010	Sturo	7/28/2010	8/2/2010	Sturo RFI #01 - Cols. on line W	RMC
012	OK	5	7/28/2010	Sturo	7/28/2010	8/2/2010	Sturo RFI #2 - Typ. B racing Gusset	RMC
013	OK	12	8/8/2010	PJ Stella	8/8/2010	8/20/2010	Addendum #1 Footing Change	MJB
014	OK	3	7/30/2010	PJ Stella	7/30/2010	8/2/2010	Pole Riser Conduits	CK
015	OK	1	8/2/2010	PJ Stella	8/2/2010	8/3/2010	Pier Dimensions	JW
016	OK	2	8/3/2010	PJ Stella	8/3/2010	8/5/2010	Storm Drain Headwall	RMC
017	OK	0	8/6/2010	PJ Stella	8/6/2010	8/6/2010	Slab On Grade Base Course	RMC
018	OK	0	8/6/2010	PJ Stella	8/6/2010	8/6/2010	Footing Subgrade Preparation	HSR
019	OK	21	8/6/2010	PJ Stella	8/6/2010	8/27/2010	Phase 1A Asbestos Quantities	RMC
020	OK	27	8/6/2010	PJ Stella	8/6/2010	9/2/2010	Sturo RFI #3 Davit Location & Dims	JW
021	OK	14	8/13/2010	PJ Stella	8/13/2010	8/27/2010	Site Grading Information	HSR
022	OK	0	8/13/2010	PJ Stella	8/13/2010	8/13/2010	Parts A and B Roof Details	LBF
022.2	OK	5	8/19/2010	PJ Stella	8/19/2010	8/24/2010	Parts A and B Roof Details (Follow-up)	HSR
023	OK	1	8/17/2010	PJ Stella	8/17/2010	8/18/2010	0.40 W/C Concrete	RMC
23.2	OK	1	8/19/2010	PJ Stella	8/19/2010	8/20/2010	0.40 W/C Concrete	LBF
024	OK	29	8/17/2010	PJ Stella	8/17/2010	9/15/2010	Building Layout Discrepancies	HSR
024R1	OK	21	8/25/2010	PJ Stella	8/25/2010	9/15/2010	Building Layout Discrepancies - PJS Field Sketches	LBF
025	OK	1	8/17/2010	PJ Stella	8/17/2010	8/18/2010	Wood Flooring Systems	JED
026	OK	1	8/19/2010	PJ Stella	8/19/2010	8/20/2010	Basketball Backstops Supports	HSR
027	OK	5	8/19/2010	PJ Stella	8/19/2010	8/24/2010	Lobby Skylight Size	HSR
028	OK	1	8/19/2010	PJ Stella	8/19/2010	8/20/2010	Part A Existing Door Openings	HSR
029	OK	13	8/20/2010	PJ Stella	8/20/2010	9/2/2010	Waterproofing Dimension	CK
030	OK	9	8/22/2010	Sturo	8/22/2010	8/31/2010	Dim and Size - Sturo RFI #13 and sketch regarding same	RMC
031	OK	5	8/22/2010	Sturo	8/22/2010	8/27/2010	Hole at B Brace - Sturo RFI #14	



RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional
 Job Name: Stow Pomposittut Elementary School
 Job Location:
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Reviewer	
					Received	Returned
032	OK	9	8/22/2010	Sturo	8/22/2010	8/31/2010 Screen Wall - Sturo RFI #16
033	OK	9	8/22/2010	Sturo	8/22/2010	8/31/2010 Column at U/21 - Sturo RFI #17
034	OK	4	8/23/2010	Sturo	8/23/2010	8/27/2010 Column Prep - Sturo RFI #18
034.2	OK	4	8/30/2010	PJ Stella	8/30/2010	9/3/2010 Column Prep - Sturo RFI #18
035	OK	8	8/22/2010	Sturo	8/23/2010	8/31/2010 Stair D178 - Sturo RFI #9
036	OK	8	8/22/2010	Sturo	8/23/2010	8/31/2010 Skylight Frame - Sturo RFI #10
037	OK	8	8/22/2010	Sturo	8/23/2010	8/31/2010 Edge of Slab - Sturo RFI #11
038	OK	9	8/22/2010	R&R	8/22/2010	8/31/2010 Frame SF14 - R&R RFI #01
039	OK	9	8/22/2010	R&R	8/22/2010	8/31/2010 Curtain Wall - R&R RFI #03
040	OK	8	8/25/2010	Sturo	8/25/2010	9/2/2010 C-D Corner - Sturo RFI #08
041	OK	1	8/26/2010	Sturo	8/26/2010	8/27/2010 Masonry Ties - Sturo RFI #19
042	OK	8	8/26/2010	Sturo	8/26/2010	9/3/2010 Det. 3/S2.03 - Sturo RFI #20
043	OK	7	8/26/2010	Sturo	8/26/2010	9/2/2010 Dim. at 24 and 30 - S turo RFI #21
044	OK	7	8/26/2010	Sturo	8/26/2010	9/2/2010 Bldg D Connections - Sturo RFI #24
045	OK	5	8/26/2010	Sturo	8/26/2010	8/31/2010 Applied Fireproofing Scope
046	OK	6	8/27/2010	PJ Stella	8/27/2010	9/2/2010 Platform Floor System
047	OK	5	8/28/2010	PJ Stella	8/28/2010	9/2/2010 Climbing Wall @ Gym
048	OK	5	8/28/2010	PJ Stella	8/28/2010	9/2/2010 Dim at F-Line - Sturo RFI #25
049	OK	4	8/30/2010	PJ Stella	8/30/2010	9/3/2010 Fire Tank Access Manholes
050	OK	1	8/30/2010	R&R	8/30/2010	8/31/2010 Operable Window Color
051	OK	1	8/30/2010	R&R	8/30/2010	8/31/2010 Sloped Glazing M19
052	OK	2	8/31/2010	PJ Stella	8/31/2010	9/2/2010 Onsite Reuse of materials
053	OK	1	9/1/2010	PJ Stella	9/1/2010	9/2/2010 Wood Doors Glazing
054	OK	1	9/2/2010	PJ Stella	9/2/2010	9/3/2010 Composite Wall Panel Accent Colors
055	OK	29	9/2/2010	PJ Stella	9/2/2010	10/1/2010 Pumping Concrete
056	OK	4	9/3/2010	PJ Stella	9/3/2010	9/7/2010 Fig Subgrade - fire pump pit
057	OK	2	9/7/2010	R&R	9/7/2010	9/9/2010 Operable Vents in Cur - R&R RFI #06
058	OK	2	9/7/2010	R&R	9/7/2010	9/9/2010 CW#6 Material - R&R RFI #07
059	OK	2	9/7/2010	R&R	9/7/2010	9/9/2010 Window Opg Clarificat- R&R RFI #08
060	OK	1	9/7/2010	R&R	9/7/2010	9/8/2010 Storefront Face Dimes - R&R RFI #09
061	OK	23	9/7/2010	R&R	9/7/2010	9/30/2010 Stair C122 Fire Rating - R&R RFI #10
062	OK	13	9/7/2010	R&R	9/7/2010	9/20/2010 Sloped Glazing - R&R RFI #11
063	OK	2	9/7/2010	Cindotta	9/7/2010	9/9/2010 R.S.F - Cincotta RFI #08
064	Overdue	82	9/8/2010	PJ Stella	9/8/2010	Titan Roofing Bonds Letter



RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional
 Job Name: Stow Pompositcut Elementary School
 Job Location:
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
065	OK	63	9/9/2010	Boston Showcase	9/9/2010	11/11/2010	Kitchen Equipment Customer Consent	HSR JW
066	OK	6	9/10/2010	P.J. Stella	9/10/2010	9/16/2010	Detectable Warning Panels	KCH
067	OK	6	9/10/2010	P.J. Stella	9/10/2010	9/16/2010	Electronic Scoreboards	HSR
068	OK	3	9/10/2010	Anneese	9/10/2010	9/13/2010	Watertight Seals - Anneese RFI #02	RMC
069	OK	3	9/14/2010	Studio	9/14/2010	9/17/2010	Vented Deck - Sturo RFI #26	KCH
070	OK	2	9/14/2010	R&R	9/14/2010	9/16/2010	Spanndrel Glass S - R&R RFI #12	CK
071	OK	2	9/15/2010	Studio	9/15/2010	9/17/2010	Roof Davit Bracket - Sturo RFI #27	CK
072	OK	2	9/15/2010	Studio	9/15/2010	9/17/2010	Elevation Discrepancy - Sturo RFI #29	CK
073	OK	2	9/15/2010	Sturo	9/15/2010	9/17/2010	Sturo RFI #31 - E elevations at 14/N	CK
073.2	OK	9	10/6/2010	P.J. Stella	10/6/2010	10/15/2010	Elevations at 14/N - S turo RFI #31	CK
074	OK	5	9/15/2010	Sturo	9/15/2010	9/20/2010	Screen Wall - Sturo RFI #32	CK
075	OK	0	9/16/2010	P.J. Stella	9/16/2010	9/16/2010	Gas Service Pit	MSA
075.2	OK	17	9/20/2010	P.J. Stella	9/20/2010	10/7/2010	Gas Service Pit	KCH
076	OK	1	9/16/2010	Sturo	9/16/2010	9/17/2010	Tube Steel Elev. - Sturo RFI #33	CK
077	OK	1	9/16/2010	Sturo	9/16/2010	9/17/2010	El. Chan. @ C/N - Sturo RFI #34	CK
078	OK	5	9/16/2010	Sturo	9/16/2010	9/21/2010	El. @ grid 1/M, & F - Sturo RFI #35	KCH
079	OK	11	9/20/2010	P.J. Stella	9/20/2010	10/1/2010	Longspan Joists @ Gym	CK
080	OK	3	9/20/2010	P.J. Stella	9/20/2010	9/23/2010	Exposed Structural Steel Finish	KCH
081	OK	4	9/17/2010	Cincotta	9/17/2010	9/21/2010	Pump Station Dims - Cincotta RFI #9	PSG
082	OK	25	9/17/2010	Sturo	9/17/2010	10/12/2010	W30x90 - Sturo RFI #36	RMC
083	OK	25	9/17/2010	Sturo	9/17/2010	10/12/2010	W27x55 Elevation - Sturo RFI #37	CK
084	OK	14	9/17/2010	Sturo	9/17/2010	10/1/2010	Bent Plate Elevation - Sturo RFI #38	CK
085	OK	14	9/17/2010	Sturo	9/17/2010	10/1/2010	Bent Plate Elevation - Sturo RFI #39	CK
086	OK	14	9/17/2010	Sturo	9/17/2010	10/1/2010	Bent Plate Elevation - Sturo RFI #40	KCH
087	OK	1	9/20/2010	R&R	9/20/2010	9/21/2010	CW#6 Material - R & R RFI#4	RMC
088	OK	10	9/20/2010	R&R	9/20/2010	9/30/2010	Glazing Color Match - R&R RFI#15	KCH
089	OK	1	9/22/2010	P.J. Stella	9/22/2010	9/23/2010	Maintenance Building Location - Excerpt of C3.01	JW
090	OK	14	9/23/2010	P.J. Stella	9/23/2010	10/7/2010	Exterior Soffit/Espan Joint Detail	KCH
091	OK	15	9/27/2010	Studio	9/27/2010	10/12/2010	Screen Wall Connection - Sturo RFI #44	CK
092	OK	21	9/27/2010	P.J. Stella	9/27/2010	10/18/2010	Entrance Sign Details	CK
093	OK	15	9/27/2010	Sturo	9/27/2010	10/12/2010	Outrigger at 30.1 - S turo RFI #41	CK
094	OK	14	9/28/2010	P.J. Stella	9/28/2010	10/12/2010	Joist Shop Drawings - Excerpt of Joist drawing J1	KCH
095	OK	9	9/28/2010	R&R	9/28/2010	10/7/2010	Sloped Glazing -	KCH
096	OK	7	9/30/2010	P.J. Stella	9/30/2010	10/7/2010	Elevator Scope Clarification	KCH



RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional
 Job Name: Stow Pomposititut Elementary School
 Job Location:
 Distribution:


RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
097	OK	9	9/28/2010	PJ Stella	9/28/2010	10/7/2010	Motorized Shades Scope Clarif.	KCH
098	OK	14	9/28/2010	Sturc	9/28/2010	10/12/2010	Dim at Wx10 - Sturo RFI #42	CK
099	OK	43	10/5/2010	PJ Stella	10/5/2010	11/17/2010	Window Shades Scope Clarification	KCH
100	OK	22	10/4/2010	PJ Stella	10/4/2010	10/26/2010	Telescoping Stands	KCH
101	OK	3	10/4/2010	PJ Stella	10/4/2010	10/7/2010	Retaining Wall Expansion Joint Detail	JW
101.2	OK	3	10/19/2011	PJ Stella	10/19/2010	10/22/2010	Retaining Wall Expansion Joint Detail	HSR
101.3	OK	0	10/29/2011	PJ Stella	10/29/2010	10/29/2010	Retaining Wall Expansion Joint Data	RMC
102	OK	2	10/4/2010	PJ Stella	10/4/2010	10/6/2010	Pump Station E1 - Cincotta RFI #10	JW
103	OK	1	10/4/2010	Cincotta	10/4/2010	10/5/2010	Infiltration Sys - Cincotta RFI #11	JW
104	OK	15	10/5/2010	PJ Stella	10/5/2010	10/20/2010	Operable Partition Support	KCH
105	OK	1	10/6/2010	RJ Cincotta	10/6/2010	10/7/2010	Cincotta RFI #12 - Inf. Sys. Fill	JW
106	OK	5	10/6/2010	Cincotta	10/6/2010	10/11/2010	Inverts @ Infill - Cincotta RFI #13	JW
107	OK	6	10/7/2010	PJ Stella	10/7/2010	10/7/2010	Remedial Work @ Sloped Footing 1/D	RMC
108	OK	8	10/14/2011	PJ Stella	10/14/2010	10/22/2010	Platform Stairs Layout	KCH
108.2	OK	5	11/12/2011	PJ Stella	11/12/2010	11/17/2010	Platform Stairs Layout	KCH
108.R1	OK	0	11/22/2011	PJ Stella	11/22/2010	11/22/2010	Platform Stairs Layout	RMC
109	OK	18	10/14/2011	PJ Stella	10/14/2010	11/1/2010	Leveling Plate Installation	KCH
110	OK	8	10/14/2011	PJ Stella	10/14/2010	10/22/2010	Exterior Mockup Materials	KCH
110.2	OK	0	11/12/2010	PJ Stella	11/12/2010	11/1/2010	Exterior Mockup Materials	JD
110.3	OK	0	11/4/2010	PJ Stella	11/4/2010	11/4/2010	Exterior Mockup Materials	KCH
110.4	OK	3	11/19/2011	PJ Stella	11/19/2010	11/22/2010	Exterior Mockup Materials	HSR
111	OK	7	10/15/2011	PJ Stella	10/15/2010	10/22/2010	Gym Floor Outlet Locations	KCH
112	OK	7	10/15/2011	PJ Stella	10/15/2010	10/22/2010	Platform Electrical Outlet Location	KCH
113	OK	7	10/15/2011	PJ Stella	10/15/2010	10/22/2010	Computer/Media Floor Outlets	KCH
114	OK	20	10/15/2011	R&R	10/15/2010	11/4/2010	Glazing Make-Up - R&R RFI #16	HSR
114.2	OK	31	10/18/2011	R&R	10/18/2010	11/18/2010	Glazing Make-Up - R&R RFI #16	MJB
115	OK	5	10/15/2011	Starley	10/15/2010	10/20/2010	Elevator Power - Stanley RFI #1	CK
116	OK	0	10/18/2011	Stup	10/18/2010	10/18/2010	Detail 11/S 4.03 - Sturo RFI #46	MJB
117	OK	28	10/18/2011	Annesse	10/18/2010	11/15/2010	DDC Location - Annesse RFI #4	LBF
118	OK	8	10/20/2011	Cincotta	10/20/2010	10/28/2010	Cincotta RFI #14 - 14K Recirc Tank	JW
118.2	OK	18	11/4/2010	PJ Stella	11/4/2010	11/22/2010	Cincotta RFI #14 - 14K Recirc Tank	RMC
119	OK	2	10/20/2011	PJ Stella	10/20/2010	10/22/2010	Rear dowels at column W/33	KCH
120	OK	5	10/21/2011	PJ Stella	10/21/2010	10/26/2010	Line 18 Foundation W all	RMC
121	OK	11	10/22/2011	PJ Stella	10/22/2010	11/2/2010	Per/Grade Beam @ V/36	



RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional
 Job Name: Stow Pompositcut Elementary School
 Job Location:
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Reviewer		
					Received	Returned	Description
122	OK	13	10/22/201	PJ Stella	10/22/2010	11/14/2010	Storage Garage Foundations
123	OK	23	10/25/201	PJ Stella	10/25/2010	11/17/2010	Cap Plate @ Z
124	OK	10	10/25/201	PJ Stella	10/25/2010	11/4/2010	Storage Garage Floor Pitch
124.2	OK	7	11/10/201	PJ Stella	11/10/2010	11/17/2010	Storage Garage Floor Pitch
125	OK	1	10/25/201	PJ Stella	10/25/2010	10/26/2010	Angle elev. - Sturo RFI #47
126	OK	6	10/27/201	PJ Stella	10/27/2010	11/2/2010	Elevator Pit Sump
127	OK	1	10/27/201	PJ Stella	10/27/2010	10/28/2010	Braced Column Pier Replacements
128	OK	19	10/28/201	PJ Stella	10/28/2010	11/17/2010	LIFD RFI #02 - Loc K Cylinder Types
129	OK	19	10/29/201	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #03 - Door A 101.2
130	OK	19	10/29/201	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #05 - Doors EX-A100, EX-A1
131	OK	19	10/29/201	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #06 - Doors C136A & C136C
132	OK	19	10/29/201	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #07 - Knurling Hardware
133	OK	19	10/29/201	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #08 - Door C134
134	OK	19	10/29/201	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #09 - Secure Side of Doors
135	OK	1	11/2/2010	PJ Stella	11/2/2010	11/3/2010	Retaining Wall Pour Lengths
136	OK	6	11/3/2010	PJ Stella	11/3/2010	11/9/2010	As-Built Pier Survey - Part C
136.2	Overdue	14	11/15/201	PJ Stella	11/15/2010		As-Built Pier Survey - Part C
137	OK	5	11/5/2010	PJ Stella	11/5/2010	11/10/2010	MACHPS Spreadsheets
138	OK	0	11/8/2010	PJ Stella	11/8/2010	11/8/2010	Housekeeping Pad C151.1
139	OK	5	11/10/201	PJ Stella	11/10/2010	11/15/2010	Lobby C130 Knee Walls
140	OK	1	11/10/201	Stup	11/10/2010	11/11/2010	Bldg B Conflict - Sturo RFI #50
140R1	OK	8	11/10/201	PJ Stella	11/10/2010	11/18/2010	Sturo RFI #50 - Bldg B Conflict
141	OK	1	11/10/201	Sturo	11/10/2010	11/11/2010	Roof Ops @ ERLU-1 - Sturo RFI #49
142	OK	1	11/10/201	PJ Stella	11/10/2010	11/11/2010	Steel Shop Dwg Approval Block 7A
143	OK						
144	OK						
145	OK	0	11/22/201	PJ Stella	11/22/2010	11/22/2010	Anchor Bolt Remediation
145.2	OK	1	11/23/201	PJ Stella	11/23/2010	11/24/2010	Anchor Bolt Remediation
146	OK	5	11/19/201	PJ Stella	11/19/2010	11/24/2010	Shaft Wall Thicknesses
147	Overdue	10	11/19/201	USD	11/19/2010		USD RFI #1
148	Overdue	10	11/19/201	USD	11/19/2010		Details at 3.11 - USD RFI #2
149	OK	3	11/19/201	R&R	11/19/2010	11/22/2010	SKA-045 - R&R RFI #18
150	OK	5	11/19/201	LIFD	11/19/2010	11/24/2010	Wood Door Stain - LIFD RFI #10
151	OK	0	11/22/201	PJ Stella	11/22/2010	11/22/2010	Vestibule C145 Dimension







RFI Report by Project



Job Number: 09020.00 Practice Group: Institutional
 Job Name: Stow Pompositicut Elementary School
 Job Location:
 Distribution:





RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
-------	--------	----------	----------	--------------	----------	----------	-------------	----------





152	OK	2	11/22/2011	Anneese	11/22/2010	11/24/2010	Anneese RFI #07 - Kitch. Phil & Trans	MJB
153	OK	7	11/22/2011	PJ Stella	11/22/2010		Additional Column Anchors	RMC

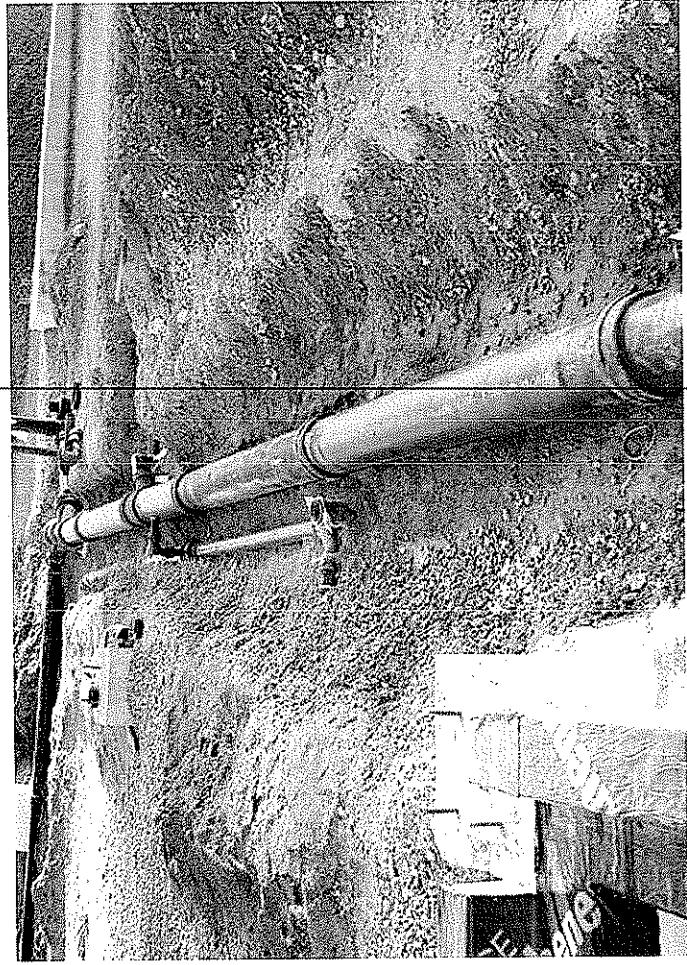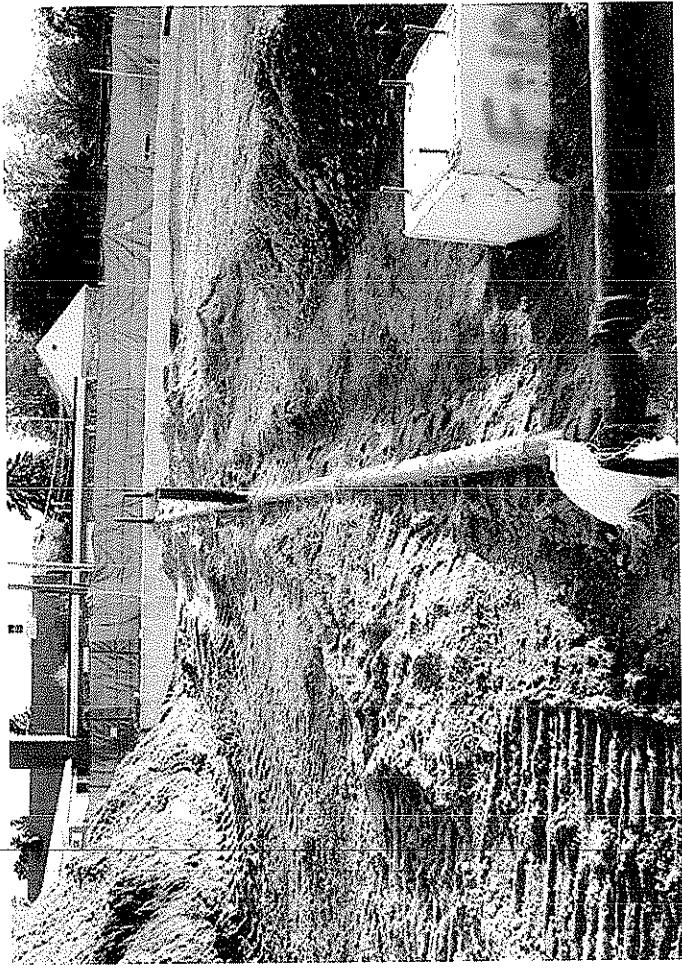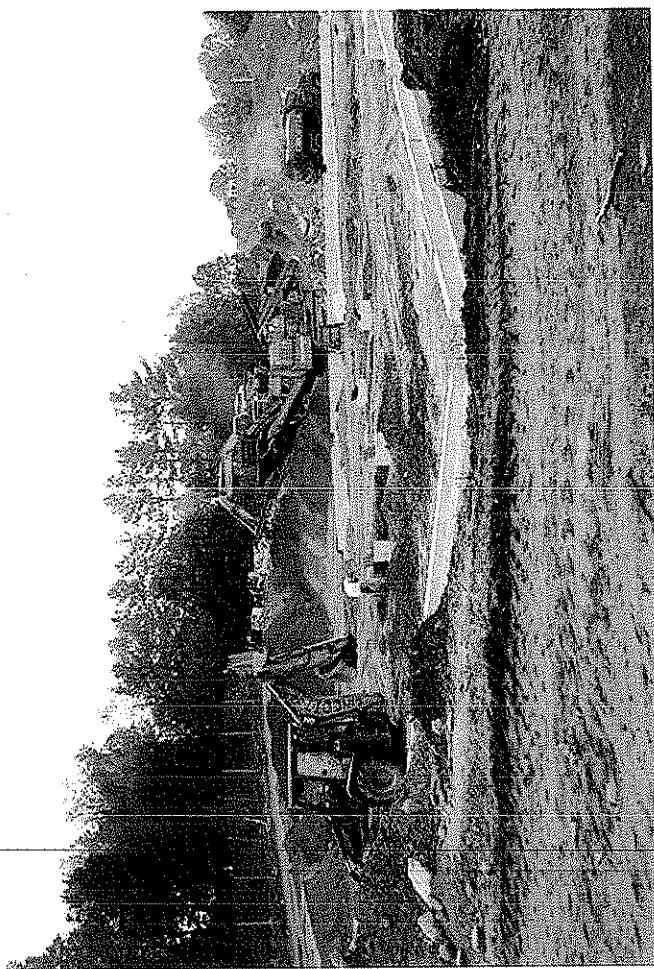

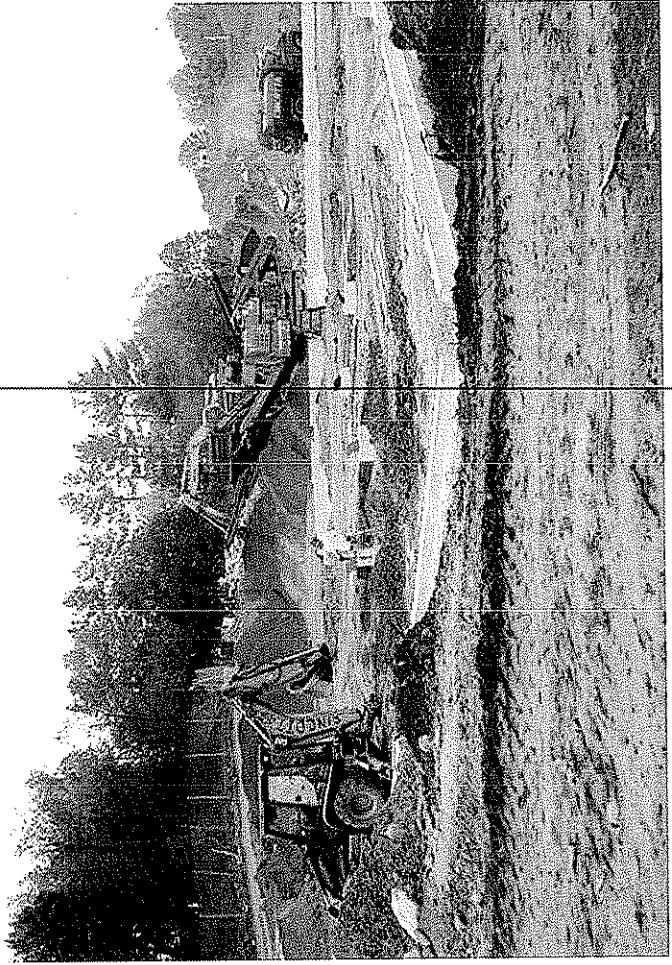

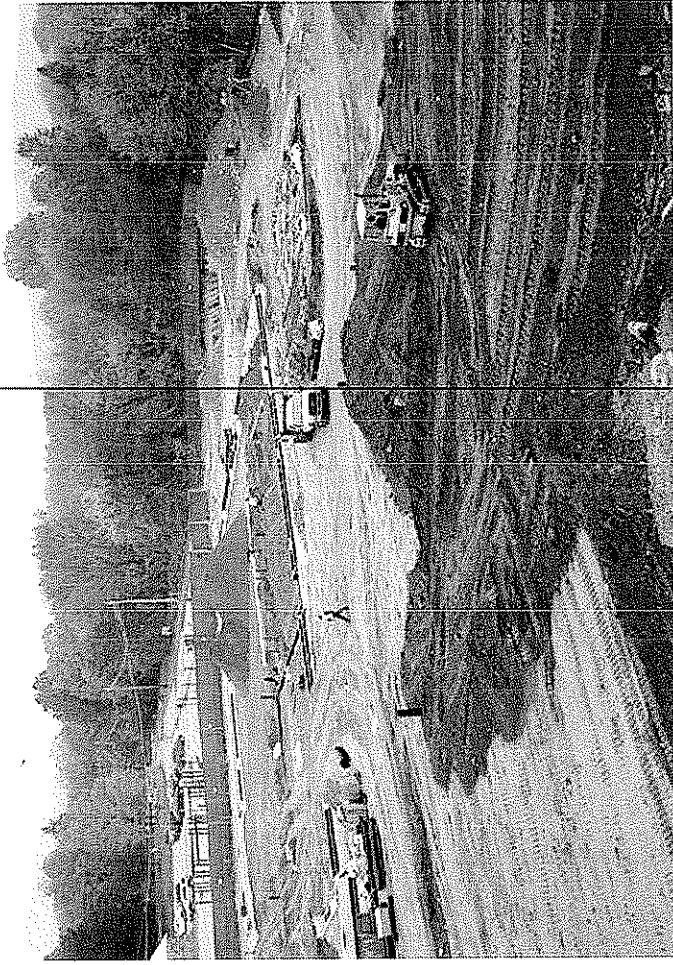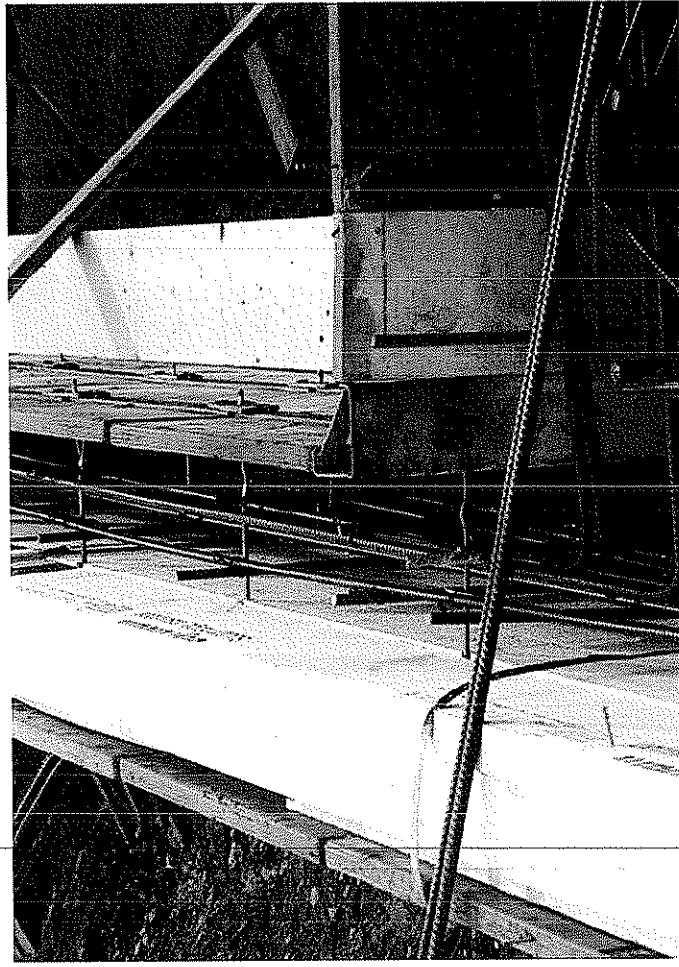

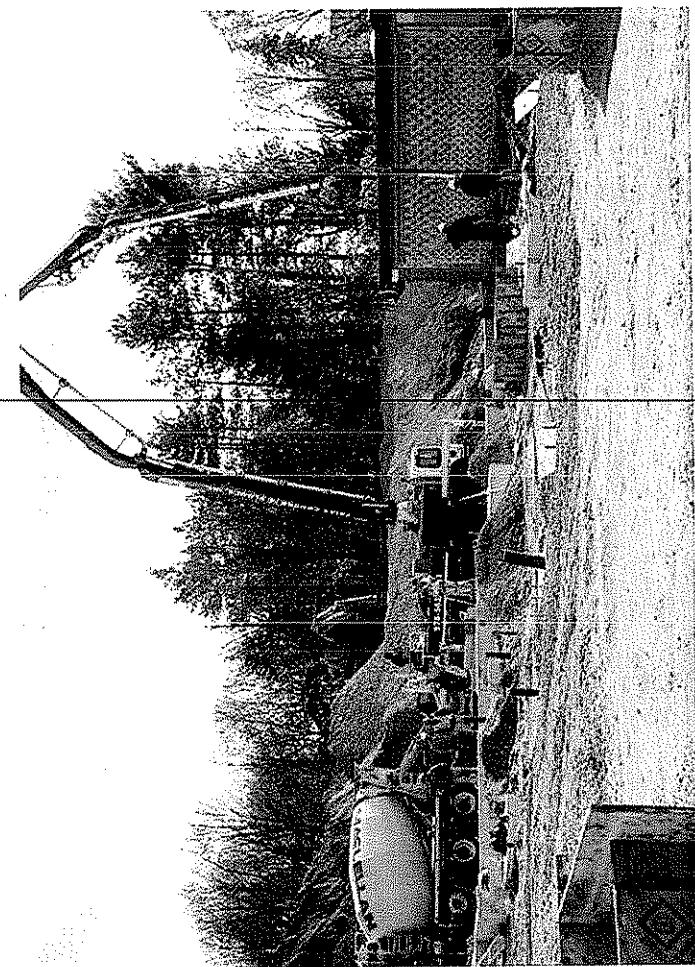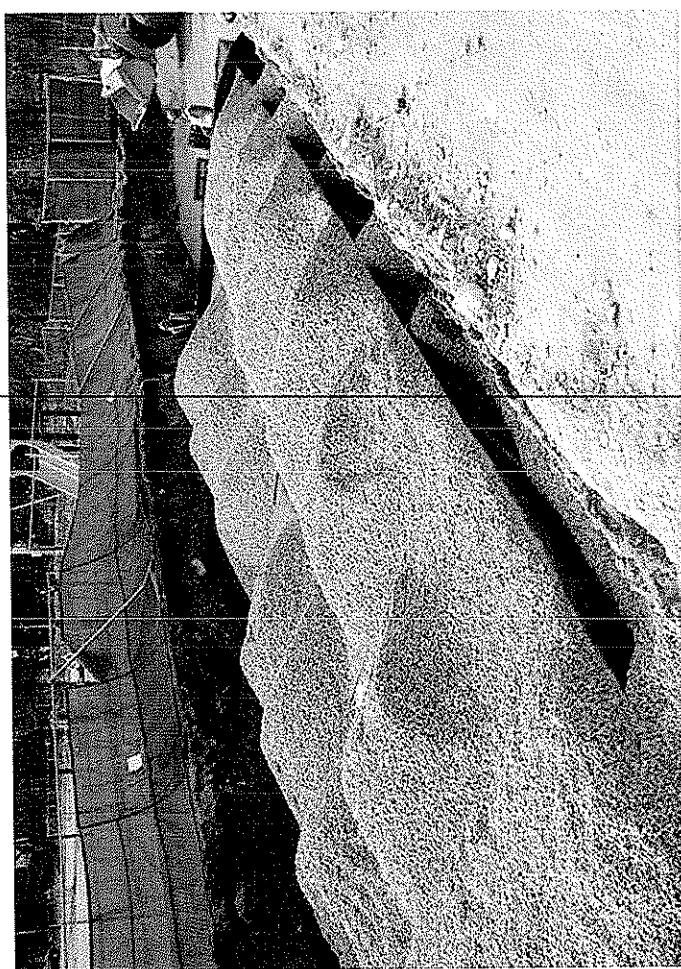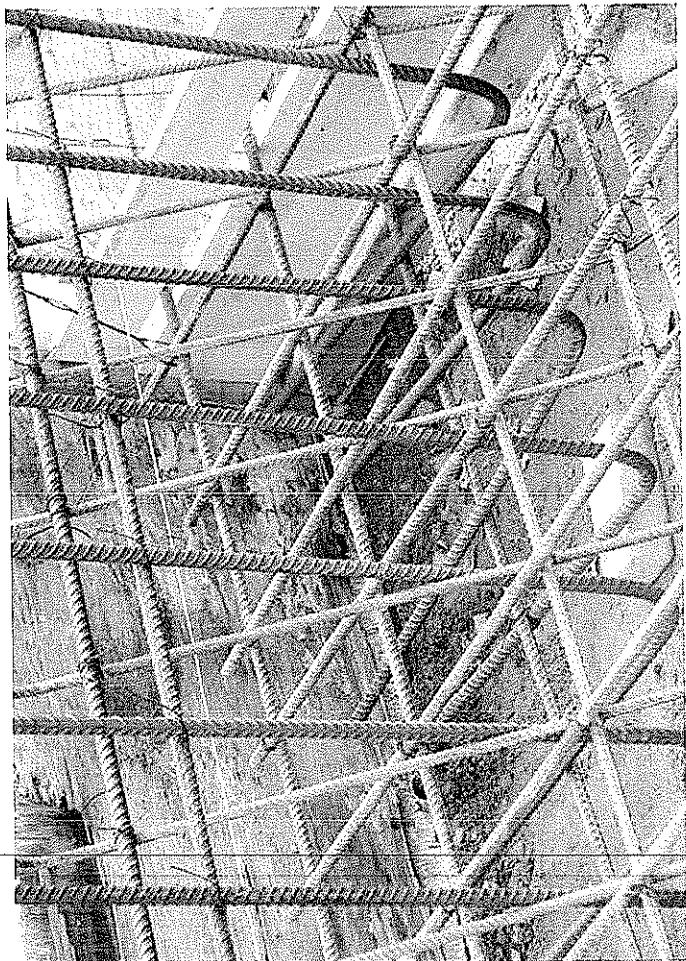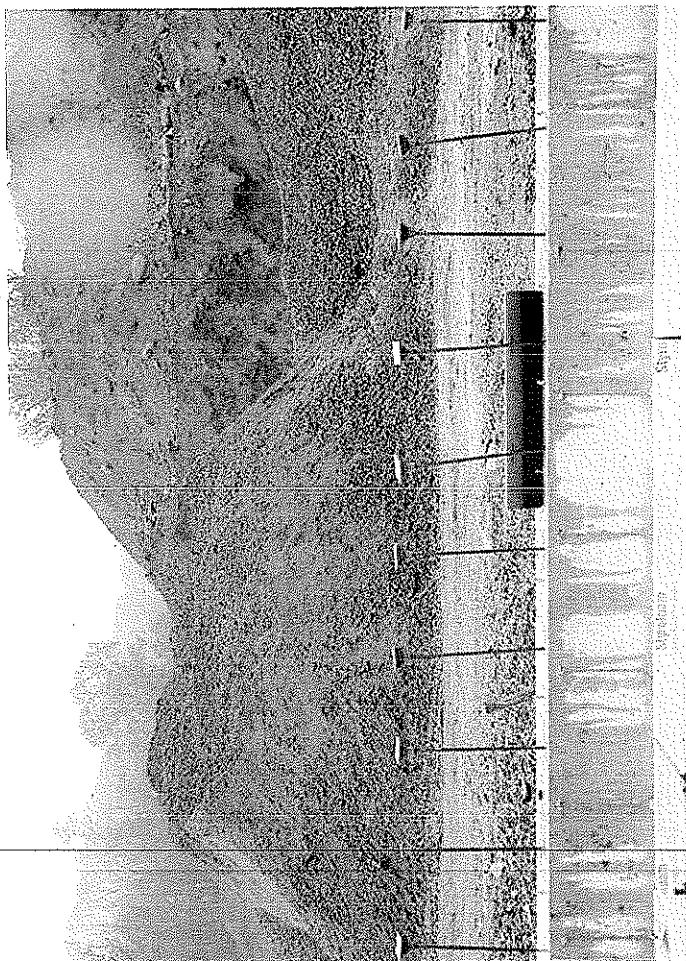

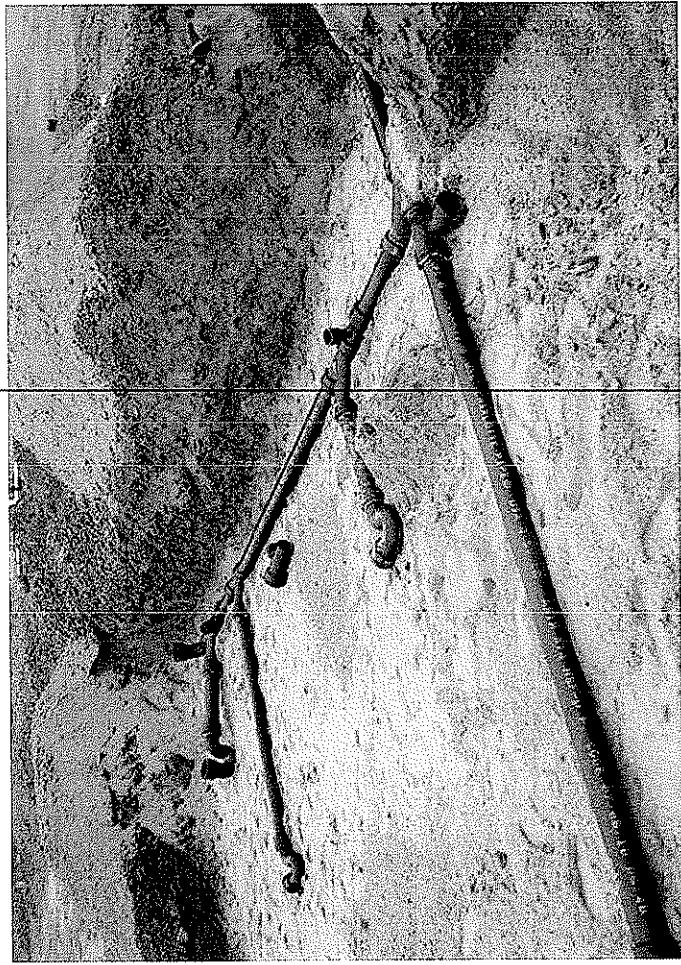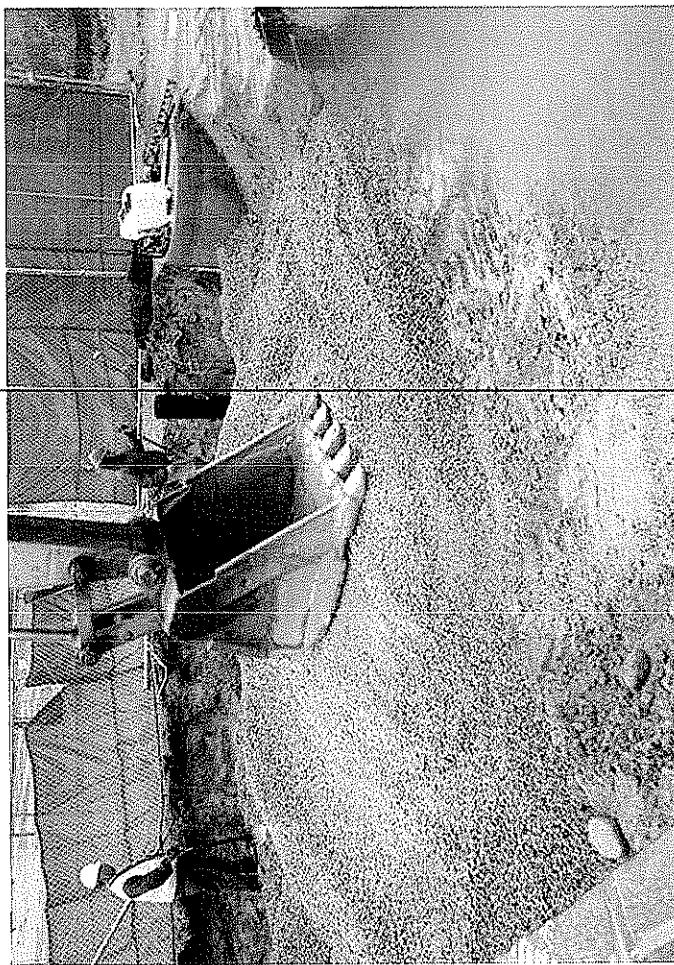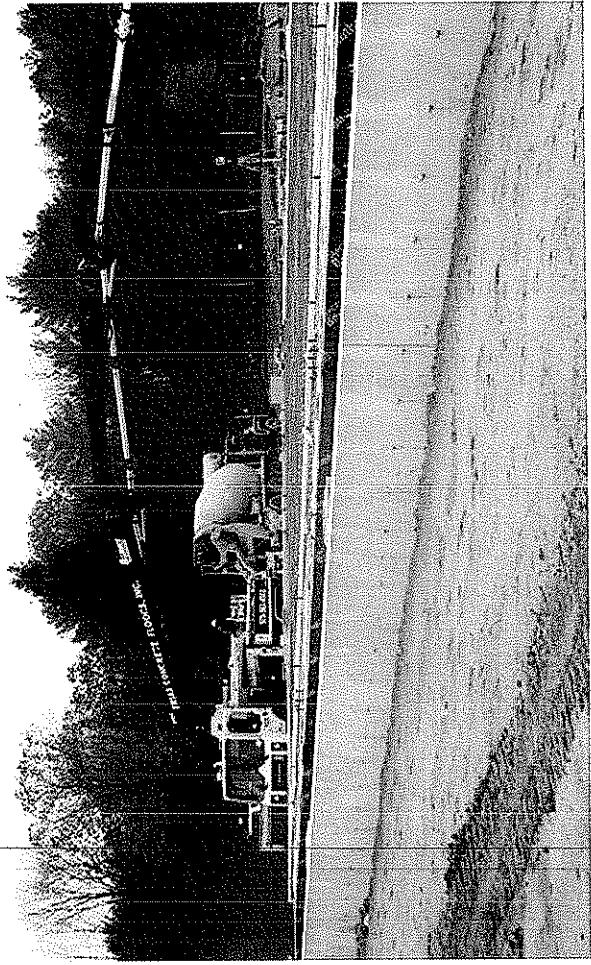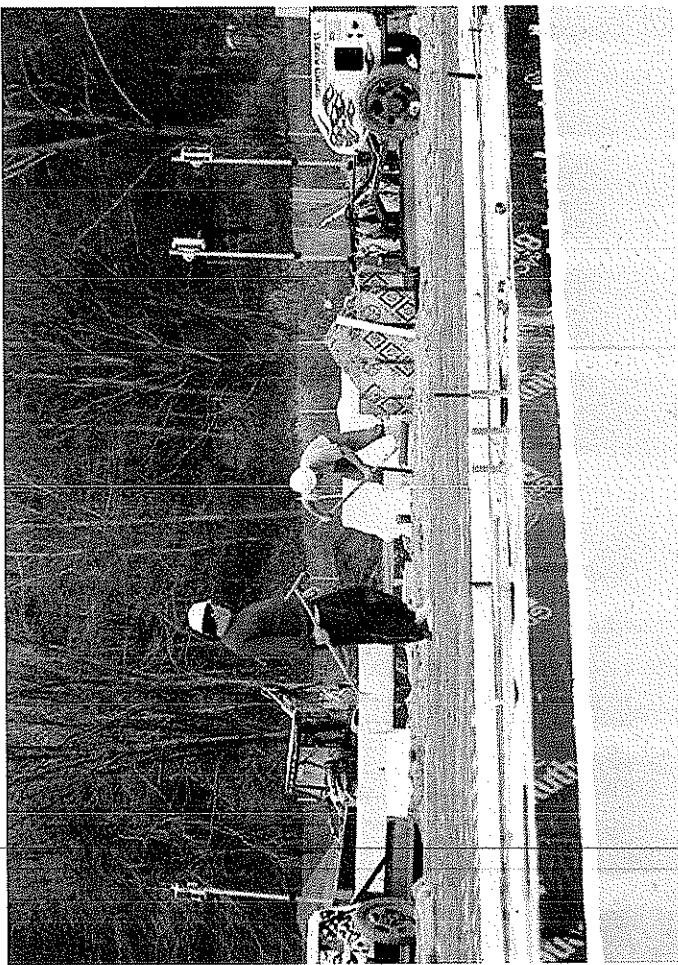

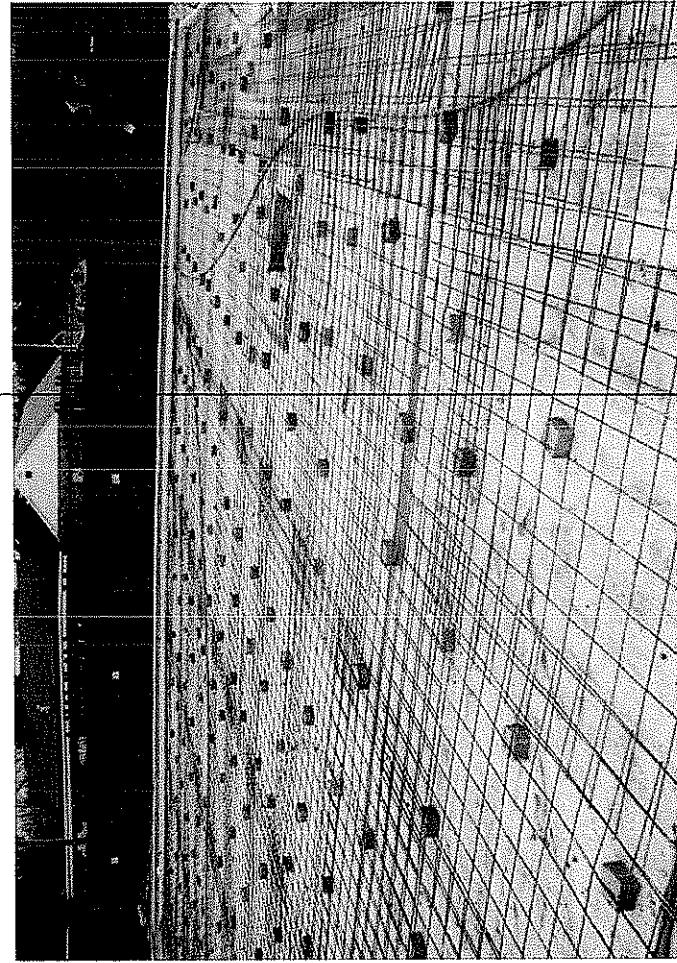



EXHIBIT C**CONTRACTOR PROGRESS PAYMENT REPORT
MINORITY/WOMEN BUSINESS ENTERPRISES PARTICIPATION**Project Number: 09020Project Name: The Pompositicut/Center Elementary SchoolProject Location: Stow, MADate: October 31, 2010Periodical Payment No.: 5General Contractor: P.J. Stella Construction Corp.MBE and/or WBE: A&J Demolition Services Corporation

One copy of this report is to be submitted for each Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) at the time of submitting a request for payment. Copies of the report must be sent to the Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) named above and to the municipalities Affirmative Marketing Construction Officer (AMCO). The AMCO will forward a copy of each Contractor Progress Payment Report to SOMWBA on a quarterly basis.

1. The total price to be paid to the above-named Minority Business Enterprise X and/or Women Business Enterprise X:
\$ 197,663.00

2. The amount remitted to the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under this project: \$ 47,605.50

3. Balance due the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under the above-named project: \$ 150,057.50

4. Comments or explanation of amounts indicated under items 1 and 2 above:

5. We hereby certify that the information supplied herein (including pages attached) is correct and complete.

General Contractor:

(Signed)

President

(Title)

(Date)

Minority and/or Women Business Enterprise

(Signed)

(Title)

(Date)



EXHIBIT C**CONTRACTOR PROGRESS PAYMENT REPORT
MINORITY/WOMEN BUSINESS ENTERPRISES PARTICIPATION**Project Number: 09020Project Name: The Pompositicut/Center Elementary SchoolProject Location: Stow, MADate: October 31, 2010Periodical Payment No.: 5General Contractor: P.J. Stella Construction Corp.MBE and/or WBE: Martin Metro East Insulation Co, Inc.

One copy of this report is to be submitted for each Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) at the time of submitting a request for payment. Copies of the report must be sent to the Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) named above and to the municipalities Affirmative Marketing Construction Officer (AMCO). The AMCO will forward a copy of each Contractor Progress Payment Report to SOMWBA on a quarterly basis.

1. The total price to be paid to the above-named Minority Business Enterprise X and/or Women Business Enterprise _____: \$ 179,300.00
2. The amount remitted to the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under this project: \$ 0.00
3. Balance due the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under the above-named project: \$ 179,300.00
4. Comments or explanation of amounts indicated under items 1 and 2 above: _____

5. We hereby certify that the information supplied herein (including pages attached) is correct and complete.

General Contractor:



(Signed)

(Title)

President

(Date)

11/11/10

Minority and/or Women Business Enterprise

(Signed)

(Title)

(Date)



EXHIBIT C**CONTRACTOR PROGRESS PAYMENT REPORT
MINORITY/WOMEN BUSINESS ENTERPRISES PARTICIPATION**Project Number: 09020Project Name: The Pompositicut/Center Elementary SchoolProject Location: Stow, MADate: October 31, 2010Periodical Payment No.: 5General Contractor: P.J. Stella Construction Corp.MBE and/or WBE: Titan Roofing, Inc.

One copy of this report is to be submitted for each Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) at the time of submitting a request for payment. Copies of the report must be sent to the Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) named above and to the municipalities Affirmative Marketing Construction Officer (AMCO). The AMCO will forward a copy of each Contractor Progress Payment Report to SOMWBA on a quarterly basis.

1. The total price to be paid to the above-named Minority Business Enterprise X and/or Women Business Enterprise _____: \$ 892,600.00
2. The amount remitted to the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under this project: \$ 8,164.30
3. Balance due the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under the above-named project: \$ 884,435.70
4. Comments or explanation of amounts indicated under items 1 and 2 above: _____

5. We hereby certify that the information supplied herein (including pages attached) is correct and complete.

General Contractor:

(Signed)

(Title)

(Date)

Minority and/or Women Business Enterprise

(Signed)

(Title)

(Date)



EXHIBIT C**CONTRACTOR PROGRESS PAYMENT REPORT
MINORITY/WOMEN BUSINESS ENTERPRISES PARTICIPATION**Project Number: 09020Project Name: The Pompositicut/Center Elementary SchoolProject Location: Stow, MADate: October 31, 2010Periodical Payment No.: 5General Contractor: P.J. Stella Construction Corp.MBE and/or WBE: West Floor Covering, Inc.

One copy of this report is to be submitted for each Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) at the time of submitting a request for payment. Copies of the report must be sent to the Minority Business Enterprise (MBE) and/or Women Business Enterprise (WBE) named above and to the municipalities Affirmative Marketing Construction Officer (AMCO). The AMCO will forward a copy of each Contractor Progress Payment Report to SOMWBA on a quarterly basis.

1. The total price to be paid to the above-named Minority Business Enterprise _____ and/or Women Business Enterprise X:
\$ 653,874.00
2. The amount remitted to the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under this project: \$ 8,740.00
3. Balance due the Minority Business Enterprise and/or Women Business Enterprise as of the above date for work performed under the above-named project: \$ 645,134.00
4. Comments or explanation of amounts indicated under items 1 and 2 above:

5. We hereby certify that the information supplied herein (including pages attached) is correct and complete.

General Contractor:

Minority and/or Women Business Enterprise

(Signed)

(Signed)

(Title)

(Title)

(Date)

(Date)

