



*Construction Monitoring Services, Inc.*

## Stow Pompositticut/Center Elementary School

### OPM Monthly Status Report December 2010

*Owner's Representatives  
Project Managers  
Construction Managers*

*Submitted by: Paul Griffin, OPM  
January, 2011*

270 Main Street  
Marlboro, Massachusetts 01752  
Tel: (508) 786-0600  
Fax: (508) 786-0608  
Email: cms@cms-ma.com

# **Monthly Status Report**

## **Pompositticut / Center Elementary School**

### **Stow, MA**

### **December, 2010**

Size: 98,050 SF  
Enrollment: 660 Students  
Reimbursement Rate: 52.11%

#### **Project Team:**

**Owner's Project Manager:** Construction Monitoring Services, Inc.  
Paul Griffin (617) 429-5100  
Neil Joyce (508) 808-1601

**Architect:** Symmes, Maini & McKee  
Phil Poinelli – (617) 547-5400  
Lorraine Finnigan – (617) 547-5400  
Henry Ricciutti – (617) 547-5700

**Project Budget:** \$37,829,870      **Status:** Construction – 16% Complete

#### **Project Status Overview – Work Completed through November, 2010 (OPM 8.1.3.01)**

Project activities previously completed included ongoing construction of building foundation elements, underground building utilities, and sitework / related infrastructure activity.

#### **Project Status Summary – Work Complete through December 30, 2010 (OPM 8.1.3.02)**

During the month of December, major construction activities completed by PJ Stella and their subcontractors included:

- Sitework activities were largely completed for the winter season during November, with site rough-grading, water line installation, and backfill of open trenches in anticipation of the onset of winter conditions.
- Installation of processed gravel, under-slab insulation and vapor barrier along with slab-on-grade construction.
- Completion of retaining wall construction at Hartley Road

- Continuation of under-slab utilities (plumbing, electrical) within the building footprint
- Continuation of application of waterproofing materials to foundation walls
- Construction of Mock-up panel construction, including metal studs, gypsum sheathing and air/vapor barrier.

**Administrative Oversight:** The following is a summary of non-construction related progress (work performed by the OPM / Architect & Design Team) during the month of November, 2010, as well as a forecast of the current administrative schedule through the anticipated end date of the project:

**Contract Administration:** The management team has been continuously involved in project and contract administration including but not limited to submittal review, RFI response and investigation, controlled construction oversight, change order review and overall project controls.

**Future Work Forecast:** It is anticipated the following major construction items will be completed during the forthcoming three-month period (January – March, 2011):

- Mock-up panel construction, including all major building elements
- Completion of foundation elements, including setting of anchor bolts and concrete pier revisions.
- Progression of under-slab utilities, and subsequent placement of slabs on grade (weather dependent)
- Steel erection has been revised to begin in early January, 2011.

#### **Schedule Update (OPM 8.1.3.03)**

The project team is currently working with PJ Stella to complete the review and approval of the overall construction schedule. The November 30, 2010 schedule update notes a three-week impact to the overall construction schedule, due in part to differing site conditions (increased rock quantity). The recovery plan for this work is under review with PJ Stella. A copy of the schedule update has been provided for review.

#### **Financial Update (OPM 8.1.3.04 / 8.1.3.05 / 8.1.3.06)**

The base contract amount for this project is \$23,640,900. Change Orders #1 through #5, amounting to \$65,401 have been issued by the Project. Change Order #6, in the amount of \$67,253, is currently being executed by the Project team. Pending Changes in the estimated amount of \$120,000 have been submitted to the project for consideration, and are under review and negotiation with the Project Team (SMMA, CMS and PJ Stella). The total amount of changes enumerated by PJ Stella to date (both pending and approved) is estimated at \$253,000 or approximately 1% of the overall project budget.

#### **Contractor's Safety Performance (OPM 8.1.3.07)**

With regard to the construction operations underway at the site, CMS is not aware of any lost-time accidents or incidents occurring at the site. CMS will provide updates on these items as soon as they are available.

#### **Designer's QA/QC (OPM 8.1.3.08)**

Construction Monitoring Services has maintained a constructive working relationship with Symmes Maini & McKee throughout the duration of our involvement with the project. We will continue to work in cooperation with SMMA to identify potential issues in the construction documents, and address them prior to their impacting construction operations or progress.

#### **Contractor's Environmental Compliance (OPM 8.1.3.09)**

With regard to environmental compliance of the current construction operations, no report of any environmental abnormalities has been received. Minor site infractions (damaged hay bales, groundwater pumping, etc.) have been remedied by PJ Stella and their site contractor without delay.

#### **Community Issues (OPM 8.1.3.10)**

CMS has been made aware of the following issues regarding project abutters:

- The project has received notification from a small number of abutters, regarding claims of minor damage resulting from vibration associated with blasting and site activity, as well as dust migration from the site. The information included in this claim has been forwarded to the contractor for action.
- The project has received notification of concerns regarding a perceived increase in rodent (mice) activity in properties abutting the site. CMS has confirmed the contractors intent to place pest control measures (bait stations) along the site perimeter to address these concerns.

CMS has been responsive to the abutter's questions and concerns regarding these matters . No other community issues are known at this time.

#### **Designer & Contractor MBE/WBE Activity (OPM 8.1.3.11)**

CMS has provided updated SOMWBA Participation Reports from PJ Stella.

#### **Project Issues and Concerns (OPM 8.1.3.10 / 8.1.3.11)**

The Project Team (SMMA and CMS) had previously identified concerns in the performance of PJ Stella and the concrete subcontractor on the project to date. In response to these concerns, PJ Stella has provided a replacement superintendent, whom started work at the site in late November. Further, they have removed the concrete subcontractor from further participation on the project, and have replaced him with an alternate subcontractor. In observing the contractors operations since these changes, CMS

has observed satisfactory progress during the last month on the remedial work associated with the concrete subcontractor's performance.

The deficiencies and associated repairs have impacted the progress of the work by an estimated 3-4 weeks. The onset of winter weather has provided an additional impact to the scheduled steel erection date, currently forecasted to begin in early January.

The Project Team (CMS, SMMA and PJ Stella) is currently working toward constructive solutions to these issues, and a swift resolution to these matters is anticipated. The project team will continue to look at schedule mitigation measures to minimize these impacts.

Should any further issues arise, CMS will notify the client and the MSBA as soon as practical.

**Total Project Budget**  
**Stow Pompositicut/Center School**

<b>Stow Pompositicut/Center School 1/4/2011</b>							<b>Stow Pompositicut/Center School</b>		
	Pre-Pray Cost Category	Budget	Reallocation	Adjusted Budget	Anticipated	Paid to Date	Balance	% Expended	Ineligible
<b>Administration</b>									
<b>Legal Fees</b>	0101-0000	40,000		40,000	27,053	27,053	-	100.0%	17,723
<b>Owner's Project Manager</b>									
<i>OPM Feasibility Study</i>	0001-0000	40,000		40,000	40,000	40,000	-	100.0%	
<i>Design Development</i>	0102-0400	33,750		33,750	33,750	33,750	-	100.0%	
<i>Construction Contract Documents</i>	0102-0500	55,800		55,800	55,800	55,800	-	100.0%	
<i>Bidding</i>	0102-0600	52,875		52,875	52,875	52,875	-	100.0%	
<i>Construction Contract Administration</i>	0102-0700	583,393		583,393	583,393	164,872	418,521	28.3%	
<i>Closout</i>	0102-0800	83,057		83,057	83,057	83,057	-	0.0%	
<i>Extra Services</i>	0102-0900								
<i>Reimbursable &amp; Other Services</i>	0102-1000	70,000		70,000	70,000	59,200	10,800	84.6%	
<i>Cost Estimates</i>	0102-1100						-		
<i>Other Project Manager Costs</i>	0102-9900	70,000		70,000	47,986	47,986	-	100.0%	
<i>Advertising</i>	0103-0000	2,000		2,000	2,000	2,000	122	1.878	6.1%
<i>Permitting</i>	0104-0000						-		
<i>Owner's Insurance</i>	0105-0000	20,000		20,000	20,000	20,000	60	19,940	0.3%
<i>Other Administrative Costs</i>	0199-0000								
<b>Administration Subtotal</b>		<b>940,875</b>		<b>70,000</b>	<b>1,010,875</b>	<b>988,871</b>	<b>454,675</b>	<b>534,196</b>	<b>117%</b>
<b>Architecture and Engineering</b>									
<b>Basic Services</b>									
<i>Prior Studies</i>	0004-0000	55,200		55,200	55,200	55,200	-	0.0%	
<i>A&amp;E Feasibility Study</i>	0002-0000	490,000		490,000	490,000	490,000	(92,500)	118.9%	37,300
<i>Design Development</i>	0201-0400	506,300		506,300	506,300	506,300	(55,700)	111.0%	
<i>Construction Contract Documents</i>	0201-0500	1,054,000		1,054,000	1,054,000	1,054,000	(40,000)	103.8%	
<i>Bidding</i>	0201-0600	85,000		85,000	85,000	85,000	-	100.0%	
<i>Construction Contract Administration</i>	0201-0700	798,000		798,000	798,000	798,000	160,000	638,000	20.1%
<i>Closout</i>	0201-0800						-		
<i>Other Basic Services</i>	0201-9900								
<b>Reimbursable Services</b>									
<i>Construction Testing</i>	0203-0100	50,000		50,000	50,000	50,000	50,000	100.0%	
<i>Printing (over minimum)</i>	0203-0200	70,000		70,000	-	-	-		
<i>Other Reimbursable Costs</i>	0203-9900	82,700		82,700	98,282	85,554	12,728	87.0%	20,260
<i>Hazardous Materials</i>	0204-0200	40,000		40,000	40,000	40,000	40,000	0.0%	
<i>Geotech &amp; Geo-Env.</i>	0204-0300	115,000		115,000	(21,381)	93,609	93,609	0.0%	
<i>Site Survey</i>	0204-0400						-		
<i>Wetlands</i>	0204-0500						-		
<i>Traffic Studies</i>	0204-1200						-		
<b>Architectural/Engineering Subtotal</b>		<b>3,346,200</b>		<b>(51,418)</b>	<b>3,291,782</b>	<b>3,305,374</b>	<b>2,604,037</b>	<b>666,37</b>	<b>78.8%</b>
									<b>57,560</b>

**Total Project Budget**  
**Stow Pompositicut/Center School**

<b>Stow Pompositicut/Center School 1/4/2011</b>						
	Proj/Pay Cost Category	Budget	Reallocation	Adjusted Budget	Anticipated	Paid to Date
						Balance
<b>Construction</b>						
Construction Contract		28,841,856		23,640,900	3,358,447	20,282,453
Change Orders				65,401	65,401	14.2%
Outstanding -Liability				146,522	146,522	
	<b>Construction Subtotal</b>	<b>0502-00001</b>	<b>28,841,856</b>	<b>(5,200,956)</b>	<b>23,852,823</b>	<b>3,358,447</b>
Const. Contingency		0507-0000	2,163,139	211,923	1,951,216	
	<b>Construction Total</b>			<b>25,804,039</b>	<b>23,933,944</b>	<b>3,358,447</b>
						20,282,453
						14.0%
						89,126
<b>Miscellaneous Project Costs</b>						
Utility company fees		0601-0000				-
Testing Services		0602-0000				-
Swing Space/Modular's		0603-0000				-
Other Project Costs (Mailing & Moving)		0699-0000	50,000.0	50,000.0	3,514.0	3,514.0
	<b>Misc. Project Costs Subtotal</b>			<b>50,000.0</b>	<b>3,514.0</b>	<b>3,514.0</b>
						-
						100.0%
<b>Furnishings and Equipment</b>						
<i>Furnishings</i>		0701-0000	720,000	720,000		720,000
<i>Equipment</i>		0702-00000	20,000	20,000		20,000
<i>Computer Equipment</i>		0703-00000	1,047,700	1,047,700		1,047,700
	<b>FF&amp;E Subtotal</b>			<b>1,787,700</b>	<b>1,787,700</b>	<b>-</b>
Owner's Contingency		0801-00000	\$620,100	\$644,518		
	<b>Total Project Budget</b>			<b>37,789,870</b>	<b>15,582</b>	<b>32,628,914</b>
					<b>30,046,456</b>	<b>6,447,726</b>
						<b>23,250,486</b>
						<b>21.5%</b>
						<b>164,409</b>

**Construction Contingency**

Item	Amount	Date	Balance	Comments
Starting Balance			2,163,139	
CO 2	14,085	8/1/2010	2,149,054	
CO 3	3,766	10/14/2010	2,145,288	
CO 4	6,476	11/4/2010	2,138,812	
CO 5	41,074	11/4/2010	2,097,738	
<b>Total</b>	<b>65,401</b>			

Owner's Contingency					
Item	Vendor	Amount	Date	Balance	Comments
Starting Balance				620,100	
PFA Adjustment		(40,000.00)		660,100	
MHC Support	SMMA	15,581.66	7/20/2010	644,518	Stone Building
<b>Total</b>		<b>15,581.66</b>			

**Transfers**

Item	Amount	From Line	To Line	Date	Comments
Printing	70,000	0203-0200	0102-9900		Reallocation
Reimbursable	15,582	0801-0000	0203-9900		Owner's Contingency
A&E Feasibility	92,500	0002-0000			
Design Developmer	55,700	0201-0400			
Construction Doc's	40,000	0201-0500			
<b>Total</b>	<b>273,782</b>				



<b>Outstanding - Liability</b>			
<b>Item</b>	<b>Reference</b>	<b>Amount</b>	<b>Comments</b>
Anesse Electric Service Pipe	PCO 19	3,845.00	
Stella Open Rock	PCO 7	99,776.00	
Oetaining wall expansion joint	PCO 18	639.00	
Asbestos Tile/carpet	Claim	3,000.00	Protest
Fire Dumpster	CCD 4	1,000.00	
Asbestos Pipe	PCO 11	10,000.00	
Roof Opening	PCO 13	1,061.00	
Roof Drain Pipe	PCO 15	3,079.00	
Transformer Pad	PR 5	1,000.00	
Roof openings	PCO 13	1,061.00	
Gas Pit	PCO 20	4,365.00	
Motorized Shades	PR 13	6,651.00	
Site Entrance sign	PR 14	2,000.00	
Turf & Grass Revisions	PR 15		
Structural Changes	PR 2	4,771.00	
Plumbing Changes SKP 06	PR 3	1,000.00	
Ceiling Changes SKA66	PR 8	274.00	
Fireproofing Changes		3,000.00	
<b>Total</b>		<b>146,522.00</b>	

CMS Amendments		
Item	Amount	Paid From
Structural Peer Review	6/4/2010 4,400.00	Reimbursable 0102-1000
ProjectDog Printing	6/4/2010 47,996.25	Printing 0203-0200
T&L Floor Testing	6/4/2010 2,058.10	Reimbursable 0102-1000
Cost Estimates	8/4/2010 59,200.00	Reimbursable 0102-1000
113,654.35		

SMMA Amendments			
Item		Amount	Paid From
Permitting	7/12/2010	75,000.00	Reimbursables 0203-9900
MA-CHPS Registration	7/12/2010	7,600.00	Reimbursables 0203-9901
MHC Support	7/12/2010	15,581.66	Owner's Contingency
Hazmat Observation	7/12/2010	27,900.00	Hazmat 0204-0200
Geotechnical Observation	7/12/2010	45,000.00	Geotech 0204-0300
Testing & Inspection	7/12/2010	50,000.00	Transfer 0204-0300
Geotechnical Observation	10/12/2010	16,000.00	Geotech 0204-0300
237,081.66			

# C M S

## Change Order Detail Log

### Stow Center Elementary School

Change Order #1		Owner	Unforeseen	Requested by	Insufficient
POO#	Description	Condition	Inspector	Design	Error
	Contract changes	\$0.00			
<hr/>					
Change Order #2 - Approved		Owner	Unknown		
POO#	Description	Condition	Omission		Error
00001.2	Wetland Flagging - Hay Bales	\$98.00			
00003.2	Existing fire dumpster	\$13,100.00			
Change Order #3		Owner	Unknown		
POO#	Description	Condition	Omission		Error
2.2	Primary electric riser conduit	\$1,772.00			
9	Electrical panel at existing building	\$1,994.00			
Change Order #4		Owner	Unknown		
POO#	Description	Condition	Omission		Error
5	Increase flood and earthquake limits	\$5,299.00			
12	Provide 4 x 8 gate temporary construction fence	\$1,177.00			
Change Order #5		Owner	Unknown		
POO#	Description	Condition	Omission		Error
<hr/>					



# C M S

## Consolidated CO Log

### Stow Center Elementary School

<u>PCO</u>	<u>Description</u>	<u>Date</u>	<u>CCD</u>	<u>PR</u>	<u>Proposed</u>	<u>Approved</u>	<u>CO#</u>	<u>Outstanding Liability</u>
00001	Wetland Flagging - Hay Bales	7/15/2010		1	\$985.00	\$985.00	2	
00001.2	Wetland Flagging - Hay Bales	7/16/2010		1	\$985.00	\$985.00	2	
00002	Primary electric riser conduit	8/9/2010		4	\$1,772.00		3	
00002.2	Primary electric riser conduit	9/23/2010		4	\$1,772.00		3	
00003	Existing fire dumpster	8/20/2010	002R1					
00003.2	Existing fire dumpster	8/27/2010	002R1		\$13,100.00	\$13,100.00	2	
00004	Architectural/structural modifications	8/22/2010		2	\$4,771.00		X	
00005	Builders risk insurance	8/23/2010			\$35,299.00		4	
00006	Wetland Mitigation	8/25/2010					5	
00006.2	Wetland Mitigation	8/28/2010					5	
00006.3	Wetland Mitigation	9/13/2010					5	
00006.4	Wetland Mitigation	9/28/2010		6	\$41,074.00		5	
00007	Rock removal	8/30/2010			\$99,776.00		X	
00007.2	Rock removal - open	12/22/2010			\$154,797.00			
00008	Ceiling revisions	9/7/2010						
00008.2	Ceiling revisions	12/8/2010		8	(\$475.00)		X	
00009	Electric panel at existing building	9/17/2010	001R1					
000010	Concrete for fire pump pit	10/11/2010			\$1,994.00		3	
000011	Asbestos cement pipe	10/19/2010	3		\$2,050.00		6	
000012	Temporary construction gate	11/1/2010			\$11,002.00		X	
000013	Roof opening revisions	11/1/2010			\$11,177.00		4	
000014	Asbestos cement pipe	11/3/2010			\$11,061.00		X	
000015	Roof drain piping	11/12/2010		3	\$29,411.00		6	
000015R2	Roof draining piping	11/12/2010		3	\$2,181.80		X	
000016	Doors C264 & EX302	11/18/2010		7			6	
000017	Stair C122 opening	11/19/2010		10	\$26,855.00			
000017.2	Stair C122 opening	11/22/2010		10	\$639.00		6	
000018	Retraining wall expansion joint detail	12/7/2010						
000019	Primary electric duct bank conduit	12/8/2010			\$3,845.00			
000020	Gas service pit	12/8/2010		12	\$4,365.00			

<u>PCO</u>	<u>Description</u>	<u>Date</u>	<u>CCD</u>	<u>PR</u>	<u>Proposed</u>	<u>Approved</u>	<u>CO#</u>	<u>Liability</u>	<u>Outstanding</u>
000021	Motorized shades scope clarification	12/8/2010		13	\$6,651.00				
000022	Rock removal - trench	12/22/2010			\$6,684.00				
000023	Transformer pad	12/30/2010			\$7,372.00				
	Dispose at dumpster	8/30/2010	4						
	Provide site work modifications	10/6/2010	5	6	\$41,074.00				5
	Delete work associated with transformer pad	8/6/2010		5					
	Cost for fireproofing revisions	8/31/2010		11					
	Cost to revise site entry sign	10/18/2010		14					
	Seeding application	10/22/2010		15					
	Revisions to Door B132	11/19/2010		16					
	Pipe tap & gate valve off of new water line	12/10/2010		18					

Nashoba Pompo/Center School Project  
Cash Flow Projections


	Paid to Date	Jan-09	Feb-09	Mar-09	Apr-09	May-09	Jun-09	Jul-09	Aug-09	Sep-09	Oct-09	Nov-09	Dec-09	Total
<b>Construction</b>														
<b>Fee's</b>	Architect													
	A&E additional Project Manager													
	Other													
<b>FFE &amp; Tech</b>														
<b>Misc</b>														
<b>Monthly Total</b>														
	Prior Year Total	Jan-10	Feb-10	Mar-10	Apr-10	May-10	Jun-10	Jul-10	Aug-10	Sep-10	Oct-10	Nov-10	Dec-10	Total
<b>Construction</b>														
<b>Fee's</b>	Architect	750,110	199,462	200,000	250,000	250,000	250,000	108,250	33,250	33,250	150,000	800,000	900,000	3,250,000
	A&E additional Project Manager	92,500						22,000	22,000	25,600	25,600	25,600	25,600	450,000
	Project Manager PM additional	55,000	18,750	22,000	32,000	32,000	32,000	25,600	25,600	25,600	25,600	25,600	25,600	360,950
	Other	9,400	15,800	17,000	17,000									59,200
		394												394
<b>FFE &amp; Tech</b>														
<b>Misc</b>														
<b>Monthly Total</b>														
	Prior Year Total	Jan-11	Feb-11	Mar-11	Apr-11	May-11	Jun-11	Jul-11	Aug-11	Sep-11	Oct-11	Nov-11	Dec-11	Total
<b>Construction</b>														
<b>Fee's</b>	Architect	3,250,000	1,182,045	945,638	1,418,454	1,654,863	1,891,272	2,127,681	1,634,863	1,418,454	1,182,045	945,638	945,638	19,562,223
	A&E additional Project Manager	450,000	150,000	150,000	150,000	150,000	150,000	150,000	150,000	150,000	150,000	150,000	150,000	2,100,000
	Project Manager PM additional	136,500												
	Other	360,950	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	2,823,073
		59,200												179,500
		394												668,150
<b>FFE &amp; Tech</b>														
<b>Misc</b>														
<b>Monthly Total</b>														
	Prior Year Total	Jan-12	Feb-12	Mar-12	Apr-12	May-12	Jun-12	Jul-12	Aug-12	Sep-12	Oct-12	Nov-12	Dec-12	Total
<b>Construction</b>														
<b>Fee's</b>	Architect	19,562,223	709,227	600,000	472,818	591,022	472,818	354,613	200,000	57,000	21,179			23,640,900
	A&E additional Project Manager	2,100,000	63,139											2,163,139
	Project Manager PM additional	179,500	22,000	33,250	33,250	33,250	33,250	33,250	33,250	33,250	33,250	33,250	33,250	3,031,000
	Other	668,150	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	25,600	276,722
		59,200												848,875
		96,394	10,000	10,000	10,000	10,000	10,000	10,000	10,000	10,000	10,000	10,000	10,000	70,000
<b>FFE &amp; Tech</b>														
<b>Misc</b>														
<b>Monthly Total</b>														
	Prior Year Total	881,216	686,850	708,850	541,668	681,872	1,047,710	519,338	220,549	67,000	31,179	36,100	5,160,462	37,789,870

**Pompo/Center Elementary School  
Stow, MA**

Forwarded to Architect/Owner:  
September 21, 2010  
Page 1A of 23A


**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4		
ST02X	Anchor Bolt Layout Drawings	10	10																
FN20X	Concrete Accessories Submittals	15	15																
ST03X	Steel RFI/Clarifications	45	45																
SW20X	Cutting Submittals	20	20																
PL30X	Plumbing Rough Submittals	10	10																
SW10X	Topsoil Samples	20	20																
SF01X	Fireproofing Submittals	25	25																
PL70X	Plumbing Finish Submittals	20	20																
LV01X	Louver Submittals	30	30																
WP20X	Joint Sealers Submittals	20	20																
GL01X	Glazing & Mirror Submittals	30	30																
SK30X	Skylight Submittals	25	25																
ST04X	Steel Shop Drawings	40	40																
ST05X	Steel Joist Shop Drawings	15	15																
ST06X	Steel Deck Shop Drawings	15	15																
EV01X	Elevator Submittals	15	15																
HV10X	HVAC Rooftop Equipment Submittals	15	15																
HV20X	HVAC Rough Submittals	15	15																
HV60X	HVAC Boiler Room Submittals	20	20																
HV70X	HVAC Finish Submittals	20	20																
KN01X	Food Service Rough-in Submittals	15	15																
MM02X	Steel Stair Submittals	30	30																
WF01X	Wood Flooring Submittals	15	15																
EL20X	Electrical Rough Submittals	15	15																
HV90X	MEP Coordination Drawings	70	70																
KN02X	Food Service Remaining Submittals	20	20																
SW21X	Paving Mix Submittals	10	10																
AB10X	Air/Vapor Barrier Submittals	20	20																
RC02X	Wood Truss Submittals	15	15																
WN01X	Aluminum Window/CW/SF Submittals	30	30																
WN02X	Aluminum Entrances Submittals	30	30																
WN10X	Wood Window Submittals	20	20																
FP01X	Fire Protection Submittals	20	20																
MC01X	Masonry Materials Submittals	20	20																
MV01X	Masonry Veneer Submittals	20	20																
DW10X	Exterior Stud Framing Mat's Submittals	20	20																
DW11X	Exterior Stud Framing Shop Drawings	20	20																
FC01X	Finish Carpentry Submittals	25	25																
RF01X	Roofing Submittals	20	20																

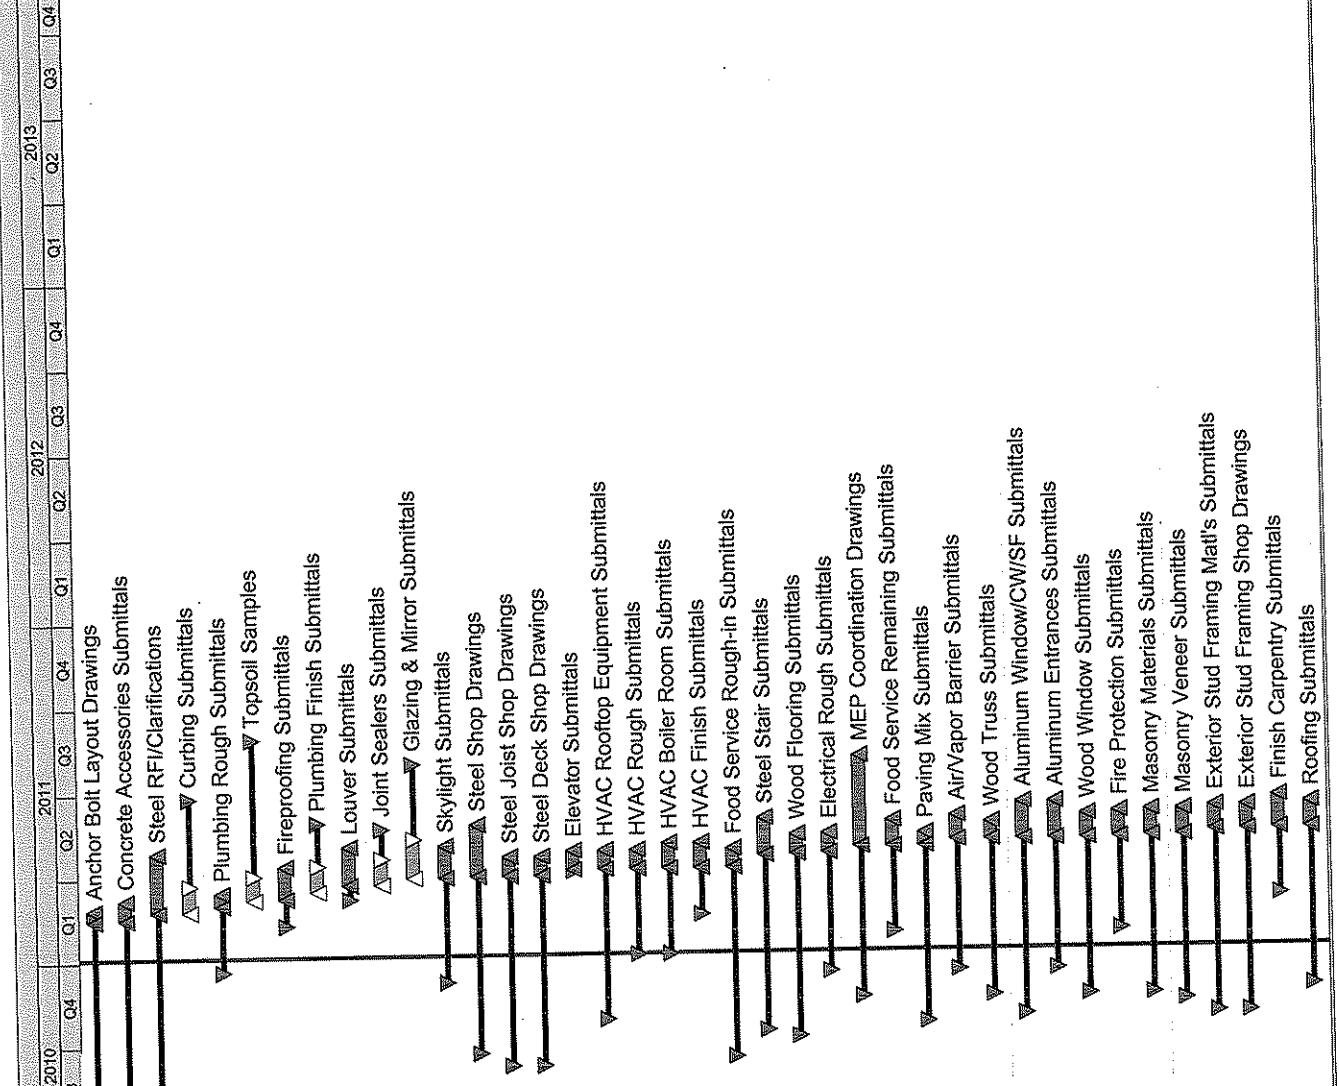

**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
RF20X	Roofing Accessories Submittals	15	15																
SW22X	Paint Striping Submittals	15	15																
EL70X	Electrical Finish Submittals	20	20																
EL71X	F/A & Telecommunication Submittals	20	20																
ST10X	Steel Pre-Installation Conference	0	0																
DW20X	Drywall Submittals	20	20																
RC01X	Rough Carpentry Submittals	20	20																
FC10X	Wood & Stile Door Submittals	25	25																
FC11X	Door Hardware Submittals	25	25																
HV91X	HVAC Layout Drawings	50	50																
OP01X	Operable Partition Submittals	20	20																
RC10X	HM Door & Frame Submittals	25	25																
EJ01X	Expansion Control Submittals	20	20																
AB11X	Air/Vapor Barrier Conference	0	0																
MM03X	Misc. Metals Submittals	40	40																
FP02X	Fire Protection Layout Drawings	30	30																
OH01X	Sectional Door Submittals	25	25																
MP01X	Composite Panel System Submittals	30	30																
CW01X	Fixed Casework Submittals	30	30																
RF10X	Pre-Roofing Conference	0	0																
CL01X	Acoustical Ceiling Submittals	30	30																
CT01X	Tiling Submittals	30	30																
DW30X	Insulation Submittals	15	15																
FM01X	Floor Moisture Mitigation Subm	20	20																
RS01X	Resilient Flooring Submittals	30	30																
BL01X	Bleachers Submittals	30	30																
LK01X	Locker Submittals	30	30																
MS10X	Misc. Specialties Submittals	30	30																
MS50X	Projections Screens Submittals	30	30																
SW52X	Site Improvement, etc. Submittals	25	25																
SW53X	Outdoor Seating Submittals	25	25																
SW55X	Play Equipment Submittals	25	25																
TA01X	Toilet Accessories Submittals	30	30																
TP01X	Toilet Compartment Submittals	30	30																
MV03X	Masonry Pre-Installation Conference	0	0																
EM01X	Foot Grilles/Entrance Mats Submittals	30	30																
MS40X	Residential Appliances Submittals	30	30																
PA01X	Painting Submittals	30	30																
MP02X	Metal Wall Panel Submittals	20	20																

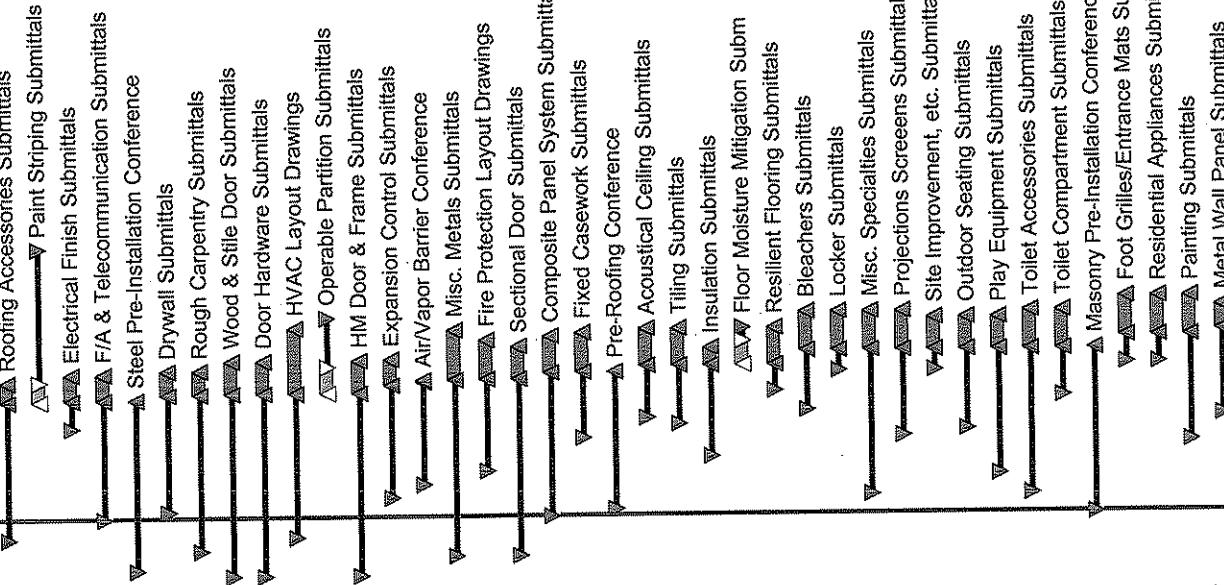

**Pompo/Center Elementary School  
Stow, MA**

Forwarded to Architect/Owner:  
September 21, 2010  
Page 4A of 23A


Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 5A of 23A

**Pompo/Center Elementary School  
Stow, MA**

**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
SW1220	Patch Utility Trenching	5	5																
SW1330	Remove Existing Drainage	5	5																
SW1340	Building Cuts & Fills, East	10	10																
SW1410	Initial Rough Grade Entry Road	5	5																
SW1350	Sewer Temporary Force Main	5	5																
SW1420	Cuts and Fills Roadway	10	10																
SW1430	Cuts and Fills, Northeast Parking	5	5																
SW1510	Excavate Site Conc. Retaining Wall	10	10																
FN50S	Site Concrete Retaining Wall	10	10																
EL11SW	Electric UG under Roadway	5	5																
SW1520	Backfill Site Conc. Retaining Wall	5	5																
EL10SW	UG Site Electric to Bldg	5	5																
SW1360	Rough Grade Around Building	5	5																
SW1440	Prepare Storage Staging Area	5	5																
FN500	Concrete Bench Wall	5	5																
EL50SW	Set Transformer	5	5																
EL51SW	Set Emergency Generator	5	5																
EL90SW	Test and Inspect Emergency Generator	5	5																
<b>Sitework: Utilities, Roadways, Paving</b>																			
SW2210	Gas Service to Phase 1	15	15																
SW2310	Set DMH1-5, DMH1-6 at South, Building	5	5																
SW2312	New Drain Line at South, Building	3	3																
SW2314	Temporary Drain Line at South, Building	3	3																
SW2410	Drainage at Roadway	10	10																
SW2316	Drainage at Building Area	20	20																
SW2412	Grade Northeast Parking	5	5																
SW2414	Force Main at Roadway	10	10																
SW2416	Under Drain at Northeast Parking	5	5																
SW2418	Water Mains at Roadway	10	10																
SW2430	New Sanitary System	25	25																
SW2420	Gravel and Finish Grade, NE Parking	5	5																
SW2318	Infiltration Area 1	10	10																
SW2422	Rough Grade Roadway - Partial	5	5																
SW2424	Excavate Electric under Roadway	3	3																
SW2426	Backfill Electric under Roadway	2	2																
SW2428	Gravel and Finish Grade Roadway - Partial	5	5																
SW2320	Site Roof Drain Piping	5	5																
SW2322	Water Mains at Building Area, Partial	10	10																

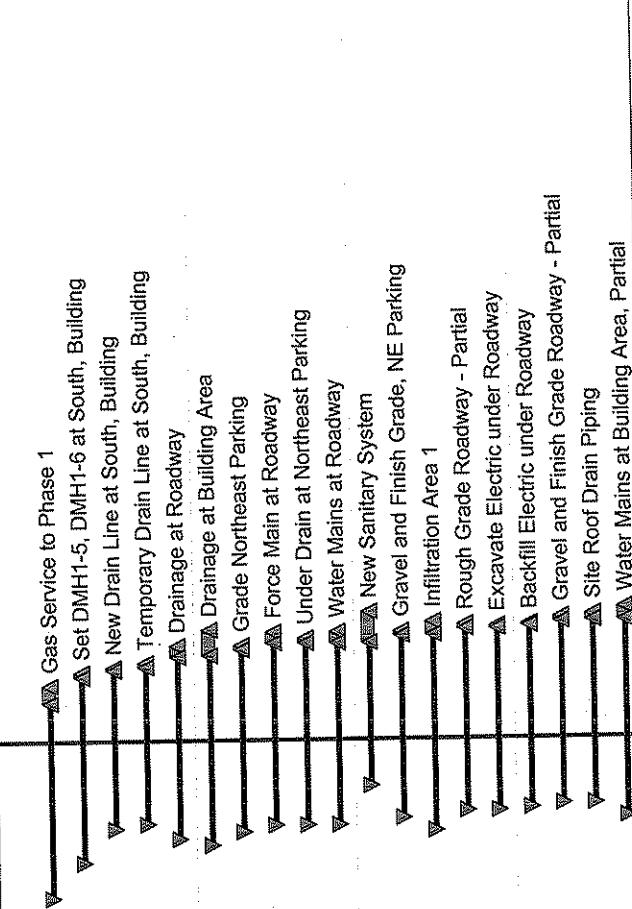

**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4		Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
SW2328	Infiltration Area 2	10	10																
SW2510	Leaching Field - Partial	10	10																
SW2432	Paving Binder, NE Parking and Partial Road	5	5																
SW2326	Excavate Site UG Electric to Building	5	5																
SW2434	Rough Grade Roadway - Complete	5	5																
SW2436	Test, Inspect, Approve New Sanitary	5	5																
SW2512	Grade Leaching Area - Partial	5	5																
SW2330	Backfill UG Site Electric to Building	2	2																
SW2438	Remove Existing Sanitary System	8	8																
SW2324	Infiltration Area 3	10	10																
SW2514	Remove Existing Leaching Field	10	10																
SW2332	Ex/Sel/Bckfl Fire Suppression Tanks	5	5																
SW2334	Water/Fire Piping at Fire Supp Tanks	5	5																
SW2516	Leaching Field - Complete	15	15																
SW2336	Well Water Piping	5	5																
SW2338	Test & Chlorinate Water System	5	5																
SW2340	Complete Gas Service to Building	5	5																
SW2342	Excavate/Prep Transf, Gen, Gas Pads	5	5																
SW2344	Form/Pour/Strip Conc Trnf, Gen, Gas	5	5																
SW2346	Backfill Transf, Gen, Gas Pads	5	5																
EL13SW	UG Site Lighting, Building	10	10																
SW2348	Grade Fire Lane/Service, Building	10	10																
SW2350	E/B Site Lighting, Building	10	10																
SW2352	Under Drain at Fire Lane, Building	5	5																
SW2354	Complete Rims, Inverts, Misc. Utilities, Bldg	10	10																
SW2440	Gravel and FG Roadway - Complete	5	5																
SW2442	Paving Binder Complete, Roadway	5	5																
SW2444	Light Pole Bases	10	10																
EL14SW	UG Site Lighting, Parking and Roadway	10	10																
SW2446	E/B Site Lighting, Parking and Roadway	10	10																
SW2448	Curbing, Parking and Roadway	15	15																
SW2356	Prep and FG Fire Lane/Service at Building	10	10																
SW2450	Complete Rims, Inverts, Misc. Utilities,	10	10																
SW2358	Finish Pave Fire Lane/Service at Building	5	5																
SW2452	Prep and Finish Paving, Roadway/Parking	5	5																
<b>Foundations and Structure</b>																			
SW331SB	Excavate Found, Storage Bldg	5	5																
FN10SB	Foundations, Storage Bldg	10	10																

▲ Excavate Found, Storage Bldg  
▲ Foundations, Storage Bldg



Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 10A of 23A

Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 11A of 23A

Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 12A of 23A


Pompo/Center Elementary School  
Stow, MA

Sorted by Division, Trade

Forwarded to Architect/Owner:  
September 21, 2010  
Page 13A of 23A

**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
EL517	Electric Connections at Mech Equipment	15	15																
HV617	Breaching and Chimney Flue	10	10																
PL627	Plumbing - Gas Piping, Mech/Elect	10	10																
HV627	Complete HVAC at Boiler & Mech Room	20	20																
PL309	Plumbing - Gas Piping to Roof Units	5	5																
PL324	Plumbing - Gas Piping, Kitch	5	5																
<b>Interior Finishes</b>																			
MM207	Roof Access Treads, Mech	5	5																
DW303	Drywall, Tape & Sand, Gym/Café	25	25																
DW305	Drywall, Tape & Sand, Media/Art	20	20																
KN104	Set Cooler/Freezer, Kitch	10	10																
PA103	Prime Paint, Gym/Café	15	15																
ELL907	Activate Permanent Power	15	15																
AP103	Sound Wall Panels, Gym/Cafe	10	10																
FS103	Firestopping, Gym/Café	10	10																
PA105	Prime Paint, Media/Art	15	15																
CL103	Ceiling Grid, Gym/Café	15	15																
DW304	Drywall, Tape & Sand, Kitch	10	10																
DW306	Drywall, Tape & Sand, Lobby/Admin	15	15																
DW403	Touch-up Drywall, Gym/Café	10	10																
FS105	Firestopping, Media/Art	15	15																
HV703	HVAC Radiation, Gym/Café	15	15																
MM103	Unistrut Proj. Support, Gym/Cafe	5	5																
WP203	Interior Caulking, Gym/Café	10	10																
FC103	Finish Millwork, Panelling, Gym/Cafe	30	30																
GL105	Ceiling Grid, Media/Art	15	15																
CT105	Ceramic Tile Toilets, Media/Art	15	15																
DW405	Touch-up Drywall, Media/Art	10	10																
FS104	Firestopping, Kitch	10	10																
HV705	HVAC Radiation, Media/Art	15	15																
PA107	Prime Paint, Mech/Elect	10	10																
PA114	Prime Paint, Kitch	5	5																
PA303	Finish Paint Exposed Struct, Gym	10	10																
WP205	Interior Caulking, Media/Art	15	15																
CL104	Ceiling Grid, Kitch	10	10																
DW404	Touch-up Drywall, Kitch	10	10																
EL703	Lighting Fixtures, Gym/Café	20	20																
FC203	Hang Interior Doors, Gym/Café	5	5																

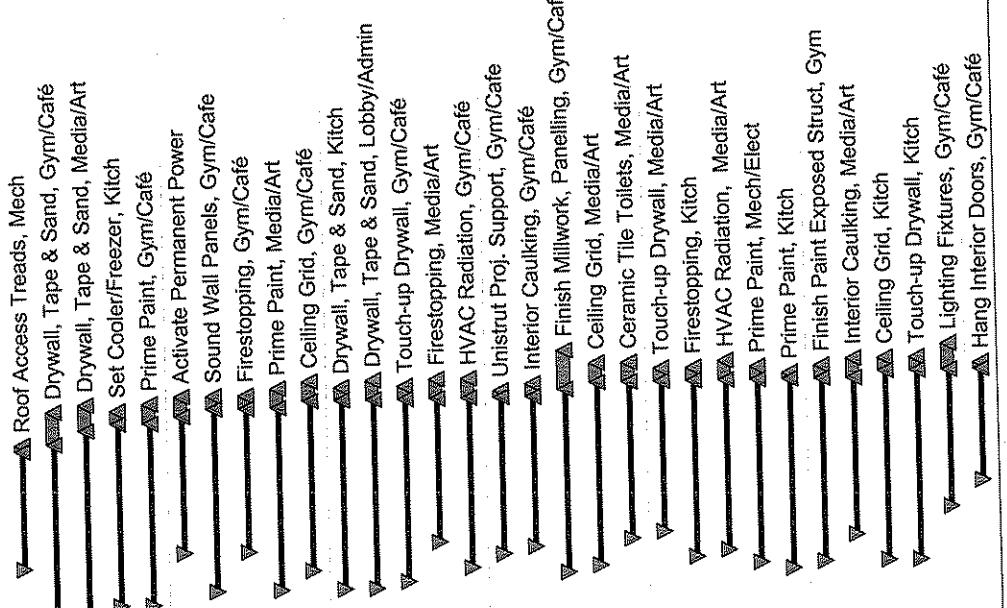

**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
FP403	Fire Protection - Finish Heads, Gym/Café	15	15																
FP507	Fire Protection - Compl, Test, Inspect Fire	5	5																
HV704	HVAC Radiation, Kitch	15	15																
HV723	Reg, Grilles, Fans, Finishes, Gym/Café	15	15																
HV803	ATC Controls - Finish, Gym/Café	10	10																
PA106	Prime Paint, Lobby/Admin	10	10																
WP204	Interior Caulking, Kitch	10	10																
DW503	Misc. Interior Drywall, Gym/Café	10	10																
GE103	Gym Backboards, Gym/Café	10	10																
MS503	Projection Screens, Gym/Café	5	5																
CL106	Ceiling Grid, Lobby/Admin	10	10																
CT104	Ceramic Tile, Kitch	10	10																
CT106	Wall Tile, Lobby/Admin	20	20																
CW105	Fixed Casework, Media/Art	15	15																
CW106	Fixed Casework, Lobby/Admin	5	5																
DW504	Misc. Interior Drywall, Kitch	10	10																
DW505	Misc. Interior Drywall, Media/Art	10	10																
EL704	Lighting Fixtures, Kitch	15	15																
EL705	Lighting Fixtures, Media/Art	15	15																
FC105	Finish Millwork, Media/Art	15	15																
FC106	Finish Millwork, Lobby/Admin	25	25																
FC205	Hang Interior Doors, Media/Art	15	15																
FP404	Fire Protection - Finish Heads, Kitch	15	15																
FP405	Fire Protection - Finish Heads, Media/Art	15	15																
HV714	Set/Connect CUH's, misc., Kitch	10	10																
HV715	Reg, Grilles, Finishes, Media/Art	15	15																
HV724	Reg, Grilles, Fans, Finishes, Kitch	15	15																
HV805	ATC Controls Finish, Media/Art	15	15																
MS104	FRP Walls, Kitch	15	15																
PL705	Plumbing Finish, Media/Art	15	15																
EL803	Scoreboard, Gym/Café	5	5																
HV804	ATC Controls - Finish, Kitch	15	15																
PA203	Complete Finish Paint Walls & Ceilings,	15	15																
PA204	Finish Paint Walls & Ceilings, Kitch	10	10																
CB106	MB/TB, Display Cases, Lobby/Admin	5	5																
ELL606	Lighting Fixtures, Lobby/Admin	10	10																
FP406	Fire Protection - Finish, Lobby/Admin	10	10																
HV706	HVAC Finish, Lobby/Admin	15	15																
MM203	Metal Rails, Gym/Café	10	10																

Forwarded to Architect/Owner:  
September 21, 2010  
Page 15A of 23A

```

graph TD
    HVACRad[HVAC Radiation] --> HVACPump[HVAC Protection - Compl, Test, Inspect Fire Pump]
    HVACPump --> HVACFin[HVAC Protection - Finish Heads, Gym/Café]
    HVACFin --> HVACGrilles[Reg, Grilles, Fans, Finishes, Gym/Café]
    HVACGrilles --> HVACCeil[ATC Controls - Finish, Gym/Café]
    HVACCeil --> HVACWalls[Complete Finish Paint Walls & Ceilings]
    HVACWalls --> HVACPWalls[Finish Paint Walls & Ceilings, Kitch]
    HVACPWalls --> MBTB[MB/TB, Display Cases, Lobby/Admin]
    MBTB --> LightingFixtures[Lighting Fixtures, Lobby/Admin]
    LightingFixtures --> FRPWalls[FRP Walls, Kitch]
    FRPWalls --> PlumbingFinish[Plumbing Finish, Media/Art]
    PlumbingFinish --> Scoreboard[Scoreboard, Gym/Café]
    Scoreboard --> ATCControls[ATC Controls - Finish, Kitch]
    ATCControls --> HVACFin
    HVACFin --> HVACGrilles
    HVACGrilles --> HVACCeil
    HVACCeil --> HVACWalls
    HVACWalls --> HVACPWalls
    HVACPWalls --> MBTB
    MBTB --> LightingFixtures
    LightingFixtures --> FRPWalls
    FRPWalls --> PlumbingFinish
    PlumbingFinish --> Scoreboard
    Scoreboard --> ATCControls
    ATCControls --> HVACFin
    
```

**Pompo/Center Elementary School  
Stow, MA**

Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 17A of 23A

Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 18A of 23A

**Pompo/Center Elementary School  
Stow, MA**

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
WN20D	Complete Alum Entr D184, Area D	5	5																
<b>Roughing-in</b>																			
HV201	Rough Ductwork Mains, 1st Class	20	20																
EL201	Electric - Rough Mains, Risers; 1st Class	20	20																
HV301	Rough HVAC Piping, 1st Class	20	20																
PL301	Plumbing - Rough & Test, 1st Class	20	20																
DW201	Interior Metal Stud Framing, 1st Class	20	20																
HV202	Rough Ductwork Mains, 2nd Class	20	20																
EL202	Electric - Rough Mains, Riser; 2nd Class	20	20																
EL301	Electric - Rough Ptns & Complete, 1st	20	20																
FP201	Fire Protection - Rough & Test, 1st Class	20	20																
HV302	Rough HVAC Piping, 2nd Class	20	20																
PL302	Plumbing - Rough & Test, 2nd Class	20	20																
DW202	Interior Metal Stud Framing, 2nd Class	20	20																
HV211	Complete Rough Ductwork, 1st Class	15	15																
HV401	Controls - Roughing-in, 1st Class	15	15																
RC401	Interior Rough Carpentry, 1st Class	15	15																
TC301	Telecommunications Rough, 1st Class	20	20																
EL302	Electric - Rough Pins & Complete, 2nd	20	20																
FP202	Fire Protection - Rough & Test, 2nd Class	20	20																
HV501	HVAC Pipe Insulation, 1st Class	15	15																
PL311	Plumbing - Rough Inspect, 1st Class	5	5																
EL208	Electric Rough, Stairs, Area D	10	10																
FP118	Fire Protection Rough, Stairs, Area D	10	10																
HV118	HVAC Rough, Stairs, Area D	10	10																
HV212	Complete Rough Ductwork, 2nd Class	15	15																
HV402	Controls - Roughing-in, 2nd Class	15	15																
PL401	Plumbing - Pipe Covering, 1st Class	10	10																
RC402	Interior Rough Carpentry, 2nd Class	15	15																
TC302	Telecommunications Rough, 2nd Class	20	20																
DW208	Shaft Walls, Elevator & Stairs, Area D	10	10																
EL401	Electric - Inspect Rough-in, 1st Class	5	5																
HV502	HVAC Pipe Insulation, 2nd Class	15	15																
PL312	Plumbing - Rough Inspect, 2nd Class	5	5																
PL402	Plumbing - Pipe Covering, 2nd Class	10	10																
EL402	Electric - Inspect Rough-in, 2nd Class	5	5																
<b>Interior Finishes</b>																			
DW301	Drywall, Tape & Sand, 1st Class	20	20																

▼ Drywall, Tape & Sand, 1st Class

**Pompo/Center Elementary School  
Stow, MA**

Forwarded to Architect/Owner:  
September 21, 2010  
Page 20A of 23A

Activity Description	Orig Dur	Rem Dur	2013						
			2010		2011		2012		
			Q2	Q3	Q1	Q2	Q3	Q4	
MM128	Misc. Metals at Elevator	5	5						
FS101	Firestopping, 1st Class	15	15						
DW302	Drywall, Tape & Sand, 2nd Class	20	20						
PA101	Prime Paint, 1st Class	15	15						
FS102	Firestopping, 2nd Class	15	15						
CB101	MB/TB, 1st Class	10	10						
CL101	Ceiling Grid, 1st Class	20	20						
CT101	Ceramic Tile Toilets, 1st Class	15	15						
DW401	Touch-up Drywall, 1st Class	10	10						
FC101	Finish Millwork, 1st Class	10	10						
PA102	Prime Paint, 2nd Class	15	15						
WP201	Interior Caulking, 1st Class	15	15						
DW508	Complete Sheetrock, Stairs	10	10						
FC201	Hang Interior Doors, 1st Class	15	15						
RS101	VCT Rooms, 1st Class	10	10						
CB102	MB/TB, 2nd Class	10	10						
CL102	Ceiling Grid, 2nd Class	20	20						
CT102	Ceramic Tile Toilets, 2nd Class	15	15						
CT201	Wall Tile at Corridors, 1st Class	20	20						
DW402	Touch-up Drywall, 2nd Class	10	10						
EV108	Elevator	30	30						
FC102	Finish Millwork, 2nd Class	10	10						
PA108	Prime Paint, Stairs	5	5						
PL701	Plumbing Finish, 1st Class	15	15						
WP202	Interior Caulking, 2nd Class	15	15						
CL108	Ceiling Grid, Stairs	10	10						
CP101	Carpet, 1st Class	5	5						
CW101	Fixed Casework, 1st Class	20	20						
EL701	Lighting Fixtures, 1st Class	20	20						
FC211	Complete Finish Hardware, 1st Class	15	15						
FP401	Fire Protection - Finish Heads, 1st Class	20	20						
HV701	HVAC Radiation, 1st Class	15	15						
HV711	Reg. Grilles, Fans, Finishes, 1st Class	15	15						
PA201	Finish Paint Walls & Ceilings, 1st Class	15	15						
FC202	Hang Interior Doors, 2nd Class	15	15						
RS102	VCT Rooms, 2nd Class	10	10						
CT202	Wall Tile at Corridors, 2nd Class	20	20						
CT208	Wall Tile, Stairs	15	15						
EL808	Electric Finish, Stairs	10	10						

Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 21A of 23A


Pompo/Center Elementary School  
Stow, MA

Forwarded to Architect/Owner:  
September 21, 2010  
Page 22A of 23A

**Pompo/Center Elementary School  
Stow, MA**

Forwarded to Architect/Owner:  
September 21, 2010  
Page 23A of 23A

Act ID	Activity Description	Orig Dur	Rem Dur	2010				2011				2012				2013			
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
<b>Completion</b>																			
END1A	Complete Phase 1A	0	0																
GC420	Building Commissioning - Phase 1	50	50																
ENDP1	Complete - Phase 1	15	15																
ENFP1	Owner's Float - Phase 1	15	15																
ENSPI1	Substantial Completion - Phase 1	0	0																
GC600	Owner - Teachers/Staff Move-in Phase 1	16	16																
GC610	Owner Vacate Existing Building	0	0																
GC700	Phase 2	121	121																
ENDP2	Substantial Completion - Phase 2	0	0																
		527	527																

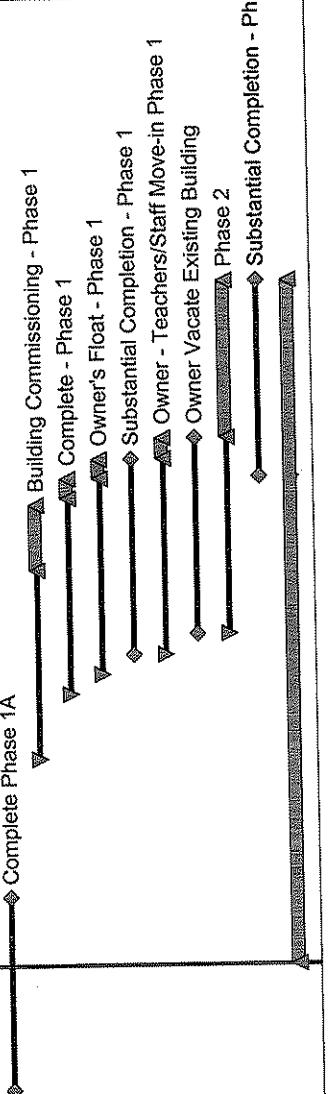

**Project Open Submittals**

09020.00

Stow Pompositicut Elementary School

P.J. Stella

03-Jan-11

In	Submittal Number	Type	Date In	Date Due	Review	Description	Comments
19	61000 . 1	Product Data	12/15/2010	12/30/2010	HSR	(5) Rough Carpentry - Arch Wood Pro	
19	61000 . 2	Product Data	12/15/2010	12/30/2010	HSR	(6) Rough Carpentry - Arch Wood Pro	
19	61000 . 3	Product Data	12/15/2010	12/30/2010	HSR	(7) Rough Carpentry - Arch Wood Pro	
19	61000 . 4	Product Data	12/15/2010	12/30/2010	HSR	(8) Rough Carpentry - Arch Wood Pro	
19	61000 . 5	Product Data	12/15/2010	12/30/2010	HSR	(9) Rough Carpentry - Star Sales / Hilt	
18	81113 . 3	Product Data	12/16/2010	12/31/2010	HSR	(20) Fasteners for Hollow Metal Fram	
18	92216 . 1	Product Data	12/16/2010	12/31/2010	HSR	(1) Non-Structural Metal Framing - M	
18	92216 . 2	Product Data	12/16/2010	12/31/2010	HSR	(4) Mfg Data: Framing Members - See	
18	92216 . 3	Product Data	12/16/2010	12/31/2010	HSR	(5) Mfg Data: Auxiliary materials - Fas	
17	85113 . 7	Product Data	12/17/2010	1/1/2011	KCH	(1) Aluminum Windows MA-CHPS Su	
17	85113 . 8	Shop Drawings	12/17/2010	1/1/2011	KCH	(4) Architectural Window Shops	
17	55000 . 2	Shop Drawings	12/17/2010	1/1/2011	HSR	(18) Loose Lintels Shop Drawing VG I	
17	55000 . 3	Shop Drawings	12/17/2010	1/1/2011	HSR	(12) Alternating Tread Devices Shop	
17	55000 . 4	Shop Drawings	12/17/2010	1/1/2011	HSR	(17) Beam Lintels Shop Dwgs VG Iron	
17	55000 . 5	Shop Drawings	12/17/2010	1/1/2011	HSR	(16) Dr Sup. Plan @ Storefront Shop	
14	84113 . 9	Schedule	12/20/2010	1/4/2011	HSR	(7) Entrance Door Hardware Schedul	
14	84113 . 10	Product Data	12/20/2010	1/4/2011	HSR	(20) Door Hardware Catalog Cuts	
12	84113 . 6	Shop Drawings	12/22/2010	1/6/2011	HSR	(084133-3) R&R Window Shop Drawi	
12	84113 . 11	Shop Drawings	12/22/2010	1/6/2011	HSR	(084113-2) R&R Window Shop Drawi	
13	55000 . 7	Shop Drawings	12/21/2010	1/5/2011	HSR	(11) Metal Ladders, VG Iron Sheets M	
13	55000 . 9	Shop Drawings	12/21/2010	1/5/2011	HSR	(22) Bent Plate at Lobby Bench	
13	55000 . 13	Shop Drawings	12/21/2010	1/5/2011	HSR	(19) Rails; VG Iron Drawings	
11	72726 . 7	Product Data	12/23/2010	1/7/2011	HSR	(6) ABAA Member Certificate - Install	
11	233423 . 5	Product Data	12/23/2010	1/7/2011	SES	(1R3) Resubmittal - Greenheck Mfg D	
11	233423 . 6	Shop Drawings	12/23/2010	1/7/2011	SES	(2R3) Resubmittal - Greenheck Shop	
10	260573 . 1	Product Data	12/24/2010	1/8/2011	MJB	260573-01 (#14 Pg147) Overcurrent Pr	
10	260573 . 2	Product Data	12/24/2010	1/8/2011	MJB	260573-06 (#13 Pg144) Overcurrent Pr	
10	262200 . 1	Product Data	12/24/2010	1/8/2011	MJB	262200-01 (#12 Pg128) Low-Voltage T	
10	262200 . 2	Product Data	12/24/2010	1/8/2011	MJB	262200-02 (#11 Pg118) Ea Trans. Type	
10	262200 . 3	Shop Drawings	12/24/2010	1/8/2011	MJB	262200-03 (#10 Pg133) Wiring Diagra	
10	262413 . 1	Product Data	12/24/2010	1/8/2011	MJB	262413-02 (#9 Pg6) Switchboards PD	
10	262413 . 2	Shop Drawings	12/24/2010	1/8/2011	MJB	262413-03 (#8 Pg5) Switchboards Dw	
10	262416 . 1	Product Data	12/24/2010	1/8/2011	MJB	262416-01 (#6 Pg60) Panelboards - M	
10	262416 . 2	Product Data	12/24/2010	1/8/2011	MJB	262416-02 (#5 Pg15) Panelboards PD -	
10	262416 . 3	Shop Drawings	12/24/2010	1/8/2011	MJB	262416-03 (#7 Pg16) Panelboards Dw	
10	262813 . 1	Product Data	12/24/2010	1/8/2011	MJB	262813-01 (#3 Pg184) Fuses - MA-CH	
10	262813 . 2	Product Data	12/24/2010	1/8/2011	MJB	262813-02 (#4 Pg182) Fuses Product	
10	264313 . 1	Product Data	12/24/2010	1/8/2011	MJB	264313-01 (#1 Pg170) Surge Protectiv	
10	264313 . 2	Product Data	12/24/2010	1/8/2011	MJB	264313-02 (#2 Pg167) Surge Protectiv	
10	262816 . 1	Product Data	12/24/2010	1/8/2011	MJB	262816-02 (#15 Pg101) Encl Switches	



# RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional  
 Job Name: Stow Pompositicut Elementary School  
 Job Location:

Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
								JW JW MSA HSR
001	OK	1	6/15/2010	PJ Stella	6/15/2010	6/16/2010	Grade Beam Reinforcing	RMC
002	OK	4	6/21/2010	PJ Stella	6/21/2010	6/25/2010	30' Drain Line Note	JW
003	OK	2	6/21/2010	PJ Stella	6/21/2010	6/23/2010	Enclosure Fence Windscreen	JW
004	OK	31	6/22/2010	PJ Stella	6/25/2010	7/26/2010	Roof Drain Piping	MSA
005	OK	16	6/29/2010	PJ Stella	6/29/2010	7/15/2010	Part B Canopy Foundation	HSR
006	OK	6	7/16/2010	PJ Stella	7/16/2010	7/22/2010	Survey Information	JW
007	OK	4	7/19/2010	PJ Stella	7/19/2010	7/23/2010	Materials Attributes Calculations	HSR
008	OK	3	7/23/2010	PJ Stella	7/23/2010	7/26/2010	Primary Electric Duct-Bank Conduit	HSR
009	OK	31	7/27/2010	PJ Stella	7/27/2010	8/27/2010	Electric Service Pole	JW
010	OK	9	7/28/2010	PJ Stella	7/28/2010	8/6/2010	Electric Panel at Existing Building	HSR
011	OK	5	7/28/2010	Sturo	7/28/2010	8/2/2010	Sturo RFI #01 - Col's. on line W	RMC
012	OK	5	7/28/2010	Sturo	7/28/2010	8/2/2010	Sturo RFI #2 - Typ. Bracing Gusset	RMC
013	OK	12	8/8/2010	PJ Stella	8/8/2010	8/20/2010	Addendum #1 Footing Change	M.B.
014	OK	3	7/30/2010	PJ Stella	7/30/2010	8/21/2010	Pole Riser Conduits	CK
015	OK	1	8/2/2010	PJ Stella	8/2/2010	8/31/2010	Pier Dimensions	JW
016	OK	2	8/3/2010	PJ Stella	8/3/2010	8/5/2010	Storm Drain Headwall	HSR
017	OK	0	8/6/2010	PJ Stella	8/6/2010	8/6/2010	Slab On Grade Base Course	RMC
018	OK	0	8/6/2010	PJ Stella	8/6/2010	8/6/2010	Footing Subgrade Preparation	RMC
019	OK	21	8/6/2010	PJ Stella	8/6/2010	8/27/2010	Phase 1A Asbestos Quantities	HSR
020	OK	27	8/6/2010	PJ Stella	8/6/2010	9/2/2010	Sturo RFI #3 Davit Location & Dims	RMC
021	OK	14	8/13/2010	PJ Stella	8/13/2010	8/27/2010	Site Grading Information	JW
022	OK	0	8/13/2010	PJ Stella	8/13/2010	8/13/2010	Parts A and B Roof Details	HSR
022.2	OK	5	8/19/2010	PJ Stella	8/19/2010	8/24/2010	Parts A and B Roof Details (Follow-up)	LBF
023	OK	1	8/17/2010	PJ Stella	8/17/2010	8/18/2010	0.40 W/C Concrete	RMC
23.2	OK	1	8/19/2010	PJ Stella	8/19/2010	8/20/2010	0.40 W/C Concrete	LBF
024	OK	29	8/17/2010	PJ Stella	8/17/2010	9/15/2010	Building Layout Discrepancies - PJS Field Sketches	HSR
024R1	OK	21	8/25/2010	PJ Stella	8/25/2010	9/15/2010	Building Layout Discrepancies - PJS Field Sketches	LBF
025	OK	1	8/17/2010	PJ Stella	8/17/2010	8/18/2010	Wood Flooring Systems	JED
026	OK	1	8/19/2010	PJ Stella	8/19/2010	8/20/2010	Basketball Backstops Supports	HSR
027	OK	5	8/19/2010	PJ Stella	8/19/2010	8/24/2010	Lobby Skylight Size	HSR
028	OK	1	8/19/2010	PJ Stella	8/19/2010	8/20/2010	Part A Existing Door Openings	JW
029	OK	13	8/20/2010	PJ Stella	8/20/2010	9/2/2010	Waterproofing Dimension	CK
030	OK	9	8/22/2010	Sturo	8/22/2010	8/31/2010	Dim and Size - Sturo RFI #13 and sketch regarding same	RMC
031	OK	5	8/22/2010	Sturo	8/22/2010	8/27/2010	Hole at Brace - Sturo RFI #14	



# RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional  
 Job Name: Stow Pompositcut Elementary School  
 Job Location:

## Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
032	OK	9	8/22/2010	Sturo	8/22/2010	8/31/2010	Screen Wall - Sturo RFI #16	CK
033	OK	9	8/22/2010	Sturo	8/22/2010	8/31/2010	Column at U/21 - Sturo RFI #17	CK
034	OK	4	8/23/2010	Sturo	8/23/2010	8/27/2010	Column Prep - Sturo RFI #18	RMC
034.2	OK	4	8/30/2010	PJ Stella	8/30/2010	9/3/2010	Column Prep - Sturo RFI #18	RMC
035	OK	8	8/22/2010	Sturo	8/23/2010	8/31/2010	Stair D178 - Sturo RFI #09	RMC
036	OK	8	8/22/2010	Sturo	8/23/2010	8/31/2010	Skylight Frame - Sturo RFI #10	CK
037	OK	8	8/22/2010	Sturo	8/23/2010	8/31/2010	Edge of Slab - Sturo RFI #11	CK
038	OK	9	8/22/2010	R&R	8/22/2010	8/31/2010	Frame SF14 - R&R RFI #01	KCH
039	OK	9	8/22/2010	R&R	8/22/2010	8/31/2010	Curtain Wall - R&R RFI #03	JED
040	OK	8	8/25/2010	Sturo	8/25/2010	9/2/2010	C-D Corner - Sturo RFI #08	CK
041	OK	1	8/26/2010	Sturo	8/26/2010	8/27/2010	Masonry Ties - Sturo RFI #19	LBF
042	OK	8	8/26/2010	Sturo	8/26/2010	9/3/2010	Det 3/S2.03 - Sturo RFI #20	RMC
043	OK	7	8/26/2010	Sturo	8/26/2010	9/2/2010	Dim at 24 and 30 - Sturo RFI #21	CK
044	OK	7	8/26/2010	Sturo	8/26/2010	9/2/2010	Bldg D Connections - Sturo RFI #24	RMC
045	OK	5	8/26/2010	Sturo	8/26/2010	8/31/2010	Applied Fireproofing Scope	KCH
046	OK	6	8/27/2010	PJ Stella	8/27/2010	9/2/2010	Platform Floor System	HSR
047	OK	5	8/28/2010	PJ Stella	8/28/2010	9/2/2010	Climbing Wall @ Gym	KCH
048	OK	5	8/28/2010	PJ Stella	8/28/2010	9/2/2010	Dim at F-Line - Sturo RFI #25	CK
049	OK	4	8/30/2010	PJ Stella	8/30/2010	9/3/2010	Fire Tank Access Manholes	JW
050	OK	1	8/30/2010	R&R	8/30/2010	8/31/2010	Operable Window Color	KCH
051	OK	1	8/30/2010	R&R	8/30/2010	8/31/2010	Sloped Glazing Mfg	HSR
052	OK	2	8/31/2010	PJ Stella	8/31/2010	9/2/2010	Onsite Reuse of materials	JW/RMC
053	OK	1	9/1/2010	PJ Stella	9/1/2010	9/2/2010	Wood Doors Glazing	KCH
054	OK	1	9/2/2010	PJ Stella	9/2/2010	9/3/2010	Composite Wall Panel Accent Colors	HSR
055	OK	29	9/2/2010	PJ Stella	9/2/2010	10/1/2010	Pumping Concrete	HSR
056	OK	4	9/3/2010	PJ Stella	9/3/2010	9/7/2010	Ftg Subgrade ~ fire pump pit	HSR
057	OK	2	9/7/2010	R&R	9/7/2010	9/9/2010	Operable Vents in Cur - R&R RFI #06	HSR
058	OK	2	9/7/2010	R&R	9/7/2010	9/9/2010	CW#6 Material - R&R RFI #07	HSR
059	OK	2	9/7/2010	R&R	9/7/2010	9/9/2010	Window Opg Clarificat - R&R RFI #08	HSR
060	OK	1	9/7/2010	R&R	9/7/2010	9/8/2010	Storefront Face Dimes - R&R RFI #09	KCH
061	OK	23	9/7/2010	R&R	9/7/2010	9/30/2010	Stair C122 Fire Rating - R&R RFI #10	KCH
062	OK	13	9/7/2010	R&R	9/7/2010	9/20/2010	Sloped Glazing - R&R RFI #11	PSG
063	OK	2	9/7/2010	Cincotta	9/7/2010	9/9/2010	R.S.F - Cincotta RFI #08	HSR
064	Overdue	117	9/8/2010	PJ Stella	9/8/2010		Titan Roofing Bonds Letter	HSR

# SMMA

## RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional  
 Job Name: Stow Pompositicut Elementary School  
 Job Location:  
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
065	OK	63	9/9/2010	Boston Showcase	9/9/2010	11/1/2010	Kitchen Equipment Customer Consent	HSR JW
066	OK	6	9/10/2010	PJ Stella	9/10/2010	9/16/2010	Detectable Warning Panels	KCH
067	OK	6	9/10/2010	PJ Stella	9/10/2010	9/16/2010	Electronic Scoreboards	HSR
068	OK	3	9/10/2010	Annesse	9/10/2010	9/13/2010	Watertight Seals - Annesse RFI #02	RMC
069	OK	3	9/14/2010	Sturo	9/14/2010	9/17/2010	Ventilated Deck - Sturo RFI #26	KCH
070	OK	2	9/14/2010	R&R	9/14/2010	9/16/2010	Spandrel Glass - R&R RFI #12	CK
071	OK	2	9/15/2010	Sturo	9/15/2010	9/17/2010	Roof Davit Bracket - Sturo RFI #27	CK
072	OK	2	9/15/2010	Sturo	9/15/2010	9/17/2010	Elevation Discrepancy - Sturo RFI #29	CK
073	OK	2	9/15/2010	Sturo	9/15/2010	9/17/2010	Sturo RFI #31 - Elevations at 14/N	CK
073.2	OK	9	10/6/2010	PJ Stella	10/6/2010	10/15/2010	Elevations at 14/N - Sturo RFI #31	CK
074	OK	5	9/15/2010	Sturo	9/15/2010	9/20/2010	Screen Wall - Sturo RFI #32	CK
075	OK	0	9/16/2010	PJ Stella	9/16/2010	9/16/2010	Gas Service Pit	MSA
075.2	OK	17	9/20/2010	PJ Stella	9/20/2010	10/7/2010	Gas Service Pit	KCH
076	OK	1	9/16/2010	Sturo	9/16/2010	9/17/2010	Tube Steel Elev. - Sturo RFI #33	CK
077	OK	1	9/16/2010	Sturo	9/16/2010	9/17/2010	El. Chan. @ CW - Sturo RFI #34	CK
078	OK	5	9/16/2010	Sturo	9/16/2010	9/21/2010	El. @ grid 1M & F - Sturo RFI #35	KCH
079	OK	11	9/20/2010	PJ Stella	9/20/2010	10/1/2010	Longspan Joists @ Gym	CK
080	OK	3	9/20/2010	PJ Stella	9/20/2010	9/23/2010	Exposed Structural Steel Finish	KCH
081	OK	4	9/17/2010	Cincotta	9/17/2010	9/21/2010	Pump Station Dims - Cincotta RFI #9	PSG
082	OK	25	9/17/2010	Sturo	9/17/2010	10/12/2010	W30x80 - Sturo RFI #36	RMC
083	OK	25	9/17/2010	Sturo	9/17/2010	10/12/2010	W27x55 Elevation - Sturo RFI #37	RMC
084	OK	14	9/17/2010	Sturo	9/17/2010	10/1/2010	Bent Plate Elevation - Sturo RFI #38	CK
085	OK	14	9/17/2010	Sturo	9/17/2010	10/1/2010	Bent Plate Elevation - Sturo RFI #39	CK
086	OK	14	9/17/2010	Sturo	9/17/2010	10/1/2010	Bent Plate Elevation - Sturo RFI #40	KCH
087	OK	1	9/20/2010	R&R	9/20/2010	9/21/2010	CW#6 Material - R&R RFI #14	KCH
088	OK	10	9/20/2010	R&R	9/20/2010	9/30/2010	Glassing Color Match - R&R RFI #15	KCH
089	OK	1	9/22/2010	PJ Stella	9/22/2010	9/23/2010	Maintenance Building Location - Excerpt of C3.01	JW
090	OK	14	9/23/2010	PJ Stella	9/23/2010	10/7/2010	Exterior Soffit Expan Joint Detail	KCH
091	OK	15	9/27/2010	Sturo	9/27/2010	10/12/2010	Screen Wall Connection - Sturo RFI #44	RMC
092	OK	21	9/27/2010	PJ Stella	9/27/2010	10/18/2010	Entrance Sign Details	KCH
093	OK	15	9/27/2010	Sturo	9/27/2010	10/12/2010	Outrigger at 30.1 - Sturo RFI #41	CK
094	OK	14	9/28/2010	PJ Stella	9/28/2010	10/12/2010	Joist Shop Drawings - Excerpt of Joist drawing J1	KCH
095	OK	9	9/28/2010	R&R	9/28/2010	10/7/2010	Sloped Glazing -	KCH
096	OK	7	9/30/2010	PJ Stella	9/30/2010	10/7/2010	Elevator Scope Clarification	KCH



# RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional  
 Job Name: Stow Pompositicut Elementary School  
 Job Location:

## Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
097	OK	9	9/28/2010	PJ Stella	9/28/2010	10/7/2010	Motorized Shades Scope Clarif..	KCH
098	OK	14	9/28/2010	Sturo	9/28/2010	10/12/2010	Dim at W8x10 - Sturo RFI #42	CK
099	OK	43	10/5/2010	PJ Stella	10/5/2010	11/17/2010	Window Shades Scope Clarification	KCH
100	OK	22	10/4/2010	PJ Stella	10/4/2010	10/26/2010	Telescoping Stands	KCH
101	OK	3	10/4/2010	PJ Stella	10/4/2010	10/7/2010	Retaining Wall Expansion Joint Detail	JW
101.2	OK	3	10/19/2010	PJ Stella	10/19/2010	10/22/2010	Retaining Wall Expansion Joint Detail	HSR
101.3	OK	0	10/29/2010	PJ Stella	10/29/2010	10/29/2010	Retaining Wall Expansion Joint Data	RMC
102	OK	2	10/4/2010	PJ Stella	10/4/2010	10/6/2010	Pump Station El. - Cincotta RFI #10	JW
103	OK	1	10/4/2010	Cincotta	10/4/2010	10/5/2010	Infiltration Sys - Cincotta RFI #11	JW
104	OK	15	10/5/2010	PJ Stella	10/5/2010	10/20/2010	Operable Partition Support	KCH
105	OK	1	10/6/2010	RJ Cincotta	10/6/2010	10/7/2010	Cincotta RFI #12 - Inf. Sys. Fill	JW
106	OK	5	10/6/2010	Cincotta	10/6/2010	10/11/2010	Inverts @ Infill - Cincotta RFI #13	RMC
107	OK	6	10/7/2010	PJ Stella	10/7/2010	10/13/2010	Remedial Work @ Sloped Footing 1/D	KCH
108	OK	8	10/14/2010	PJ Stella	10/14/2010	10/22/2010	Platform Stairs Layout	KCH
108.2	OK	5	11/12/2010	PJ Stella	11/12/2010	11/17/2010	Platform Stairs Layout	HSR
108.2R1	OK	0	11/22/2010	PJ Stella	11/22/2010	11/22/2010	Platform Stairs Layout	RMC
109	OK	18	10/14/2010	PJ Stella	10/14/2010	11/1/2010	Leveling Plate Installation	KCH
110	OK	8	10/14/2010	PJ Stella	10/14/2010	10/22/2010	Exterior Mockup Materials	JD
110.2	OK	0	11/1/2010	PJ Stella	11/1/2010	11/1/2010	Exterior Mock-Up Materials	KCH
110.3	OK	0	11/4/2010	PJ Stella	11/4/2010	11/4/2010	Exterior Mockup Materials	HSR
110.4	OK	3	11/19/2010	PJ Stella	11/19/2010	11/22/2010	Exterior Mockup Materials	KCH
111	OK	7	10/15/2010	PJ Stella	10/15/2010	10/22/2010	Gym Floor Outlet Locations	KCH
112	OK	7	10/15/2010	PJ Stella	10/15/2010	10/22/2010	Platform Electrical Outlet Location	KCH
113	OK	7	10/15/2010	PJ Stella	10/15/2010	10/22/2010	Computer/Media Floor Outlets	KCH
114	OK	20	10/15/2010	R&R	10/15/2010	11/4/2010	Glazing Make-Up - R&R RFI #16	HSR
114.2	OK	31	10/18/2010	R&R	10/18/2010	11/18/2010	Glazing Make-Up - R&R RFI #16	MJB
115	OK	5	10/15/2010	Stanley	10/15/2010	10/20/2010	Elevator Power - Stanley RFI #1	CK
116	OK	0	10/18/2010	Sturo	10/18/2010	10/18/2010	Detail 11/S4.03 - Sturo RFI #46	MJB
117	OK	28	10/18/2010	Annece	10/18/2010	11/15/2010	DDC Location - Annece RFI #4	LBF
118	OK	8	10/20/2010	Cincotta	10/20/2010	10/28/2010	Cincotta RFI #14 - 14K Recirc Tank	JW
118.2	OK	18	11/4/2010	PJ Stella	11/4/2010	11/22/2010	Cincotta RFI #14 - 14K Recirc Tank	RMC
119	OK	2	10/20/2010	PJ Stella	10/20/2010	10/22/2010	Rebar dowels at column W/33	KCH
120	OK	5	10/21/2010	PJ Stella	10/21/2010	10/26/2010	Line 18 Foundation Wall	RMC
121	OK	11	10/22/2010	PJ Stella	10/22/2010	11/2/2010	Pier/Grade Beam @ V/36	



# RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional  
 Job Name: Stow Pompositicut Elementary School  
 Job Location:  
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
122	OK	13	10/22/2010	PJ Stella	10/22/2010	11/14/2010	Storage Garage Foundations	KCH
123	OK	23	10/25/2010	PJ Stella	10/25/2010	11/17/2010	Cap Plate @ Z	CK
124	OK	10	10/25/2010	PJ Stella	10/25/2010	11/4/2010	Storage Garage Floor Pitch	KCH
124.2	OK	7	11/10/2010	PJ Stella	11/10/2010	11/7/2010	Storage Garage Floor Pitch	KCH
125	OK	1	10/25/2010	PJ Stella	10/25/2010	10/26/2010	Angle elev. - Sturo RFI #47	CK
126	OK	6	10/27/2010	PJ Stella	10/27/2010	11/12/2010	Elevator Pit Sump	HSR
127	OK	1	10/27/2010	PJ Stella	10/27/2010	10/28/2010	Braced Column Pier Replacements	RMC
128	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #02 - Lock Cylinder Types	KCH
129	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #03 - Door A101.2	KCH
130	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #05 - Doors EX-A100, EX-A1	KCH
131	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #06 - Doors C136A & C136C	KCH
132	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #07 - Knurling Hardware	KCH
133	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #08 - Door C134	KCH
134	OK	19	10/29/2010	PJ Stella	10/29/2010	11/17/2010	LIFD RFI #09 - Secure Side of Doors	KCH
135	OK	1	11/2/2010	PJ Stella	11/2/2010	11/3/2010	Retaining Wall Pour Lengths	RMC
136	OK	6	11/3/2010	PJ Stella	11/3/2010	11/9/2010	As-Built Pier Survey - Part C	RMC
136.2	OK	17	11/15/2010	PJ Stella	11/15/2010	12/2/2010	As-Built Pier Survey - Part C	RMC
136.3	OK	6	12/8/2010	PJ Stella	12/8/2010	12/14/2010	As-Built Pier Survey	RMC
137	OK	5	11/5/2010	PJ Stella	11/5/2010	11/10/2010	MACHPS Spreadsheets	LBF
138	OK	0	11/8/2010	PJ Stella	11/8/2010	11/8/2010	Housekeeping Pad C151.1	HSR
139	OK	5	11/10/2010	PJ Stella	11/10/2010	11/15/2010	Lobby C130 Knee Walls	HSR
140	OK	1	11/10/2010	Sturo	11/10/2010	11/11/2010	Bldg B Conflict - Sturo RFI #50	RMC
140R1	OK	8	11/10/2010	PJ Stella	11/10/2010	11/18/2010	Sturo RFI #30 - Bldg B Conflict	RMC
140.2	OK	25	12/9/2010	Sturo	12/9/2010	1/3/2011	Bldg B Conflict	RMC
141	OK	1	11/10/2010	Sturo	11/10/2010	11/11/2010	Roof Ops @ ERU-1 - Sturo RFI #49	CK
142	OK	1	11/10/2010	PJ Stella	11/10/2010	11/11/2010	Steel Shop Dwg Approval Block 7A	CK
143	OK							
144	Overage	46	11/18/2010	RJ Cincotta	11/18/2010		Slope of Road CB1-8 to CB1-3	JW
145	OK	0	11/22/2010	PJ Stella	11/22/2010	11/22/2010	Anchor Bolt Remediation	RMC
145.2	OK	1	11/23/2010	PJ Stella	11/23/2010	11/24/2010	Anchor Bolt Remediation	RMC
146	OK	4	11/19/2010	PJ Stella	11/19/2010	11/23/2010	Shaft Wall Thicknesses	KCH
147	OK	11	11/19/2010	USD	11/19/2010	11/30/2010	USD RFI #1	KCH
148	OK	5	11/19/2010	USD	11/19/2010	11/24/2010	Details at 3.11 - USD RFI #2	KCH
149	OK	3	11/19/2010	R&R	11/19/2010	11/22/2010	SKA-045 - R&R RFI #18	HSR



## RFI Report by Project

Job Number: 09020.00 Practice Group: Institutional  
 Job Name: Stow Pompositicut Elementary School  
 Job Location:  
 Distribution:

RFI #	Status	Days Out	RFI Date	Initiated By	Received	Returned	Description	Reviewer
150	OK	5	11/19/2010	LIFD	11/19/2010	11/24/2010	Wood Door Stain - LIFD RFI #10	HSR
151	OK	0	11/22/2010	PJ Stella	11/22/2010	11/22/2010	Vestibule C145 Dimension	HSR
152	OK	2	11/22/2010	Anneese	11/22/2010	11/24/2010	Anneese RFI #07 - Kitch. Pnl & Trans	MJB
153	OK	7	11/22/2010	PJ Stella	11/22/2010	11/29/2010	Additional Column Anchors	RMC
154	OK	5	11/24/2010	PJ Stella	11/24/2010	11/29/2010	Slab On Grade Construction Joint	RMC
155	OK	5	11/24/2010	PJ Stella	11/24/2010	11/29/2010	Moment Column Pier B-21	RMC
155.2	OK	1	12/2/2010	PJ Stella	12/2/2010	12/3/2010	Moment Column Pier B-21	RMC
155.3	OK	7	12/2/2010	PJ Stella	12/2/2010	12/9/2010	Moment Column Pier B-21	RMC
156	OK	3	11/26/2010	Sturo	11/26/2010	11/29/2010	Base Column Screen Wall	CK
157	OK	3	11/26/2010	Sturo	11/26/2010	11/29/2010	Edge of Deck Detail 13 on S4.02	CK
158	OK	17	11/26/2010	PJ Stella	11/26/2010	12/1/3/2010	W-36 Footing	RMC
159	OK	0	11/29/2010	PJ Stella	11/29/2010	11/29/2010	Column Pockets @ N-24, N-27, & N-29	RMC
160	OK	0	11/29/2010	PJ Stella	11/29/2010	11/29/2010	Remedial Work @ N-24, N-27, N-29	RMC
160.2	OK	2	12/7/2010	PJ Stella	12/7/2010	12/9/2010	Remedial Work @ N-24, N-27 & N-29	RMC
161	OK	3	11/30/2010	PJ Stella	11/30/2010	12/3/2010	Proposed Column Adjustments	RMC
162	OK	1	12/13/2010	LIFD	12/13/2010	12/14/2010	LIFD RFI #11 - SMMA P.R. #16	KCH
163	OK	1	12/13/2010	LIFD	12/13/2010	12/14/2010	LIFD RFI #12 - Floor Mag at Door C1	KCH
164	OK	4	12/13/2010	LIFD	12/13/2010	12/17/2010	LIFD RFI #013 - Keying @ Fixed Core	KCH
165	OK	6	12/13/2010	LIFD	12/13/2010	12/19/2010	LIFD RFI #14 - Tag # C136A and C13	KCH
166	OK	9	12/13/2010	LIFD	12/13/2010	12/22/2010	LIFD RFI #15 - Door Tag #C134	KCH
167	Oversize	21	12/13/2010	LIFD	12/13/2010	12/13/2010	LIFD RFI #16 - HW Set #10	KCH
168	OK	6	12/13/2010	LIFD	12/13/2010	12/19/2010	LIFD RFI #18 - HW Set #12 Ex-C151	KCH
169	OK	21	12/13/2010	USD	12/13/2010	1/3/2011	DWG Ref. 3/A3.20, 8/A4.18 , 5/A4.05 & STRCUTRUAL DRAWING S1.01C	RMC
170	Oversize	21	12/13/2010	USD	12/13/2010	12/13/2010	USD RFI #4.	KCH
171	OK	1	12/13/2010	Stanley	12/13/2010	12/14/2010	High epoxy primer	KCH
172	OK	2	12/21/2010	PJ Stella	12/21/2010	12/23/2010	Exterior Pier at W/37	CK
173	OK	12	12/22/2010	PJ Stella	12/22/2010	1/3/2011	GEM RFI #1 - 140H & 140HW conflict	IL

