CMS

Construction Monitoring Services, Inc.

Stow Pompositticut/Center Elementary School

OPM Monthly Status Report September 2010

Owner's Representatives

Project Managers

Construction Managers

Submitted by: Paul Griffin, OPM
October, 2010

270 Main Street
Marlboro, Massachusetts 01752
Tel: (508) 786-0600
Fax: (508) 786-0608
Email: cms@cms-ma.com

Monthly Status Report

Stow Pompositticut / Center Elementary School

September, 2010

Size: 98,050 SF
Enrollment: 660 Students
Reimbursement Rate: 52.11%

Project Team:

Owner's Project Manager: Construction Monitoring Services, Inc.
Paul Griffin (617) 429-5100
Neil Joyce (508) 808-1601

Architect: Symmes, Maini & McKee
Phil Poinelli – (617) 547-5400
Lorraine Finnigan – (617) 547-5400

Project Budget: $37,829,870 ***Status:*** Construction – 12% Complete

Project Status Overview – Work Completed through August, 2010 (OPM 8.1.3.01)

Project activities previously completed included completion of Phase IA work items, including partial building demolition, site drainage and site restoration activities critical to the start of school. The General Contractor staging area was relocated to the Hartley Road site. School was opened without incident.

Project Status Summary – Work Complete through September 30, 2010 (OPM 8.1.3.02)

During the month of September, major construction activities completed by PJ Stella and their subcontractors included:

- Completion of project layout and perimeter fencing.
- Extensive sitework, including cut / fill of site, ledge excavation, perimeter drainage, headwall construction at 30" drain line, and processing on-site materials.
- Footing, frost wall and grade beam construction on the proposed addition is approximately 80% complete, with the balance of foundation work forecast for completion during early October.

- Commencement of under-slab utilities (plumbing, electrical) within the building footprint

Administrative Oversight: The following is a summary of non-construction related progress (work performed by the OPM / Architect & Design Team) during the month of September, 2010, as well as a forecast of the current administrative schedule through the anticipated end date of the project:

Contract Administration: The management team has been continuously involved in project and contract administration including but not limited to submittal review, RFI response and investigation, controlled construction oversight, change order review and overall project controls.

Future Work Forecast: A preliminary construction schedule prepared by the contractor has been provided for information. It is anticipated the following major construction items will be completed during the forthcoming three-month period (October – December, 2010):

- Site Access Road from east site limits (Hartley Road), complete with associated project infrastructure.
- Utility construction, including site drainage and infiltration systems
- Building Cut / Fill at proposed access road
- Completion of under-slab utilities
- Completion of footing and foundation construction for proposed building addition and storage building. Waterproofing and backfill of the foundation walls will be complete. Additional concrete operations will include installation of the slabs on grade.
- Steel erection is planned to begin in early November, 2010.

Schedule Update (OPM 8.1.3.03)

PJ Stella Construction Company has presented a preliminary construction schedule for the current period through the completion of Phase IA, in late August, 2010. Current progress is largely consistent with activities forecasted on the schedule.

The project has received the full contract schedule and currently has it under review.

Financial Update (OPM 8.1.3.04 / 8.1.3.05 / 8.1.3.06)

Change Order #1 (zero cost – administrative changes) and Change Order #2 (in the amount of $14,085) have been executed by the Project. Pending Changes in the estimated amount of $150,000 have been submitted to the project for considerataion, and are under review and negotiation with PJ Stella.

Contractor's Safety Performance (OPM 8.1.3.07)

With regard to the construction operations underway at the site, CMS is not aware of any lost-time accidents or incidents occurring at the site. CMS will provide updates on these items as soon as they are available.

Designer's QA/QC (OPM 8.1.3.08)

Construction Monitoring Services has maintained a constructive working relationship with Symmes Maini & McKee throughout the duration of our involvement with the project. We will continue to work in cooperation with SMMA to identify potential issues in the construction documents, and address them prior to their impacting construction operations or progress.

Contractor's Environmental Compliance (OPM 8.1.3.09)

With regard to environmental compliance of the current construction operations, no report of any environmental abnormalities has been received. Minor site infractions (damaged hay bales, groundwater pumping, etc.) have been remedied by PJ Stella and their site contractor without delay.

Community Issues (OPM 8.1.3.10)

CMS continues to be proactive with the Town, Building Committee and community in addressing any issues. No community issues are known at this time.

Designer & Contractor MBE/WBE Activity (OPM 8.1.3.11)

CMS has requested from P.J. Stella Company the SOMWBA Reports.

Project Issues and Concerns (OPM 8.1.3.10 / 8.1.3.11)

No project issues and/or concerns exist at this point in time. Should any issues arise, CMS will notify the client and the MSBA as soon as practical.

Stow - Center Elementary School

10/1/2010

CMS

	Budget	Reallocations	Budget Contracted	Anticipated	Paid to Date	(Anticipated minus Paid)	% Expended
1. General Construction							
1a. General Contractor	28,841,856	(5,200,956)	23,640,900	23,640,900	751,781	22,948,044	3%
1b. Change Orders	-	58,925	58,925	58,925	-	-	
1c. Outstanding	-	-	-	-	-	-	
1d. Contingency	2,163,139		2,163,139				
Total	**31,004,995**	**(5,142,031)**	**25,862,964**	**23,699,825**	**751,781**	**22,948,044**	**0**
2. Architect							
Prior	55,200	*37,300*	92,500	92,500	92,500	-	100%
2a. Architect's Basic Service Fees	3,031,000		3,031,000	3,031,000	2,295,000	736,000	76%
2b. Architect's Amendments	184,222		184,222	184,222	77,897	106,325	0%
2c. Architects Reimbursables	-		-	-		-	0%
2d Architect's Consultants	-		-	-	-	-	0%
Total	**3,270,422**	**37,300**	**3,307,722**	**3,307,722**	**2,465,397**	**842,325**	**75%**
3. Site Development							
	-	-	-	-	-	-	0%
4. Furniture, Fixtures, Technology & Equipment							
Furnishings	720,000	-	720,000	720,000	-	720,000	0%
Technlogy	1,047,700		1,047,700	1,047,700	-	1,047,700	
Misc.	20,000		20,000	20,000	-	20,000	0%
Total	**1,787,700**	-	**1,787,700**	**1,787,700**	-	**1,787,700**	-
5. Other							
	-	-	-	-	-	-	0%
6. P.M. & Clerk Services							
CMS	848,875		848,875	848,875	73,750	775,125	9%
Amendments	-	124,454	124,454	124,454	113,654	10,800	0%
CMS Reimburseables	70,000	(70,000)	-	-		-	0%
Total	**918,875**	54,454	**973,329**	**973,329**	**187,404**	**785,925**	**0**
7. Testing & Inspections							
7a. Testing & Inspections	50,000	(6,458)	43,542	43,542	-	43,542	0%
7b. Boring and Surveys			-	-	-	-	0%
Total	**50,000**		**43,542**	**43,542**	-	**43,542**	**0%**
8. Legal, Bonding & Moving							
8a. Legal	40,000		40,000	40,000	11,280	28,720	28%
8b. Bonding	-		-	-	-	-	0%
8c. Moving	50,000	-	50,000	50,000	-	50,000	0%
Total	**90,000**		**90,000**	**90,000**	**11,280**	**78,720**	**13%**
9. Advertising & Printing							
9a.Printing & Adverstising	**70,000**	*-47996*	22,004	22,004	74	21,930	0%
10. Other/Miscellaneous Expense							
10a. Administrative	20,000	-	20,000	-	-	-	0%
10b. Miscellaneous Expenses	2,000		2,000	2,000	-	2,000	0%
10c. Utilities & Other Misc. Fees			-	-	1,313	(1,313)	0%
Total	**22,000**	-	**22,000**	**2,000**	**1,313**	687	**66%**
Subtotal	37,213,992	(5,098,273)	32,109,261	29,926,122	3,417,250	26,508,872	11%
Contingency/Uncommitted:							
Owner's Contingency	615,878	(37,300)	5,720,609			-	
TOTAL COST	37,829,870		37,829,870	29,926,122	3,417,250	26,508,872	11.42%

Change Order Detail Log

Stow Center Elementary School

CMS

Change Order #1 -			Owner	Unknown			Local	Other
PCO#	Description		Adds	Condition	Omission	Error	Authorities	(Credit)
	Contract changes	$0.00						

Change Order #2 - Approved			Owner	Unknown			Local	Other
PCO#	Description		Adds	Condition	Omission	Error	Authorities	(Credit)
00001.2	Wetland Flagging - Hay Bales	$985.00						
00003.2	Existing fire dumpster	$13,100.00						
		$14,085.00						

Change Order #3			Owner	Unknown			Local	Other
PCO#	Description		Adds	Condition	Omission	Error	Authorities	(Credit)
2.2	Primary electric riser conduit	$1,772.00						
6.4	Wetland mitigation	$41,074.00						
9	Electrical panel at existing building	$1,994.00						
		$44,840.00						

Change Order #4			Owner	Unknown			Local	Other
PCO#	Description		Adds	Condition	Omission	Error	Authorities	(Credit)
TOTALS:		$58,925.00	$0.00	$0.00	$0.00	$0.00	$0.00	$0.00

C M S

Proposed Change Order Log

Stow Center Elementary School

PCO	Description	Date	CCD	PR	Proposed	Approved	CO#
00001	Wetland Flagging - Hay Bales	7/15/2010					
00001.2	Wetland Flagging - Hay Bales	7/16/2010		1	$985.00	$985.00	2
00002	Primary electric riser conduit	8/9/2010		4			
00002.2	Primary electric riser conduit	9/23/2010		4	$1,772.00		3
00003.2	Existing fire dumpster	8/27/2010	002R1		$13,100.00	$13,100.00	2
00004	Architectural/structural modifications	8/22/2010		2	$4,771.00		
00005	Builders risk insurance	8/23/2010			$5,299.00		
00006.2	Wetland Mitigation	8/28/2010					
00006.3	Wetland Mitigation	9/13/2010					
00006.4	Wetland Mitigation	9/28/2010		6	$41,074.00		3
00007	Rock removal	8/30/2010			$99,776.00		
00008	Ceiling revisions	9/7/2010			$1,083.00		
00009	Electric panel at existing building	9/17/2010	001R1		$1,994.00		3

C M S

Construction Change Directive Log

Stow Center Elementary School

No.	Description	Amount	Date	COR	CO	PR	PCO
1	Disconnect & relocate existing panel P2 as indicated in sketch SKE-05		7/15/2010				
1R1	Signed partial field T&M slips regarding electric panel existing building		8/17/2010				
2R1	Remove & dispose existing asbestos containing floor tile material	$13,100.00	7/30/2010		2		3.2
3	Removal of tranite pipe		8/24/2010				

Nashoba Pompo/Center School Project
Cash Flow Projections

10/6/2010

	Prior Year Total	Jan-10	Feb-10	Mar-10	Apr-10	May-10	Jun-10	Jul-10	Aug-10	Sep-10	Oct-10	Nov-10	Dec-10	Total
Budget	1,119,941	234,012	239,000	282,000	289,000	282,000	297,600	283,850	498,850	476,850	826,850	1,026,850	1,126,850	6,983,653
Actual	782,924	317,362	235,288	391,929	557,300	129,415	83,410	408,024	408,476	103,122				3,417,250
Variance	337,017	-83,350	3,712	-109,929	-268,300	152,585	214,190	-124,174	90,374	373,728	0	0	0	585,853

	Prior Year Total	Jan-11	Feb-11	Mar-11	Apr-11	May-11	Jun-11	Jul-11	Aug-11	Sep-11	Oct-11	Nov-11	Dec-11	Total
Budget	6,983,653	1,234,850	1,734,850	1,756,850	1,734,850	1,734,850	2,234,850	2,234,850	1,934,850	1,734,850	1,755,850	1,234,850	1,084,850	27,394,853
Actual														0
Variance	6,983,653	1,234,850	1,734,850	1,756,850	1,734,850	1,734,850	2,234,850	2,234,850	1,934,850	1,734,850	1,755,850	1,234,850	1,084,850	27,394,853

	Prior Year Total	Jan-12	Feb-12	Mar-12	Apr-12	May-12	Jun-12	Jul-12	Aug-12	Sep-12	Oct-12	Nov-12	Dec-12	Total
Budget	27,394,853	971,989	886,850	608,850	568,850	490,850	974,892	464,725	220,549	67,000	10,000	10,000	5,160,462	37,829,870
Actual														0
Variance	27,394,853	971,989	886,850	608,850	568,850	490,850	974,892	464,725	220,549	67,000	10,000	10,000	5,160,462	37,829,870

Prepared by: CMS

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Contract Changes								
Contract Changes								
Contract Changes								
CCCIC2A	CIC #2 Issued - Electric Panel at Exst	0	12JUL10 A		12JUL10 A			100
CCCIC2B	CCD #1R Issued - Electric Panel at Exst	0	12JUL10 A	26JUL10 A	12JUL10 A	26JUL10 A		100
CCCIC2C	Procure and Complete CCD #1R Work	0	27JUL10 A	10AUG10 A	27JUL10 A	10AUG10 A		100
CCNOC3A	NOC #3 Issued - Topsoil Removal	0	11AUG10 A		11AUG10 A			100
CCCIC2D	Remobilize Demolition	0	11AUG10 A	12AUG10 A	11AUG10 A	12AUG10 A		100
CCNOC3B	NOC #3 - Topsoil Removal Direction Issued	0	11AUG10 A	17AUG10 A	11AUG10 A	17AUG10 A		100
CCCIC6A	CIC #6 Issued - Rock Removal	0	12AUG10 A		12AUG10 A			100
CCCIC7A	CIC #7 Issued - ACM Pipe	0	12AUG10 A		12AUG10 A			100
CCCIC7B	CCD #3 Issued - ACM Pipe	0	12AUG10 A	26AUG10 A	12AUG10 A	26AUG10 A		100
CCCIC6B	CIC #6 - Additional Rock Removal	5	16AUG10 A	08OCT10	16AUG10 A	24SEP10	-10d	0
CCCIC7C	CCD #3 - Remove ACM Pipe	0	26AUG10 A	14SEP10 A	26AUG10 A	14SEP10 A		100
CCNOC3C	NOC #7 Issued - Topsoil Removal Site	0	21SEP10 A		21SEP10 A			100
CCNOC3D	NOC #7 - Topsoil Removal Direction Issued	0	21SEP10 A	24SEP10 A	21SEP10 A	24SEP10 A		100
General Conditions/Start-up/Owner/AE								
General Conditions/Start-up/Owner/AE								
General Conditions/Start-up/Owner/AE								
GC100	Bid - Award - NTP	0	07JUN10 A	15JUN10 A	07JUN10 A	15JUN10 A		100
GC110	Commence Construction	0	15JUN10 A		15JUN10 A			100
GC120	Obtain CADD Files, Prepare Layout	0	16JUN10 A	23JUN10 A	16JUN10 A	23JUN10 A		100
GC140	Procure Abatement, Demo, Sitework Subs	0	16JUN10 A	25JUN10 A	16JUN10 A	25JUN10 A		100
GC130	Obtain Building Permit	0	16JUN10 A	02JUL10 A	16JUN10 A	02JUL10 A		100
GC150	Mobilize, Set-up	0	16JUN10 A	23JUL10 A	16JUN10 A	23JUL10 A		100
GC160	Commence Submittals	0	21JUN10 A		21JUN10 A			100
GC180	Initial Site Layout, Engineering	0	29JUN10 A	19JUL10 A	29JUN10 A	19JUL10 A		100
GC170	File Abatement Notices	0	30JUN10 A	12JUL10 A	30JUN10 A	12JUL10 A		100
GC400	Exterior Building Mock-up Panel	5	04NOV10	10NOV10	06DEC10	10DEC10	22d	0
GC410	Exterior Building Mock-up Commissioning	15	11NOV10	01DEC10	13DEC10	31DEC10	22d	0
GC500	School Out for 2011 Summer	0	22JUN11 *		22JUN11		0	0
GC510	School Summer Break 2011	48	22JUN11	26AUG11	22JUN11	26AUG11	0	0
GC520	School Summer Break 2011 Ends	0		26AUG11		26AUG11 *	0	0
Initial Sitework Prep - Phase 1								
General Conditions/Start-up/Owner/AE								
GC190	Set Office Trailers (Temporary)	0	01JUL10 A	01JUL10 A	01JUL10 A	01JUL10 A		100
GC200	Meeting with Conservation Commission	0	02JUL10 A	02JUL10 A	02JUL10 A	02JUL10 A		100
GC210	Temporary Construction Fencing	0	02AUG10 A	27AUG10 A	02AUG10 A	27AUG10 A		100
GC220	Prepare Trailer, Staging Areas	0	16AUG10 A	16AUG10 A	16AUG10 A	16AUG10 A		100

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Initial Sitework - Phase 1A								
General Conditions/Start-up/Owner/AE								
GC300	Owner Relocate Blacksmith Shop	0	28JUL10 A	10AUG10 A	28JUL10 A	10AUG10 A		100
GC250	Relocate Office Trailers	0	17AUG10 A	19AUG10 A	17AUG10 A	19AUG10 A		100
GC240	Vacate Existing School Area	0	20AUG10 A	23AUG10 A	20AUG10 A	23AUG10 A		100
Existing Building - Phase 1A								
General Conditions/Start-up/Owner/AE								
GC230	Secure Existing Building	0	23AUG10 A	23AUG10 A	23AUG10 A	23AUG10 A		100
Existing Building								
Existing Building - Phase 1A								
Abatement, Demolition								
DM100	Asbestos Abatement	0	20JUL10 A	30JUL10 A	20JUL10 A	30JUL10 A		100
HV101A	Cut/Cap MEP	0	30JUL10 A	30JUL10 A	30JUL10 A	30JUL10 A		100
DM120	Building Demolition	0	12AUG10 A	19AUG10 A	12AUG10 A	19AUG10 A		100
Sitework								
Initial Sitework Prep - Phase 1								
Sitework: Preparation								
SW1120	Erosion Control, Protections	0	06JUL10 A	13JUL10 A	06JUL10 A	13JUL10 A		100
SW1130	Clear and Grub	0	12JUL10 A	19JUL10 A	12JUL10 A	19JUL10 A		100
SW1140	Strip, Stockpile Topsoil	0	12JUL10 A	28JUL10 A	12JUL10 A	28JUL10 A		100
SW1110	Cut-In Initial Site Access	0	12JUL10 A	30JUL10 A	12JUL10 A	30JUL10 A		100
SW1160	Haul Out Excess Topsoil (Partial)	0	19AUG10 A	21SEP10 A	19AUG10 A	21SEP10 A		100
SW1150	Existing Utility Relocations	0	24AUG10 A	27AUG10 A	24AUG10 A	27AUG10 A		100
SW1160A	Haul Out Excess Topsoil (Complete)	10	27SEP10 A	15OCT10	27SEP10 A	29OCT10	10d	0
Initial Sitework - Phase 1A								
Sitework: Preparation								
SW1210	Cut/Prep Utility Trenching	0	16AUG10 A	19AUG10 A	16AUG10 A	19AUG10 A		100
EL101A	Power & Communications Service to Phase 1	0	19AUG10 A	26AUG10 A	19AUG10 A	26AUG10 A		100
SW1220	Patch Utility Trenching	0	27AUG10 A	27AUG10 A	27AUG10 A	27AUG10 A		100
Sitework: Utilities, Roadways, Paving								
SW2210	Gas Service to Phase 1	0	23AUG10 A	24AUG10 A	23AUG10 A	24AUG10 A		100
Sitework - Building Area								
Sitework: Preparation								
SW1310	Building Cuts & Fills, West	0	28JUL10 A	13AUG10 A	28JUL10 A	13AUG10 A		100
SW1320	New 30" Drain Line at West	0	02AUG10 A	13AUG10 A	02AUG10 A	13AUG10 A		100
SW1340	Building Cuts & Fills, East	0	18AUG10 A	27AUG10 A	18AUG10 A	27AUG10 A		100
SW1330	Remove Existing Drainage	0	26AUG10 A	14SEP10 A	26AUG10 A	14SEP10 A		100
SW1350	Sewer Temporary Force Main	0	30AUG10 A	31AUG10 A	30AUG10 A	31AUG10 A		100
EL10SW	UG Site Electric to Bldg	5	01NOV10	05NOV10	25OCT10	29OCT10	-5d	0
SW1360	Rough Grade Around Building	5	08NOV10	12NOV10	01NOV10	05NOV10	-5d	0
FN500	Concrete Bench Wall	5	19MAY11	25MAY11	09JUN11	15JUN11	15d	0
EL50SW	Set Transformer	5	30MAY11	03JUN11	18JUL11	22JUL11	35d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
EL51SW	Set Emergency Generator	5	30MAY11	03JUN11	03OCT11	07OCT11	90d	0
EL90SW	Test and Inspect Emergency Genarator	5	27JUN11	01JUL11	10OCT11	14OCT11	75d	0
Sitework: Utilities, Roadways, Paving								
SW2310	Set DMH1-5, DMH1-6 at South, Building	0	06SEP10 A	07SEP10 A	06SEP10 A	07SEP10 A		100
SW2312	New Drain Line at South, Building	0	07SEP10 A	13SEP10 A	07SEP10 A	13SEP10 A		100
SW2316	Drainage at Building Area	10	14SEP10 A	15OCT10	14SEP10 A	08OCT10	-5d	50
SW2314	Temporary Drain Line at South, Building	0	27SEP10 A	27SEP10 A	27SEP10 A	27SEP10 A		100
SW2318	Infiltration Area 1	3	27SEP10 A	06OCT10	27SEP10 A	08OCT10	2d	70
SW2328	Infiltration Area 2	10	07OCT10	20OCT10	25OCT10	05NOV10	12d	0
SW2320	Site Roof Drain Piping	5	18OCT10	22OCT10	25OCT10	29OCT10	5d	0
SW2322	Water Mains at Building Area, Partial	10	18OCT10	29OCT10	11OCT10	22OCT10	-5d	0
SW2326	Excavate Site UG Electric to Building	5	25OCT10	29OCT10	18OCT10	22OCT10	-5d	0
SW2330	Backfill UG Site Electric to Building	2	04NOV10	05NOV10	28OCT10	29OCT10	-5d	0
SW2332	Ex/Set/Bckfl Fire Suppression Tanks	5	20DEC10	24DEC10	07FEB11	11FEB11	35d	0
SW2334	Water/Fire Piping at Fire Supp Tanks	5	27DEC10	31DEC10	14FEB11	18FEB11	35d	0
SW2336	Well Water Piping	5	03JAN11	07JAN11	18APR11	22APR11	75d	0
SW2338	Test & Chlorinate Water System	5	10JAN11	14JAN11	25APR11	29APR11	75d	0
SW2340	Complete Gas Service to Building	5	02MAY11	06MAY11	23MAY11	27MAY11	15d	0
SW2342	Excavate/Prep Transf, Gen, Gas Pads	5	09MAY11	13MAY11	30MAY11	03JUN11	15d	0
SW2344	Form/Pour/Strip Conc Tranf, Gen, Gas Pads	5	16MAY11	20MAY11	06JUN11	10JUN11	15d	0
SW2346	Backfill Transf, Gen, Gas Pads	5	23MAY11	27MAY11	13JUN11	17JUN11	15d	0
SW2348	Grade Fire Lane/Service, Building	10	30MAY11	10JUN11	20JUN11	01JUL11	15d	0
SW2350	E/B Site Lighting, Building	10	30MAY11	10JUN11	11JUL11	22JUL11	30d	0
EL13SW	UG Site Lighting, Building	10	30MAY11	10JUN11	18JUL11	29JUL11	35d	0
SW2352	Under Drain at Fire Lane, Building	5	13JUN11	17JUN11	25JUL11	29JUL11	30d	0
SW2354	Complete Rims, Inverts, Misc. Utilities, Bldg	10	13JUN11	24JUN11	15AUG11	26AUG11	45d	0
SW2324	Infiltration Area 3	10	04JUL11	15JUL11	08AUG11	19AUG11	25d	0
SW2356	Prep and FG Fire Lane/Service at Building	10	01AUG11	12AUG11	01AUG11	12AUG11	0	0
SW2358	Finish Pave Fire Lane/Service at Building	5	29AUG11	02SEP11	29AUG11	02SEP11	0	0
Sitework: Walks, Finishes, Landscaping								
SW4310	Excavate Concrete Bench Wall	3	16MAY11	18MAY11	06JUN11	08JUN11	15d	0
SW4312	Backfill Bench Wall	2	26MAY11	27MAY11	16JUN11	17JUN11	15d	0
SW5310	Granite Top & Edging at Bench Wall	5	30MAY11	03JUN11	04JUL11	08JUL11	25d	0
SW4314	Segmental Retaining Wall, Building	5	13JUN11	17JUN11	20JUN11	24JUN11	5d	0
SW4316	Prep/Grade Concrete Walkways, Building	20	04JUL11	29JUL11	27JUN11	22JUL11	-5d	0
SW4318	Traffic Signage, Building	5	11JUL11	15JUL11	25JUL11	29JUL11	10d	0
SL400	Concrete Walkways, Building	20	18JUL11	12AUG11	11JUL11	05AUG11	-5d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
MM400	Site Bollards	5	01AUG11	05AUG11	25JUL11	29JUL11	-5d	0
SW5312	Barricade Gates, Building	5	01AUG11	05AUG11	15AUG11	19AUG11	10d	0
SW4320	Paving Binder at Service, Building	5	15AUG11	19AUG11	15AUG11	19AUG11	0	0
SW4324	Mow Strip, Stone Pit, Building	10	15AUG11	26AUG11	08AUG11	19AUG11	-5d	0
SW4322	Bit Berm, Building	5	22AUG11	26AUG11	22AUG11	26AUG11	0	0
SW4326	Spread Topsoil, Building	15	29AUG11	16SEP11	22AUG11	09SEP11	-5d	0
SW5314	Plantings, Building	10	05SEP11	16SEP11	12SEP11	23SEP11	5d	0
SW5316	Waste Receptacles, Wood Benches, Building	10	19SEP11	30SEP11	17OCT11	28OCT11	20d	0
SW5318	FG and Lawns, Building	10	03OCT11	14OCT11	26SEP11	07OCT11	-5d	0
SW4328	Pavement Markings	5	31OCT11	04NOV11	24OCT11	28OCT11	-5d	0
Sitework - Entry/Roadway/Parking								
Sitework: Preparation								
SW1410	Initial Rough Grade Entry Road	0	16AUG10 A	17AUG10 A	16AUG10 A	17AUG10 A		100
SW1420	Cuts and Fills Roadway	0	22SEP10 A	24SEP10 A	22SEP10 A	24SEP10 A		100
SW1430	Cuts and Fills, Northeast Parking	5	04OCT10	08OCT10	20SEP10	24SEP10	-10d	0
EL11SW	Electric UG under Roadway	5	01NOV10	05NOV10	18OCT10	22OCT10	-10d	0
SW1440	Prepare Storage Staging Area	5	22NOV10	26NOV10	20DEC10	24DEC10	20d	0
Sitework: Utilities, Roadways, Paving								
SW2412	Grade Northeast Parking	5	11OCT10	15OCT10	27SEP10	01OCT10	-10d	0
SW2410	Drainage at Roadway	10	11OCT10	22OCT10	27SEP10	08OCT10	-10d	0
SW2416	Under Drain at Northeast Parking	5	18OCT10	22OCT10	04OCT10	08OCT10	-10d	0
SW2414	Force Main at Roadway	10	18OCT10	29OCT10	04OCT10	15OCT10	-10d	0
SW2418	Water Mains at Roadway	10	18OCT10	29OCT10	04OCT10	15OCT10	-10d	0
SW2420	Gravel and Finish Grade, NE Parking	5	25OCT10	29OCT10	11OCT10	15OCT10	-10d	0
SW2430	New Sanitary System	25	25OCT10	26NOV10	15NOV10	17DEC10	15d	0
SW2424	Excavate Electric under Roadway	3	01NOV10	03NOV10	18OCT10	20OCT10	-10d	0
SW2422	Rough Grade Roadway - Partial	5	01NOV10	05NOV10	18OCT10	22OCT10	-10d	0
SW2426	Backfill Electric under Roadway	2	04NOV10	05NOV10	21OCT10	22OCT10	-10d	0
SW2428	Gravel and Finish Grade Roadway - Partial	5	08NOV10	12NOV10	25OCT10	29OCT10	-10d	0
SW2432	Paving Binder, NE Parking and Partial Road	5	15NOV10	19NOV10	01NOV10	05NOV10	-10d	0
SW2434	Rough Grade Roadway - Complete	5	29NOV10	03DEC10	20DEC10	24DEC10	15d	0
SW2436	Test, Inspect, Approve New Sanitary	5	29NOV10	03DEC10	29JUN11	05JUL11	152d	0
SW2440	Gravel and FG Roadway - Complete	5	13JUN11	17JUN11	04JUL11	08JUL11	15d	0
SW2442	Paving Binder Complete, Roadway	5	20JUN11	24JUN11	11JUL11	15JUL11	15d	0
SW2438	Remove Existing Sanitary System	8	22JUN11	01JUL11	06JUL11	15JUL11	10d	0
SW2444	Light Pole Bases	10	27JUN11	08JUL11	18JUL11	29JUL11	15d	0
EL14SW	UG Site Lighting, Parking and Roadway	10	04JUL11	15JUL11	25JUL11	05AUG11	15d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
SW2446	E/B Site Lighting, Parking and Roadway	10	04JUL11	15JUL11	25JUL11	05AUG11	15d	0
SW2448	Curbing, Parking and Roadway	15	18JUL11	05AUG11	08AUG11	26AUG11	15d	0
SW2450	Complete Rims, Inverts, Misc. Utilities, Roadway	10	08AUG11	19AUG11	03OCT11	14OCT11	40d	0
SW2452	Prep and Finish Paving, Roadway/Parking	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0
Sitework: Walks, Finishes, Landscaping								
SW4410	Prep/Grade Concrete Walkways, Roadway	10	08AUG11	19AUG11	29AUG11	09SEP11	15d	0
SW4412	Traffic Signage, Roadway	5	15AUG11	19AUG11	05SEP11	09SEP11	15d	0
MS20S	Site School Sign	5	22AUG11	26AUG11	17OCT11	21OCT11	40d	0
SL500	Concete Walkways, Roadway	10	05SEP11	16SEP11	05SEP11	16SEP11	0	0
SW4414	Spread Topsoil, Roadway	10	19SEP11	30SEP11	19SEP11	30SEP11	0	0
EL15SW	Site Lighting	10	19SEP11	30SEP11	03OCT11	14OCT11	10d	0
SW5410	Plantings, Roadway	5	03OCT11	07OCT11	03OCT11	07OCT11	0	0
SW5412	Chain Link Fence at Turnaround, Roadway	5	03OCT11	07OCT11	10OCT11	14OCT11	5d	0
SW5414	FG and Lawns, Roadway	5	17OCT11	21OCT11	10OCT11	14OCT11 *	-5d	0
Storage Building								
Foundations and Structure								
SW331SB	Excavate Found, Storage Bldg	0	27SEP10 A	28SEP10 A	27SEP10 A	28SEP10 A		100
FN10SB	Foundations, Storage Bldg	10	12OCT10	25OCT10	13DEC10	24DEC10	44d	0
SW332SB	Backfill, Grade, Storage Bldg	5	26OCT10	01NOV10	27DEC10	31DEC10	44d	0
SL10SB	Prep, Pour SOG, Storage Bldg	5	02NOV10	08NOV10	03JAN11	07JAN11	44d	0
MC10SB	CMU at Storage Bldg	10	09NOV10	22NOV10	10JAN11	21JAN11	44d	0
RC10SB	Ro Carpentry/Trusses/Framing, Storage Bldg	5	06DEC10	10DEC10	24JAN11	28JAN11	35d	0
Exterior/Closing-in								
RC20SB	Windows, Storage Bldg	2	13DEC10	14DEC10	03FEB11	04FEB11	38d	0
RF10SB	Roofing, Storage Bldg	5	13DEC10	17DEC10	31JAN11	04FEB11	35d	0
RC30SB	Siding and Trim, Storage Bldg	10	20DEC10	31DEC10	07FEB11	18FEB11	35d	0
OH10SB	OH Door, Storage Bldg	5	01FEB11	07FEB11	21FEB11	25FEB11	14d	0
Roughing-in								
EL12SB	Electric Rough, Storage Bldg	5	09NOV10	15NOV10	17JAN11	21JAN11	49d	0
Interior Finishes								
MM10SB	Bollards, Storage Bldg	5	08FEB11	14FEB11	26SEP11	30SEP11	164d	0
PA10SB	Painting, Storage Bldg	5	11JUL11	15JUL11	03OCT11	07OCT11	60d	0
EL20SB	Electric Finish, Inspect, Storage Bldg	5	18JUL11	22JUL11	10OCT11	14OCT11	60d	0
Completion								
ENDSB	Complete Storage Building	5	25JUL11	29JUL11	17OCT11	21OCT11	60d	0
Sitework - Leaching Field Area								
Sitework: Preparation								
SW1510	Excavate Site Conc. Retaining Wall	10	04OCT10 A	15OCT10	04OCT10 A	12NOV10	20d	0
FN50S	Site Concrete Retaining Wall	10	11OCT10	22OCT10	08NOV10	19NOV10	20d	0
SW1520	Backfill Site Conc. Retaining Wall	5	25OCT10	29OCT10	22NOV10	26NOV10	20d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Sitework: Utilities, Roadways, Paving								
SW2510	Leaching Field - Partial	10	01NOV10	12NOV10	29NOV10	10DEC10	20d	0
SW2512	Grade Leaching Area - Partial	5	15NOV10	19NOV10	13DEC10	17DEC10	20d	0
SW2514	Remove Existing Leaching Field	10	04JUL11	15JUL11	18JUL11	29JUL11	10d	0
SW2516	Leaching Field - Complete	15	18JUL11	05AUG11	01AUG11	19AUG11	10d	0
Sitework: Walks, Finishes, Landscaping								
SW4510	Complete Grading at Leaching	5	08AUG11	12AUG11	22AUG11	26AUG11	10d	0
SW5510	Chain Link Fence, Leaching	10	22AUG11	02SEP11	29AUG11	09SEP11	5d	0
SW4512	Spread Topsoil, Leaching	5	05SEP11	09SEP11	12SEP11	16SEP11	5d	0
SW5512	FG and Lawns, Leaching	5	12SEP11	16SEP11	19SEP11	23SEP11	5d	0
Sitework - Playfields Area								
Sitework: Walks, Finishes, Landscaping								
SW4610	Prep and Rough Grade, Field	10	23MAY11	03JUN11	23MAY11	03JUN11	0	0
SW4616	Remove/Distribute Loam Pile	5	06JUN11	10JUN11	06JUN11	10JUN11	0	0
SW4618	Prep and Grade Playground/BB	5	13JUN11	17JUN11	13JUN11	17JUN11	0	0
SW4620	Curbing at Playground/BB	5	20JUN11	24JUN11	20JUN11	24JUN11	0	0
SW4622	Prep/Fine Grade BB/Walk	5	27JUN11	01JUL11	04JUL11	08JUL11	5d	0
SW4516	1-5 Playground Equipment	15	27JUN11	15JUL11	27JUN11	15JUL11	0	0
SW4624	Pave Basketball Court and Walk	5	04JUL11	08JUL11	11JUL11	15JUL11	5d	0
SW5616	Basketball Court Striping	5	11JUL11	15JUL11	24OCT11	28OCT11	75d	0
SW5618	Resilient Play Surface	10	18JUL11	29JUL11	18JUL11	29JUL11	0	0
SW5620	Chain Link Fencing, Field	15	01AUG11	19AUG11	08AUG11	26AUG11	5d	0
SW5610	Players Benches, Field	5	22AUG11	26AUG11	05SEP11	09SEP11	10d	0
SW4614	Stone Dust Path, Field	5	29AUG11	02SEP11	12SEP11	16SEP11	10d	0
SW4612	Spread Topsoil, Field	10	05SEP11	16SEP11	29AUG11	09SEP11	-5d	0
SW5612	Skinned Infield, Field	5	19SEP11	23SEP11	12SEP11	16SEP11	-5d	0
SW5614	FG and Lawns, Field	5	26SEP11	30SEP11	19SEP11	23SEP11	-5d	0
SW5624	Playfield Equipment (Bases, etc.)	5	26SEP11	30SEP11	24OCT11	28OCT11	20d	0
Phase 1								
Completion								
ENDSW	Complete Finish Sitework	10	07NOV11	18NOV11	31OCT11	11NOV11 *	-5d	0
New Addition - Area B and C								
New Addition - Area B and C								
Foundations and Structure								
SW3310C	Excavate Foundations, Area B/C	0	16AUG10 A	07SEP10 A	16AUG10 A	07SEP10 A		100
FN10C	Foundations Area B/C	5	26AUG10 A	08OCT10	26AUG10 A	01OCT10	-5d	83
FN20C	Interior Footings, Piers, Area B/C	2	08SEP10 A	05OCT10	08SEP10 A	28SEP10	-5d	85
PL10C	Plumbing Underslab Storm Drain at B	0	13SEP10 A	14SEP10 A	13SEP10 A	14SEP10 A		100
SW3320C	Perim Insul/Backfill Foundations, Area B/C	6	20SEP10 A	11OCT10	20SEP10 A	13OCT10	2d	60

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
SW3330C	E/B for US Utilities, Area B/C	15	29SEP10 A	22OCT10	29SEP10 A	15OCT10	-5d	0
PL11C	Underslab Plumbing, Area B/C	15	04OCT10	22OCT10	27SEP10	15OCT10	-5d	0
WP10C	Waterproofing, Area B/C	15	04OCT10	22OCT10	27SEP10	15OCT10	-5d	0
FN30C	Grout Baseplates, Area B/C	10	06OCT10	19OCT10	11OCT10	22OCT10	3d	0
EL10C	Underslab Electric, Area B/C	10	11OCT10	22OCT10	11OCT10	22OCT10	0	0
SW3340C	BF, Grade SOG, Area B/C	10	25OCT10	05NOV10	18OCT10	29OCT10	-5d	0
SL10C	Prep & Pour Slab-on-Grade, Area B/C	10	01NOV10	12NOV10	25OCT10	05NOV10	-5d	0
ST10C	Steel Erection - Area B/C	40	22NOV10	14JAN11	08NOV10	31DEC10	-10d	0
MM30C	Tube Steel Supoort, Area B/C	5	17JAN11	21JAN11	17JAN11	21JAN11	0	0
MM20C	Angle at Roof Overhang, Area B/C	10	17JAN11	28JAN11	31JAN11	11FEB11	10d	0
MM10C	Deliver Loose Lintels	10	17JAN11	28JAN11	21FEB11	04MAR11	25d	0
RC605	Set HM Frames at CMU, Area B/C	20	07MAR11	01APR11	28FEB11	25MAR11	-5d	0
MC10C	CMU Back-up, Area B/C	15	14MAR11	01APR11	07MAR11	25MAR11	-5d	0
MC207	CMU at Boiler/Mech/Receiving Area	20	04APR11	29APR11	28MAR11	22APR11	-5d	0
MM107	Seismic Clips at CMU, Area B/C	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
MC205	CMU at Art Area, Area B/C	10	09MAY11	20MAY11	02MAY11	13MAY11	-5d	0
MC306	CMU at B, Near Existing, Area B/C	10	09MAY11	20MAY11	02MAY11	13MAY11	-5d	0
Exterior/Closing-in								
PL20C	Roof Drains, Area B/C	10	03JAN11	14JAN11	17JAN11	28JAN11	10d	0
RC10C	Roof Blocking at High Roofs, Area B/C	10	03JAN11	14JAN11	17JAN11	28JAN11	10d	0
RF10C	High Roof System, Area B/C	10	17JAN11	28JAN11	31JAN11	11FEB11	10d	0
DW10C	Ext. Studs/Sheath/Blkg Above Roofs, Area B/C	20	17JAN11	11FEB11	03JAN11	28JAN11	-10d	0
RF20C	Deliver Thru-Wall Flashings, Area B/C	5	24JAN11	28JAN11	31JAN11	04FEB11	5d	0
RC20C	Roof Blocking at Low Roofs, Area B/C	10	31JAN11	11FEB11	14FEB11	25FEB11	10d	0
DW11C	Complete Ext Studs/Sheath/Blkg, Area B/C	25	07FEB11	11MAR11	24JAN11	25FEB11	-10d	0
HV10C	Set Roof Curbs, etc., Area B/C	5	14FEB11	18FEB11	28FEB11	04MAR11	10d	0
AB10C	Air Barrier at Walls Above Low Roofs, Area B/C	10	14FEB11	25FEB11	07FEB11	18FEB11	-5d	0
MV10C	Masonry Veneer at Roofs, Area B/C	15	28FEB11	18MAR11	21FEB11	11MAR11	-5d	0
RF11C	Low Roof above Lobby, Area B/C	10	07MAR11	18MAR11	07MAR11	18MAR11	0	0
RF12C	Low Roof above Mech/Kitch, Area B/C	10	14MAR11	25MAR11	07MAR11	18MAR11	-5d	0
AB20C	Air Membrane Barriers, Area B/C	25	14MAR11	15APR11	28FEB11	01APR11	-10d	0
RC50C	Temp. Access Doors EX-C156, Area B/C	5	21MAR11	25MAR11	02MAY11	06MAY11	30d	0
WN30C	Sloped Glazing Assembly, Area B/C	10	21MAR11	01APR11	21MAR11	01APR11	0	0
MV11C	Masonry Veneer, Area B/C	30	21MAR11	29APR11	07MAR11	15APR11	-10d	0
RF30C	Roof Hatch, Area B/C	5	28MAR11	01APR11	18APR11	22APR11	15d	0
MM50C	Roof Ladder, Area B/C	5	28MAR11	01APR11	04JUL11	08JUL11	70d	0

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
HV11C	Set Roof Top Equip., Area B/C	10	28MAR11	08APR11	11APR11	22APR11	10d	0
WN10C	Wind/CW/SF at Gym/Cafe, Area B/C	20	11APR11	06MAY11	28MAR11	22APR11	-10d	0
MP10C	Composite Wall Panels, Area B/C	30	02MAY11	10JUN11	09MAY11	17JUN11	5d	0
WN11C	Wind/CW/SF at Media, Area B/C	10	09MAY11	20MAY11	25APR11	06MAY11	-10d	0
WN12C	Wind/CW/SF at Lobby West, Area B/C	10	09MAY11	20MAY11	09MAY11	20MAY11	0	0
WN13C	Wind/CW/SF at Admin/Lobb East, Area B/C	15	23MAY11	10JUN11	23MAY11	10JUN11	0	0
MP11C	Comp. Wall Panel at Slope Glazing, Area B/C	10	13JUN11	24JUN11	27JUN11	08JUL11	10d	0
MP20C	Acoustic Equip Screen (Roof), Area B/C	10	13JUN11	24JUN11	27JUN11	08JUL11	10d	0
RF40C	Complete Fascia and Roof Metal, Area B/C	15	13JUN11	01JUL11	20JUN11	08JUL11	5d	0
WN20C	Complete Alum. Entrances, Area B/C	15	13JUN11	01JUL11	04JUL11	22JUL11	15d	0
WP30C	Exterior Sealants, Area B/C	25	13JUN11	15JUL11	20JUN11	22JUL11	5d	0
RF50C	Misc. Roofing, Area B/C	10	04JUL11	15JUL11	11JUL11	22JUL11	5d	0
RC60C	Remove Temp Access - Door EX-C156, Area B/C	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
Gymnasium - Cafeteria Area								
Roughing-in								
HV203	Rough Ductwork Mains, Gym/Café	20	31JAN11	25FEB11	21FEB11	18MAR11	15d	0
PL303	Plumbing - Rough & Test, Gym/Café	20	31JAN11	25FEB11	07MAR11	01APR11	25d	0
EL203	Electric - Rough Mains, Risers, Gym/Café	25	31JAN11	04MAR11	14FEB11	18MAR11	10d	0
HV303	Rough HVAC Piping, Gym/Café	20	14FEB11	11MAR11	14MAR11	08APR11	20d	0
PL313	Plumbing - Rough Inspect, Gym/Cafe	5	28FEB11	04MAR11	04APR11	08APR11	25d	0
FP203	Fire Protection - Rough & Test, Gym/Café	25	28FEB11	01APR11	04APR11	06MAY11	25d	0
DW203	Interior Metal Stud Framing, Gym/Café	20	07MAR11	01APR11	21MAR11	15APR11	10d	0
EL303	Electric - Rough Ptns & Complete, Gym/Café	20	14MAR11	08APR11	28MAR11	22APR11	10d	0
RC403	Interior Rough Carpentry, Gym/Café	20	21MAR11	15APR11	11APR11	06MAY11	15d	0
HV413	Controls - Roughing-in, Gym/Café	25	21MAR11	22APR11	04APR11	06MAY11	10d	0
TC303	Telecommunications Rough, Gym/Café	25	21MAR11	22APR11	04APR11	06MAY11	10d	0
HV213	Complete Rough Ductwork, Gym/Café	15	28MAR11	15APR11	18APR11	06MAY11	15d	0
HV503	HVAC Pipe Insulation, Gym/Café	20	28MAR11	22APR11	11APR11	06MAY11	10d	0
PL403	Plumbing - Pipe Covering, Gym/Café	20	28MAR11	22APR11	11APR11	06MAY11	10d	0
EL403	Electric - Inspect Rough-in, Gym/Café	10	11APR11	22APR11	25APR11	06MAY11	10d	0
Interior Finishes								
DW303	Drywall, Tape & Sand, Gym/Café	25	09MAY11	10JUN11	09MAY11	10JUN11	0	0
PA103	Prime Paint, Gym/Café	15	30MAY11	17JUN11	30MAY11	17JUN11	0	0
AP103	Sound Wall Panels, Gym/Cafe	10	13JUN11	24JUN11	13JUN11	24JUN11	0	0
FS103	Firestopping, Gym/Café	10	13JUN11	24JUN11	25JUL11	05AUG11	30d	0
MM103	Unistrut Proj. Support, Gym/Cafe	5	20JUN11	24JUN11	18JUL11	22JUL11	20d	0
DW403	Touch-up Drywall, Gym/Café	10	20JUN11	01JUL11	20JUN11	01JUL11	0	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
WP203	Interior Caulking, Gym/Café	10	20JUN11	01JUL11	25JUL11	05AUG11	25d	0
CL103	Ceiling Grid, Gym/Café	15	20JUN11	08JUL11	04JUL11	22JUL11	10d	0
HV703	HVAC Radiation, Gym/Café	15	20JUN11	08JUL11	04JUL11	22JUL11	10d	0
FC103	Finish Millwork, Panelling, Gym/Cafe	30	27JUN11	05AUG11	27JUN11	05AUG11	0	0
PA303	Finish Paint Exposed Struct, Gym	10	04JUL11	15JUL11	04JUL11	15JUL11	0	0
FC203	Hang Interior Doors, Gym/Café	5	11JUL11	15JUL11	26SEP11	30SEP11	55d	0
HV803	ATC Controls - Finish, Gym/Café	10	11JUL11	22JUL11	25JUL11	05AUG11	10d	0
FP403	Fire Protection - Finish Heads, Gym/Café	15	11JUL11	29JUL11	05SEP11	23SEP11	40d	0
HV723	Reg, Grilles, Fans, Finishes, Gym/Café	15	11JUL11	29JUL11	05SEP11	23SEP11	40d	0
EL703	Lighting Fixtures, Gym/Café	20	11JUL11	05AUG11	29AUG11	23SEP11	35d	0
MS503	Projection Screens, Gym/Cafe	5	18JUL11	22JUL11	01AUG11	05AUG11	10d	0
GE103	Gym Backboards, Gym/Café	10	18JUL11	29JUL11	18JUL11	29JUL11	0	0
DW503	Misc. Interior Drywall, Gym/Café	10	18JUL11	29JUL11	25JUL11	05AUG11	5d	0
EL803	Scoreboard, Gym/Café	5	01AUG11	05AUG11	01AUG11	05AUG11	0	0
PA203	Complete Finish Paint Walls & Ceilings, Gym/Café	15	01AUG11	19AUG11	08AUG11	26AUG11	5d	0
MM203	Metal Rails, Gym/Cafe	10	08AUG11	19AUG11	19SEP11	30SEP11	30d	0
WF103	Wood Floor & Base, Gym/Café	20	08AUG11	02SEP11	08AUG11	02SEP11	0	0
EL813	Electric Finishes, Gym/Café	15	22AUG11	09SEP11	29AUG11	16SEP11	5d	0
MS103	Miscellaneous Specialties, Gym/Café	15	22AUG11	09SEP11	26SEP11	14OCT11	25d	0
TC803	Telecommunications Finish, Gym/Café	15	29AUG11	16SEP11	05SEP11	23SEP11	5d	0
FC113	Complete Finish Millwork, Gym/Cafe	10	05SEP11	16SEP11	19SEP11	30SEP11	10d	0
OP103	Operable Partition, Gym/Cafe	10	05SEP11	16SEP11	19SEP11	30SEP11	10d	0
WF203	Wood Floor at Stage, Gym/Café	10	05SEP11	16SEP11	19SEP11	30SEP11	10d	0
CT103	Porcelain Tile, Gym/Café	15	05SEP11	23SEP11	05SEP11	23SEP11	0	0
BL103	Gym Bleachers & Equipment	15	05SEP11	23SEP11	26SEP11	14OCT11	15d	0
GE113	Gym Wall Pads, Divider, & Equipment	20	05SEP11	30SEP11	19SEP11	14OCT11	10d	0
EP103	Resinous Floor, Gym/Cafe	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
RS103	VCT, Gym/Cafe	5	19SEP11	23SEP11	03OCT11	07OCT11	10d	0
CL203	Ceiling Tile, Gym/Café	15	19SEP11	07OCT11	26SEP11	14OCT11	5d	0
PL703	Plumbing Finish, Gym/Café	5	26SEP11	30SEP11	26SEP11	30SEP11	0	0
FC213	Complete Finish Hardware, Gym/Café	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
PA503	Paint at Corridors, Gym/Café	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
RS403	Vinyl Base, Gym/Café	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
PA603	Misc. Painting, Gym/Café	10	03OCT11	14OCT11	03OCT11	14OCT11	0	0
Completion								
ENDG	Complete Gym/Café	5	17OCT11	21OCT11	17OCT11	21OCT11	0	0
Kitchen								

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
Foundations and Structure								
MC104	CMU at Kitchen	5	02MAY11	06MAY11	25APR11	29APR11	-5d	0
Roughing-in								
HV204	Rough Ductwork, Kitch	15	28MAR11	15APR11	21MAR11	08APR11	-5d	0
EL204	Electric - Rough Mains, Risers; Kitch	15	28MAR11	15APR11	25APR11	13MAY11	20d	0
HV304	Rough HVAC Piping, Kitch	15	11APR11	29APR11	04APR11	22APR11	-5d	0
FP204	Fire Protection - Rough & Test, Kitch	15	11APR11	29APR11	23MAY11	10JUN11	30d	0
HV504	HVAC Pipe Insulation, Kitch	15	02MAY11	20MAY11	23MAY11	10JUN11	15d	0
PL304	Plumbing - Rough & Test, Kitch	20	02MAY11	27MAY11	25APR11	20MAY11	-5d	0
DW204	Interior Metal Stud Framing, Kitch	15	09MAY11	27MAY11	09MAY11	27MAY11	0	0
EL304	Electric - Rough Ptns & Complete, Kitch	15	16MAY11	03JUN11	16MAY11	03JUN11	0	0
HV404	Controls - Roughing-in, Kitch	10	23MAY11	03JUN11	30MAY11	10JUN11	5d	0
RC404	Interior Rough Carpentry, Kitch	10	23MAY11	03JUN11	30MAY11	10JUN11	5d	0
TC304	Telecommunications Rough, Kitch	10	23MAY11	03JUN11	30MAY11	10JUN11	5d	0
PL314	Plumbing - Rough Inspect, Kitch	5	30MAY11	03JUN11	23MAY11	27MAY11	-5d	0
EL404	Electric - Inspect Rough-in, Kitch	5	06JUN11	10JUN11	06JUN11	10JUN11	0	0
PL404	Plumbing - Pipe Covering, Kitch	10	06JUN11	17JUN11	30MAY11	10JUN11	-5d	0
PL324	Plumbing - Gas Piping, Kitch	5	25JUL11	29JUL11	01AUG11	05AUG11	5d	0
Interior Finishes								
KN104	Set Cooler/Freezer, Kitch	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
DW304	Drywall, Tape & Sand, Kitch	10	20JUN11	01JUL11	13JUN11	24JUN11	-5d	0
PA114	Prime Paint, Kitch	5	04JUL11	08JUL11	27JUN11	01JUL11	-5d	0
FS104	Firestopping, Kitch	10	04JUL11	15JUL11	11JUL11	22JUL11	5d	0
CL104	Ceiling Grid, Kitch	10	11JUL11	22JUL11	04JUL11	15JUL11	-5d	0
DW404	Touch-up Drywall, Kitch	10	11JUL11	22JUL11	04JUL11	15JUL11	-5d	0
WP204	Interior Caulking, Kithch	10	11JUL11	22JUL11	11JUL11	22JUL11	0	0
HV704	HVAC Radiation, Kitch	15	11JUL11	29JUL11	04JUL11	22JUL11	-5d	0
DW504	Misc. Interior Drywall, Kitch	10	25JUL11	05AUG11	18JUL11	29JUL11	-5d	0
CT104	Ceramic Tile, Kitch	10	25JUL11	05AUG11	25JUL11	05AUG11	0	0
HV714	Set/Connect CUH's, misc., Kitch	10	25JUL11	05AUG11	12SEP11	23SEP11	35d	0
MS104	FRP Walls, Kitch	15	25JUL11	12AUG11	18JUL11	05AUG11	-5d	0
EL704	Lighting Fixtures, Kitch	15	25JUL11	12AUG11	25JUL11	12AUG11	0	0
FP404	Fire Protection - Finish Heads, Kitch	15	25JUL11	12AUG11	25JUL11	12AUG11	0	0
HV724	Reg, Grilles, Fans, Finishes, Kitch	15	25JUL11	12AUG11	25JUL11	12AUG11	0	0
PA204	Finish Paint Walls & Ceilings, Kitch	10	01AUG11	12AUG11	25JUL11	05AUG11	-5d	0
HV804	ATC Controls - Finish, Kitch	15	01AUG11	19AUG11	05SEP11	23SEP11	25d	0
CT204	Porcelain Floor/Base, Kitch	5	15AUG11	19AUG11	08AUG11	12AUG11	-5d	0

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
FC204	Hang Interior Doors, Kitch	10	15AUG11	26AUG11	26SEP11	07OCT11	30d	0
RS104	VCT and Base, Kitch	10	15AUG11	26AUG11	03OCT11	14OCT11	35d	0
EL814	Electric Finishes, Kitch	15	15AUG11	02SEP11	19SEP11	07OCT11	25d	0
CL204	Ceiling Tile, Kitch	10	22AUG11	02SEP11	26SEP11	07OCT11	25d	0
EP104	Resinous Floor at Kitchen	15	22AUG11	09SEP11	15AUG11	02SEP11	-5d	0
TC804	Telecommunications Finish, Kitch	10	29AUG11	09SEP11	03OCT11	14OCT11	25d	0
FC214	Complete Finish Hardware, Kitch	5	12SEP11	16SEP11	10OCT11	14OCT11	20d	0
KN204	Set Kitchen Equipment, Kitch	10	12SEP11	23SEP11	05SEP11	16SEP11	-5d	0
EL804	Kitchen Equipment - Electric Connections	20	19SEP11	14OCT11	12SEP11	07OCT11	-5d	0
PL704	Kitchen Equipment - Plumbing Connections	20	19SEP11	14OCT11	12SEP11	07OCT11	-5d	0
LK104	Lockers, Kitch	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
PA604	Misc. Painting, Kitch	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
KN304	Start-up at Kitchen	10	17OCT11	28OCT11	10OCT11	21OCT11	-5d	0
Completion								
ENDK	Complete Kitchen	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0
Media Center, Art Rooms								
Roughing-in								
HV205	Rough Ductwork Mains, Media/Art	10	21MAR11	01APR11	21MAR11	01APR11	0	0
PL305	Plumbing - Rough & Test, Media/Art	15	28MAR11	15APR11	28MAR11	15APR11	0	0
EL205	Electric - Rough Mains, Risers; Media/Art	15	04APR11	22APR11	04APR11	22APR11	0	0
HV305	Rough HVAC Piping, Media/Art	15	04APR11	22APR11	04APR11	22APR11	0	0
HV215	Complete Rough Ductwork, Media/Art	15	04APR11	22APR11	25APR11	13MAY11	15d	0
DW205	Interior Metal Stud Framing, Media/Art	20	11APR11	06MAY11	11APR11	06MAY11	0	0
FP205	Fire Protection - Rough & Test, Media/Art	20	11APR11	06MAY11	18APR11	13MAY11	5d	0
PL315	Plumbing - Rough Inspect, Media/Art	5	18APR11	22APR11	18APR11	22APR11	0	0
EL305	Electric - Rough Ptns & Complete, Media/Art	15	18APR11	06MAY11	18APR11	06MAY11	0	0
HV405	Controls - Roughing-in, Media/Art	15	25APR11	13MAY11	25APR11	13MAY11	0	0
HV505	HVAC Pipe Insulation, Media/Art	15	25APR11	13MAY11	25APR11	13MAY11	0	0
PL405	Plumbing - Pipe Covering, Media/Art	15	25APR11	13MAY11	25APR11	13MAY11	0	0
RC415	Interior Rough Carpentry, Media/Art	15	25APR11	13MAY11	25APR11	13MAY11	0	0
TC305	Telecommunications Rough, Media/Art	15	25APR11	13MAY11	25APR11	13MAY11	0	0
EL405	Electric - Inspect Rough-in, Media/Art	5	09MAY11	13MAY11	09MAY11	13MAY11	0	0
Interior Finishes								
DW305	Drywall, Tape & Sand, Media/Art	20	23MAY11	17JUN11	16MAY11	10JUN11	-5d	0
PA105	Prime Paint, Media/Art	15	13JUN11	01JUL11	13JUN11	01JUL11	0	0
FS105	Firestopping, Media/Art	15	20JUN11	08JUL11	01AUG11	19AUG11	30d	0
DW405	Touch-up Drywall, Media/Art	10	04JUL11	15JUL11	08AUG11	19AUG11	25d	0
CL105	Ceiling Grid, Media/Art	15	04JUL11	22JUL11	04JUL11	22JUL11	0	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
HV705	HVAC Radiation, Media/Art	15	04JUL11	22JUL11	18JUL11	05AUG11	10d	0
CT105	Ceramic Tile Toilets, Media/Art	15	04JUL11	22JUL11	01AUG11	19AUG11	20d	0
WP205	Interior Caulking, Media/Art	15	04JUL11	22JUL11	01AUG11	19AUG11	20d	0
DW505	Misc. Interior Drywall, Media/Art	10	25JUL11	05AUG11	22AUG11	02SEP11	20d	0
FC105	Finish Millwork, Media/Art	15	25JUL11	12AUG11	25JUL11	12AUG11	0	0
FC205	Hang Interior Doors, Media/Art	15	25JUL11	12AUG11	08AUG11	26AUG11	10d	0
HV805	ATC Controls - Finish, Media/Art	15	25JUL11	12AUG11	08AUG11	26AUG11	10d	0
PL705	Plumbing Finish, Media/Art	15	25JUL11	12AUG11	22AUG11	09SEP11	20d	0
CW105	Fixed Casework, Media/Art	15	25JUL11	12AUG11	05SEP11	23SEP11	30d	0
EL705	Lighting Fixtures, Media/Art	15	25JUL11	12AUG11	05SEP11	23SEP11	30d	0
FP405	Fire Protection - Finish Heads, Media/Art	15	25JUL11	12AUG11	05SEP11	23SEP11	30d	0
HV715	Reg, Grilles, Finishes, Media/Art	15	25JUL11	12AUG11	05SEP11	23SEP11	30d	0
CB105	MB/TB, Media/Art	5	15AUG11	19AUG11	15AUG11	19AUG11	0	0
TP105	Toilet Compartments, Media/Art	10	15AUG11	26AUG11	12SEP11	23SEP11	20d	0
CL205	Ceiling Tile, Media/Art	10	15AUG11	26AUG11	26SEP11	07OCT11	30d	0
RS105	VCT, Media/Art	15	15AUG11	02SEP11	29AUG11	16SEP11	10d	0
PA205	Finish Paint Walls & Ceilings, Media/Art	15	22AUG11	09SEP11	22AUG11	09SEP11	0	0
TA105	Toilet Accessories, Media/Art	10	29AUG11	09SEP11	26SEP11	07OCT11	20d	0
CP105	Carpet, Media/Art	5	05SEP11	09SEP11	19SEP11	23SEP11	10d	0
FC215	Complete Finish Hardware, Media/Art	15	05SEP11	23SEP11	19SEP11	07OCT11	10d	0
AP105	Sound Wall Panels, Media	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
MS105	Miscellaneous Specialties, Media/Art	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
PA605	Misc. Painting, Media/Art	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
RS405	Vinyl Base, Media/Art	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
EL805	Electric Finishes, Media/Art	15	12SEP11	30SEP11	12SEP11	30SEP11	0	0
TC805	Telecommunications Finish, Media/Art	15	19SEP11	07OCT11	19SEP11	07OCT11	0	0
Completion								
ENDM	Complete Media/Art	5	10OCT11	14OCT11	10OCT11	14OCT11	0	0
Main Entrance, Lobby, Administration								
Roughing-in								
HV206	Rough Ductwork, Lobby/Admin	15	04APR11	22APR11	04APR11	22APR11	0	0
HV306	Rough HVAC Piping, Lobby/Admin	15	11APR11	29APR11	11APR11	29APR11	0	0
FP206	Fire Protection - Rough & Test, Lobby/Admin	15	11APR11	29APR11	23MAY11	10JUN11	30d	0
EL206	Electric - Rough Mains, Risers, Lobby/Admin	15	25APR11	13MAY11	25APR11	13MAY11	0	0
PL306	Plumbing - Rough & Test, Lobby/Admin	15	02MAY11	20MAY11	02MAY11	20MAY11	0	0
HV506	HVAC Pipe Insulation, Lobby/Admin	15	02MAY11	20MAY11	23MAY11	10JUN11	15d	0
DW206	Interior Metal Stud Framing, Lobby/Admin	15	09MAY11	27MAY11	09MAY11	27MAY11	0	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
PL316	Plumbing - Rough Inspect, Lobby/Admin	5	23MAY11	27MAY11	23MAY11	27MAY11	0	0
HV406	Controls - Roughing-in, Lobby/Admin	10	23MAY11	03JUN11	30MAY11	10JUN11	5d	0
RC406	Interior Rough Carpentry, Lobby/Admin	10	23MAY11	03JUN11	30MAY11	10JUN11	5d	0
EL306	Electric - Rough Ptns & Complete, Lobby/Admin	15	23MAY11	10JUN11	16MAY11	03JUN11	-5d	0
TC306	Telecommunications Rough, Lobby/Admin	15	23MAY11	10JUN11	23MAY11	10JUN11	0	0
PL406	Plumbing - Pipe Covering, Lobby/Admin	10	30MAY11	10JUN11	30MAY11	10JUN11	0	0
EL406	Electric - Inspect Rough-in, Lobby/Admin	5	13JUN11	17JUN11	06JUN11	10JUN11	-5d	0
Interior Finishes								
DW306	Drywall, Tape & Sand, Lobby/Admin	15	20JUN11	08JUL11	13JUN11	01JUL11	-5d	0
PA106	Prime Paint, Lobby/Admin	10	11JUL11	22JUL11	04JUL11	15JUL11	-5d	0
CW106	Fixed Casework, Lobby/Admin	5	25JUL11	29JUL11	08AUG11	12AUG11	10d	0
CL106	Ceiling Grid, Lobby/Admin	10	25JUL11	05AUG11	25JUL11	05AUG11	0	0
CT106	Wall Tile, Lobby/Admin	20	25JUL11	19AUG11	18JUL11	12AUG11	-5d	0
FC106	Finish Millwork, Lobby/Admin	25	25JUL11	26AUG11	25JUL11	26AUG11	0	0
CB106	MB/TB, Display Cases, Lobby/Admin	5	08AUG11	12AUG11	08AUG11	12AUG11	0	0
EL606	Lighting Fixtures, Lobby/Admin	10	08AUG11	19AUG11	22AUG11	02SEP11	10d	0
FP406	Fire Protection - Finish, Lobby/Admin	10	08AUG11	19AUG11	22AUG11	02SEP11	10d	0
HV706	HVAC Finish, Lobby/Admin	15	08AUG11	26AUG11	15AUG11	02SEP11	5d	0
MM106	Metal Handrails, Lobby/Admin	10	22AUG11	02SEP11	05SEP11	16SEP11.	10d	0
CT206	Porcelain Floor, Lobby/Admin	15	22AUG11	09SEP11	15AUG11	02SEP11	-5d	0
EL706	Electric Finish, Lobby/Admin	15	22AUG11	09SEP11	15AUG11	02SEP11	-5d	0
TC806	Telecommunications Finish, Lobby/Admin	15	22AUG11	09SEP11	15AUG11	02SEP11	-5d	0
CP106	Carpet, Lobby/Adim	10	12SEP11	23SEP11	05SEP11	16SEP11	-5d	0
RS406	Vinyl Base, Lobby/Admin	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
PA206	Complete Finish Paint, Lobby/Admin	10	26SEP11	07OCT11	19SEP11	30SEP11	-5d	0
CL206	Ceiling Tile, Lobby/Admin	10	10OCT11	21OCT11	03OCT11	14OCT11	-5d	0
Completion								
ENDL	Complete Lobby/Admin	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0
Mechanical and Electrical Rooms								
Foundations and Structure								
SL107	Concrete Equipment Pads	5	02MAY11	06MAY11	02MAY11	06MAY11	0	0
Roughing-in								
FP107	Fire Protection - Set Pump in Pit	5	02MAY11	06MAY11	02MAY11	06MAY11	0	0
LV107	Louver, Mech/Elect.	5	02MAY11	06MAY11	11JUL11	15JUL11	50d	0
EL507	Switchgear - Set & Connect	20	02MAY11	27MAY11	27JUN11	22JUL11	40d	0
HV607	HVAC Boiler Room & Mechanical Room	40	02MAY11	24JUN11	25APR11	17JUN11	-5d	0
PL507	Plumbing - at Fire Pump Pit	15	09MAY11	27MAY11	09MAY11	27MAY11	0	0
FP217	Fire Protection - at Fire Pump Pit	15	09MAY11	27MAY11	30MAY11	17JUN11	15d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
PL607	Plumbing - Boiler Room Piping	25	06JUN11	08JUL11	30MAY11	01JUL11	-5d	0
FP207	Fire Protection, Mech/Elect	20	13JUN11	08JUL11	20JUN11	15JUL11	5d	0
PL617	Plumbing - Set & Connect Water Heater	15	20JUN11	08JUL11	13JUN11	01JUL11	-5d	0
HV617	Breaching and Chimney Flue	10	27JUN11	08JUL11	01AUG11	12AUG11	25d	0
EL517	Electric Connections at Mech Equipment	15	27JUN11	15JUL11	27JUN11	15JUL11	0	0
PL627	Plumbing - Gas Piping, Mech/Elect	10	11JUL11	22JUL11	04JUL11	15JUL11	-5d	0
PL309	Plumbing - Gas Piping to Roof Units	5	25JUL11	29JUL11	01AUG11	05AUG11	5d	0
HV627	Complete HVAC at Boiler & Mech Room	20	25JUL11	19AUG11	18JUL11	12AUG11	-5d	0
Interior Finishes								
MM207	Roof Access Treads, Mech	5	02MAY11	06MAY11	11JUL11	15JUL11	50d	0
EL907	Activate Permanent Power	15	06JUN11	24JUN11	25JUL11	12AUG11	35d	0
PA107	Prime Paint, Mech/Elect	10	04JUL11	15JUL11	04JUL11	15JUL11	0	0
FP507	Fire Protection - Compl, Test, Inspect Fire Pump	5	11JUL11	15JUL11	03OCT11	07OCT11	60d	0
PA207	Finish Paint, Mech/Elect	10	22AUG11	02SEP11	19SEP11	30SEP11	20d	0
HV907	HVAC Start-up & Test	20	22AUG11	16SEP11	15AUG11	09SEP11	-5d	0
PA507	Sealed Concrete Floor, Mech/Elect	5	05SEP11	09SEP11	03OCT11	07OCT11	20d	0
EL807	Electric Finishes, Mech/Elect	10	12SEP11	23SEP11	10OCT11	21OCT11	20d	0
HV917	Permanent Systems Operational	5	19SEP11	23SEP11	19SEP11	23SEP11	0	0
HV927	HVAC Balancing	20	03OCT11	28OCT11	26SEP11	21OCT11	-5d	0
New Addition - Area D								
New Addition - Area D								
Foundations and Structure								
SW3310D	Excavate Foundations, Area D	0	08SEP10 A	16SEP10 A	08SEP10 A	16SEP10 A		100
FN10D	Foundations - Area D	2	08SEP10 A	05OCT10	08SEP10 A	28SEP10	-5d	90
SW3320D	Footing Drain, Area D	3	17SEP10 A	06OCT10	17SEP10 A	29SEP10	-5d	70
FN20D	Interior Footings, Piers, Area D	2	23SEP10 A	05OCT10	23SEP10 A	28SEP10	-5d	90
EL10D	Underslab Electric, Area D	10	04OCT10	15OCT10	27SEP10	08OCT10	-5d	0
PL10D	Underslab Plumbing, Area D	10	04OCT10	15OCT10	27SEP10	08OCT10	-5d	0
SW3330D	E/B for US Utilities, Area D	10	04OCT10	15OCT10	27SEP10	08OCT10	-5d	0
SW3340D	Perim Insul/Backfill Foundations, Area D	15	04OCT10	22OCT10	27SEP10	15OCT10	-5d	0
WP10D	Waterproofing, Area D	15	04OCT10	22OCT10	27SEP10	15OCT10	-5d	0
FN30D	Grout Baseplates, Area D	10	07OCT10	20OCT10	11OCT10	22OCT10	2d	0
SW3350D	BF, Partial Grade SOG, Area D	10	18OCT10	29OCT10	11OCT10	22OCT10	-5d	0
SL10D	Prep & Pour Slab-on-Grade, Area D	10	01NOV10	12NOV10	25OCT10	05NOV10	-5d	0
ST10D	Steel Erection - Area D	30	10JAN11	18FEB11	27DEC10	04FEB11	-10d	0
SL20D	Slabs-on-Deck, Area D	15	07FEB11	25FEB11	31JAN11	18FEB11	-5d	0
Exterior/Closing-in								
DW10D	Ext. Studs/Sheath/Blkg Above Roofs, Part D	10	21FEB11	04MAR11	07FEB11	18FEB11	-10d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
PL20D	Roof Drains, Area D	10	21FEB11	04MAR11	14FEB11	25FEB11	-5d	0
RC10D	Roof Blocking at High Roofs, Area D	10	21FEB11	04MAR11	14FEB11	25FEB11	-5d	0
HV10D	Set Roof Curbs, etc., Area D	5	28FEB11	04MAR11	21FEB11	25FEB11	-5d	0
RF30D	Deliver Thru-Wall Flashings, Area D	5	28FEB11	04MAR11	07MAR11	11MAR11	5d	0
AB10D	Air Barrier at Walls Above Low Roofs, Area D	10	07MAR11	18MAR11	28FEB11	11MAR11	-5d	0
RC20D	Roof Blocking at Low Roofs, Area D	10	07MAR11	18MAR11	28MAR11	08APR11	15d	0
RF10D	High Roof System, Area D	15	07MAR11	25MAR11	28FEB11	18MAR11	-5d	0
DW11D	Complete Ext Studs/Sheath/Blkg, Area D	25	07MAR11	08APR11	21FEB11	25MAR11	-10d	0
MV10D	Masonry Veneer at Roofs, Area D	10	21MAR11	01APR11	14MAR11	25MAR11	-5d	0
RF20D	Roof Hatch, Area D	5	28MAR11	01APR11	11APR11	15APR11	10d	0
SK10D	Unit Skylight, Area D	5	28MAR11	01APR11	11APR11	15APR11	10d	0
RF22D	Elevator Vent, Area D	5	28MAR11	01APR11	02MAY11	06MAY11	25d	0
RF21D	Roof Davit, Area D	5	28MAR11	01APR11	25JUL11	29JUL11	85d	0
AB20D	Air Membrane Barriers, Area D	25	28MAR11	29APR11	14MAR11	15APR11	-10d	0
RC50D	Temp Access Doors EX-D184, Area D	5	04APR11	08APR11	09MAY11	13MAY11	25d	0
RF11D	Low Roof System, Area D	10	04APR11	15APR11	11APR11	22APR11	5d	0
MV11D	Masonry Veneer, Area D	30	11APR11	20MAY11	28MAR11	06MAY11	-10d	0
HV11D	Set Roof Top Equip., Area D	10	18APR11	29APR11	02MAY11	13MAY11	10d	0
WN10D	Wind/CW/SF, Area D	20	02MAY11	27MAY11	18APR11	13MAY11	-10d	0
WN11D	Wind/CW/SF at Stair C122, Area D	5	23MAY11	27MAY11	09MAY11	13MAY11	-10d	0
MP10D	Composite Wall Panels, Area D	30	23MAY11	01JUL11	16MAY11	24JUN11	-5d	0
MP30D	Metal Wall Panels (Roof), Area D	15	04JUL11	22JUL11	11JUL11	29JUL11	5d	0
RF40D	Complete Fascia and Roof Metal, Area D	15	04JUL11	22JUL11	11JUL11	29JUL11	5d	0
WP30D	Exterior Sealants, Area D	15	18JUL11	05AUG11	25JUL11	12AUG11	5d	0
RF50D	Misc. Roofing, Area D	10	25JUL11	05AUG11	01AUG11	12AUG11	5d	0
RC60D	Remove Temp Access - Door EX-D184, Area D	5	12SEP11	16SEP11	19SEP11	23SEP11	5d	0
WN20D	Complete Alum Entr D184, Area D	5	19SEP11	23SEP11	26SEP11	30SEP11	5d	0
Classroom Wing - First Floor								
Roughing-in								
HV201	Rough Ductwork Mains, 1st Class	20	28MAR11	22APR11	21MAR11	15APR11	-5d	0
EL201	Electric - Rough Mains, Risers; 1st Class	20	04APR11	29APR11	28MAR11	22APR11	-5d	0
HV301	Rough HVAC Piping, 1st Class	20	04APR11	29APR11	28MAR11	22APR11	-5d	0
PL301	Plumbing - Rough & Test, 1st Class	20	04APR11	29APR11	28MAR11	22APR11	-5d	0
DW201	Interior Metal Stud Framing, 1st Class	20	11APR11	06MAY11	04APR11	29APR11	-5d	0
EL301	Electric - Rough Ptns & Complete, 1st Class	20	18APR11	13MAY11	11APR11	06MAY11	-5d	0
FP201	Fire Protection - Rough & Test, 1st Class	20	18APR11	13MAY11	18APR11	13MAY11	0	0
HV211	Complete Rough Ductwork, 1st Class	15	25APR11	13MAY11	25APR11	13MAY11	0	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
HV401	Controls - Roughing-in, 1st Class	15	25APR11	13MAY11	25APR11	13MAY11	0	0
RC401	Interior Rough Carpentry, 1st Class	15	25APR11	13MAY11	25APR11	13MAY11	0	0
TC301	Telecommunications Rough, 1st Class	20	25APR11	20MAY11	18APR11	13MAY11	-5d	0
PL311	Plumbing - Rough Inspect, 1st Class	5	02MAY11	06MAY11	25APR11	29APR11	-5d	0
HV501	HVAC Pipe Insulation, 1st Class	15	02MAY11	20MAY11	25APR11	13MAY11	-5d	0
PL401	Plumbing - Pipe Covering, 1st Class	10	09MAY11	20MAY11	02MAY11	13MAY11	-5d	0
EL401	Electric - Inspect Rough-in, 1st Class	5	16MAY11	20MAY11	09MAY11	13MAY11	-5d	0
Interior Finishes								
DW301	Drywall, Tape & Sand, 1st Class	20	30MAY11	24JUN11	16MAY11	10JUN11	-10d	0
FS101	Firestopping, 1st Class	15	13JUN11	01JUL11	04JUL11	22JUL11	15d	0
PA101	Prime Paint, 1st Class	15	20JUN11	08JUL11	27JUN11	15JUL11	5d	0
CB101	MB/TB, 1st Class	10	11JUL11	22JUL11	01AUG11	12AUG11	15d	0
DW401	Touch-up Drywall, 1st Class	10	11JUL11	22JUL11	01AUG11	12AUG11	15d	0
FC101	Finish Millwork, 1st Class	10	11JUL11	22JUL11	01AUG11	12AUG11	15d	0
CT101	Ceramic Tile Toilets, 1st Class	15	11JUL11	29JUL11	18JUL11	05AUG11	5d	0
WP201	Interior Caulking, 1st Class	15	11JUL11	29JUL11	25JUL11	12AUG11	10d	0
CL101	Ceiling Grid, 1st Class	20	11JUL11	05AUG11	25JUL11	19AUG11	10d	0
RS101	VCT Rooms, 1st Class	10	25JUL11	05AUG11	22AUG11	02SEP11	20d	0
FC201	Hang Interior Doors, 1st Class	15	25JUL11	12AUG11	15AUG11	02SEP11	15d	0
PL701	Plumbing Finish, 1st Class	15	01AUG11	19AUG11	22AUG11	09SEP11	15d	0
CT201	Wall Tile at Corridors, 1st Class	20	01AUG11	26AUG11	08AUG11	02SEP11	5d	0
CP101	Carpet, 1st Class	5	08AUG11	12AUG11	12SEP11	16SEP11	25d	0
PA201	Finish Paint Walls & Ceilings, 1st Class	15	08AUG11	26AUG11	15AUG11	02SEP11	5d	0
HV701	HVAC Radiation, 1st Class	15	08AUG11	26AUG11	22AUG11	09SEP11	10d	0
HV711	Reg, Grilles, Fans, Finishes, 1st Class	15	08AUG11	26AUG11	05SEP11	23SEP11	20d	0
FC211	Complete Finish Hardware, 1st Class	15	08AUG11	26AUG11	19SEP11	07OCT11	30d	0
CW101	Fixed Casework, 1st Class	20	08AUG11	02SEP11	22AUG11	16SEP11	10d	0
EL701	Lighting Fixtures, 1st Class	20	08AUG11	02SEP11	29AUG11	23SEP11	15d	0
FP401	Fire Protection - Finish Heads, 1st Class	20	08AUG11	02SEP11	29AUG11	23SEP11	15d	0
TP101	Toilet Compartments, 1st Class	10	22AUG11	02SEP11	12SEP11	23SEP11	15d	0
FC111	Finish Millwork at Corridor, 1st Class	5	29AUG11	02SEP11	26SEP11	30SEP11	20d	0
RS301	Linoleum Corridors, 1st Class	10	29AUG11	09SEP11	05SEP11	16SEP11	5d	0
HV801	ATC Controls - Finish, 1st Class	10	29AUG11	09SEP11	12SEP11	23SEP11	10d	0
MS101	Miscellaneous Specialties, 1st Class	10	29AUG11	09SEP11	26SEP11	07OCT11	20d	0
EL801	Electric Finishes, 1st Class	20	29AUG11	23SEP11	05SEP11	30SEP11	5d	0
DW501	Misc. Interior Drywall, 1st Class	10	05SEP11	16SEP11	19SEP11	30SEP11	10d	0

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
TA101	Toilet Accessories, 1st Class	10	05SEP11	16SEP11	26SEP11	07OCT11	15d	0
PL711	Plumbing Fixtures Classrooms, 1st Class	15	05SEP11	23SEP11	19SEP11	07OCT11	10d	0
CL201	Ceiling Tile, 1st Class	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
RS401	Vinyl Base, 1st Class	15	12SEP11	30SEP11	19SEP11	07OCT11	5d	0
TC801	Telecommunications Finish, 1st Class	15	12SEP11	30SEP11	19SEP11	07OCT11	5d	0
PA601	Misc. Painting, 1st Class	5	19SEP11	23SEP11	03OCT11	07OCT11	10d	0
EM101	Entrance Mats, 1st Class	5	26SEP11	30SEP11	03OCT11	07OCT11	5d	0
Completion								
END1	Complete 1st Class	10	03OCT11	14OCT11	10OCT11	21OCT11	5d	0
Classroom Wing - Second Floor								
Roughing-in								
HV202	Rough Ductwork Mains, 2nd Class	20	11APR11	06MAY11	04APR11	29APR11	-5d	0
EL202	Electric - Rough Mains, Riser; 2nd Class	20	18APR11	13MAY11	18APR11	13MAY11	0	0
HV302	Rough HVAC Piping, 2nd Class	20	18APR11	13MAY11	18APR11	13MAY11	0	0
PL302	Plumbing - Rough & Test, 2nd Class	20	18APR11	13MAY11	18APR11	13MAY11	0	0
DW202	Interior Metal Stud Framing, 2nd Class	20	25APR11	20MAY11	18APR11	13MAY11	-5d	0
EL302	Electric - Rough Ptns & Complete, 2nd Class	20	02MAY11	27MAY11	02MAY11	27MAY11	0	0
FP202	Fire Protection - Rough & Test, 2nd Class	20	02MAY11	27MAY11	09MAY11	03JUN11	5d	0
HV212	Complete Rough Ductwork, 2nd Class	15	09MAY11	27MAY11	16MAY11	03JUN11	5d	0
HV402	Controls - Roughing-in, 2nd Class	15	09MAY11	27MAY11	16MAY11	03JUN11	5d	0
RC402	Interior Rough Carpentry, 2nd Class	15	09MAY11	27MAY11	16MAY11	03JUN11	5d	0
TC302	Telecommunications Rough, 2nd Class	20	09MAY11	03JUN11	09MAY11	03JUN11	0	0
PL312	Plumbing - Rough Inspect, 2nd Class	5	16MAY11	20MAY11	16MAY11	20MAY11	0	0
HV502	HVAC Pipe Insulation, 2nd Class	15	16MAY11	03JUN11	16MAY11	03JUN11	0	0
PL402	Plumbing - Pipe Covering, 2nd Class	10	23MAY11	03JUN11	23MAY11	03JUN11	0	0
EL402	Electric - Inspect Rough-in, 2nd Class	5	30MAY11	03JUN11	30MAY11	03JUN11	0	0
Interior Finishes								
DW302	Drywall, Tape & Sand, 2nd Class	20	20JUN11	15JUL11	06JUN11	01JUL11	-10d	0
FS102	Firestopping, 2nd Class	15	04JUL11	22JUL11	04JUL11	22JUL11	0	0
PA102	Prime Paint, 2nd Class	15	11JUL11	29JUL11	27JUN11	15JUL11	-10d	0
CB102	MB/TB, 2nd Class	10	01AUG11	12AUG11	01AUG11	12AUG11	0	0
DW402	Touch-up Drywall, 2nd Class	10	01AUG11	12AUG11	01AUG11	12AUG11	0	0
FC102	Finish Millwork, 2nd Class	10	01AUG11	12AUG11	01AUG11	12AUG11	0	0
CT102	Ceramic Tile Toilets, 2nd Class	15	01AUG11	19AUG11	18JUL11	05AUG11	-10d	0
WP202	Interior Caulking, 2nd Class	15	01AUG11	19AUG11	25JUL11	12AUG11	-5d	0
CL102	Ceiling Grid, 2nd Class	20	01AUG11	26AUG11	25JUL11	19AUG11	-5d	0
RS102	VCT Rooms, 2nd Class	10	15AUG11	26AUG11	22AUG11	02SEP11	5d	0
FC202	Hang Interior Doors, 2nd Class	15	15AUG11	02SEP11	15AUG11	02SEP11	0	0

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
PA202	Finish Paint Walls & Ceilings, 2nd Class	15	22AUG11	09SEP11	15AUG11	02SEP11	-5d	0
PL702	Plumbing Finish, 2nd Class	15	22AUG11	09SEP11	22AUG11	09SEP11	0	0
CT202	Wall Tile at Corridors, 2nd Class	20	22AUG11	16SEP11	08AUG11	02SEP11	-10d	0
CP102	Carpet, 2nd Class	5	29AUG11	02SEP11	12SEP11	16SEP11	10d	0
HV702	HVAC Radiation, 2nd Class	15	29AUG11	16SEP11	22AUG11	09SEP11	-5d	0
HV712	Reg, Grilles, Fans, Finishes, 2nd Class	15	29AUG11	16SEP11	05SEP11	23SEP11	5d	0
FC212	Complete Finish Hardware, 2nd Class	15	29AUG11	16SEP11	19SEP11	07OCT11	15d	0
CW102	Fixed Casework, 2nd Class	20	29AUG11	23SEP11	22AUG11	16SEP11	-5d	0
EL702	Lighting Fixtures, 2nd Class	20	29AUG11	23SEP11	29AUG11	23SEP11	0	0
FP402	Fire Protection - Finish Heads, 2nd Class	20	29AUG11	23SEP11	29AUG11	23SEP11	0	0
TP102	Toilet Compartments, 2nd Class	10	12SEP11	23SEP11	12SEP11	23SEP11	0	0
MS102	Miscellaneous Specialties, 2nd Class	10	12SEP11	23SEP11	26SEP11	07OCT11	10d	0
EL802	Electric Finishes, 2nd Class	20	12SEP11	07OCT11	05SEP11	30SEP11	-5d	0
FC112	Finish Millwork at Corridor, 2nd Class	5	19SEP11	23SEP11	26SEP11	30SEP11	5d	0
RS302	Linoleum Corridors, 2nd Class	10	19SEP11	30SEP11	05SEP11	16SEP11	-10d	0
HV802	ATC Controls - Finish, 2nd Class	10	19SEP11	30SEP11	12SEP11	23SEP11	-5d	0
DW502	Misc. Interior Drywall, 2nd Class	10	26SEP11	07OCT11	19SEP11	30SEP11	-5d	0
TA102	Toilet Accessories, 2nd Class	10	26SEP11	07OCT11	26SEP11	07OCT11	0	0
PL712	Plumbing Fixtures Classrooms, 2nd Class	15	26SEP11	14OCT11	19SEP11	07OCT11	-5d	0
TC802	Telecommunications Finish, 2nd Class	15	26SEP11	14OCT11	19SEP11	07OCT11	-5d	0
CL202	Ceiling Tile, 2nd Class	10	03OCT11	14OCT11	26SEP11	07OCT11	-5d	0
RS402	Vinyl Base, 2nd Class	15	03OCT11	21OCT11	19SEP11	07OCT11	-10d	0
PA602	Misc. Painting, 2nd Class	5	10OCT11	14OCT11	03OCT11	07OCT11	-5d	0
Completion								
END2	Complete 2nd Class	10	24OCT11	04NOV11	10OCT11	21OCT11	-10d	0
Stairs and Elevator								
Foundations and Structure								
MM108	Stairs & Rails C122, Area D	10	21FEB11	04MAR11	14MAR11	25MAR11	15d	0
SL108	Concrete Pan Stairs C122, Area D	5	07MAR11	11MAR11	28MAR11	01APR11	15d	0
MM118	Stairs & Rails D178, Area D	10	07MAR11	18MAR11	04APR11	15APR11	20d	0
SL118	Concrete Pan Stairs D178, Area D	5	21MAR11	25MAR11	18APR11	22APR11	20d	0
SF105	Spray FP, Stairs, Area D	10	18APR11	29APR11	25APR11	06MAY11	5d	0
Roughing-in								
EL208	Electric Rough, Stairs, Area D	10	09MAY11	20MAY11	02MAY11	13MAY11	-5d	0
FP118	Fire Protection Rough, Stairs, Area D	10	09MAY11	20MAY11	02MAY11	13MAY11	-5d	0
HV118	HVAC Rough, Stairs, Area D	10	09MAY11	20MAY11	02MAY11	13MAY11	-5d	0
DW208	Shaft Walls, Elevator & Stairs, Area D	10	16MAY11	27MAY11	09MAY11	20MAY11	-5d	0
Interior Finishes								

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
MM128	Misc. Metals at Elevator	5	30MAY11	03JUN11	08AUG11	12AUG11	50d	0
DW508	Complete Sheetrock, Stairs	10	18JUL11	29JUL11	18JUL11	29JUL11	0	0
PA108	Prime Paint, Stairs	5	01AUG11	05AUG11	01AUG11	05AUG11	0	0
EV108	Elevator	30	01AUG11	09SEP11	15AUG11	23SEP11	10d	0
CL108	Ceiling Grid, Stairs	10	08AUG11	19AUG11	08AUG11	19AUG11	0	0
EL808	Electric Finish, Stairs	10	22AUG11	02SEP11	22AUG11	02SEP11	0	0
FP408	Fire Protection Finish, Stairs	10	22AUG11	02SEP11	22AUG11	02SEP11	0	0
HV708	HVAC Equip & Finishes, Stairs	10	22AUG11	02SEP11	22AUG11	02SEP11	0	0
CT208	Wall Tile, Stairs	15	22AUG11	09SEP11	22AUG11	09SEP11	0	0
CL208	Ceiling Tile, Stairs	10	05SEP11	16SEP11	05SEP11	16SEP11	0	0
MM208	Complete Metal Rails, Stairs	10	05SEP11	16SEP11	05SEP11	16SEP11	0	0
CT218	Porcelain Floor, Elevator	5	12SEP11	16SEP11	26SEP11	30SEP11	10d	0
FC108	Finish Millwork, Stairs	5	12SEP11	16SEP11	26SEP11	30SEP11	10d	0
MM308	Roof Access Treads, Stairs	5	12SEP11	16SEP11	26SEP11	30SEP11	10d	0
PA508	Seal Concrete Floor, Machine Room	5	12SEP11	16SEP11	26SEP11	30SEP11	10d	0
RS208	Resilient Treads/Flooring/Base, Stairs	10	19SEP11	30SEP11	19SEP11	30SEP11	0	0
EM108	Foot Grilles, Stairs	5	03OCT11	07OCT11	03OCT11	07OCT11	0	0
PA208	Finish Paint, Stairs	10	03OCT11	14OCT11	03OCT11	14OCT11	0	0
EM208	Entrance Mats, Stairs	5	10OCT11	14OCT11	10OCT11	14OCT11	0	0
Completion								
EL908	Fire Alarm Test, Elevator	5	19SEP11	23SEP11	03OCT11	07OCT11	10d	0
EV208	Elevator Final Inspection	5	26SEP11	30SEP11	10OCT11	14OCT11	10d	0
ENDS	Complete Stairs, Elevator	5	17OCT11	21OCT11	17OCT11	21OCT11	0	0
Miscellaneous								
Miscellaneous								
Interior Finishes								
EJ209	Exterior Expansion Control	10	23MAY11	03JUN11	29AUG11	09SEP11	70d	0
EJ109	Interior Expansion Control	10	20JUN11	01JUL11	12SEP11	23SEP11	60d	0
MS229	Exterior Building Letters	5	15AUG11	19AUG11	05SEP11	09SEP11	15d	0
MS409	Residential Appliances	5	29AUG11	02SEP11	17OCT11	21OCT11	35d	0
EL809	Electric Finishes, Exterior Building	10	05SEP11	16SEP11	12SEP11	23SEP11	5d	0
GL109	Interior Glazing	10	05SEP11	16SEP11	26SEP11	07OCT11	15d	0
MS309	Fire Ext. & Cabinets	10	12SEP11	23SEP11	10OCT11	21OCT11	20d	0
MS209	Interior Signage	15	12SEP11	30SEP11	03OCT11	21OCT11	15d	0
MS709	Window Treatments	20	12SEP11	07OCT11	26SEP11	21OCT11	10d	0
PA609	Misc. Painting	10	19SEP11	30SEP11	10OCT11	21OCT11	15d	0
MS219	Dedication Plaque	5	03OCT11	07OCT11	28NOV11	02DEC11	40d	0

Pompo/Center Elementary School
Stow, MA

Act ID	Activity Description	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	% Compl
TA109	Complete Toilet Accessories, Misc.	5	10OCT11	14OCT11	17OCT11	21OCT11	5d	0
Completion								
PL807	Plumbing - Gas Inspection	5	01AUG11	05AUG11	08AUG11	12AUG11	5d	0
EL909	Fire Alarm - Final Inspection	5	17OCT11	21OCT11	10OCT11	14OCT11	-5d	0
PL809	Plumbing - Final Inspection	5	17OCT11	21OCT11	17OCT11	21OCT11	0	0
EL919	Electric - Final Inspection	5	24OCT11	28OCT11	17OCT11	21OCT11	-5d	0
Overall Project Completion								
Initial Sitework - Phase 1A								
Completion								
END1A	Complete Phase 1A	0		27AUG10 A		27AUG10 A		100
Phase 1								
Completion								
GC420	Building Commissioning - Phase 1	50	22AUG11	28OCT11	15AUG11	21OCT11	-5d	0
ENDP1	Complete - Phase 1	15	07NOV11	25NOV11	24OCT11	11NOV11	-10d	0
ENFP1	Owner's Float - Phase 1	15	28NOV11	16DEC11	14NOV11	02DEC11	-10d	0
ENSP1	Substantial Completion - Phase 1	0		16DEC11		02DEC11 *	-10d	0
GC600	Owner - Teachers/Staff Move-in Phase 1	16	19DEC11	09JAN12	05DEC11	26DEC11	-10d	0
Phase 2								
Completion								
GC610	Owner Vacate Existing Building	0	10JAN12		27DEC11 *		-10d	0
GC700	Phase 2	121	10JAN12	26JUN12	27DEC11	12JUN12	-10d	0
ENDP2	Substantial Completion - Phase 2	0		26JUN12		12JUN12	-10d	0

P.J. Stella Construction Corp.

Pompo/Center Elem. School, Stow

Submittals with SMMA

by Package with days held

Job No: 21010

Project No: 09020.00 - Stow

Date: 9/27/2010

Package	Submittal	Rev.	Title	Status	Days Held	Latest Dates Sent	Latest Dates Return	BIC
01 29 00			Payment Procedures					
	001	004	Schedule of Values	OUT	24	9/3/2010		SMMA
	023	001	List of Subcontractors	OUT	66	7/23/2010		SMMA
	025	001	List of Contractors Staff assigneme	OUT	63	7/26/2010		SMMA
	027	001	Prel. Const Sched - See 013200-002	OUT	75	7/14/2010		SMMA
	032	001	Init Progress Rpt - See 013200-001	OUT	75	7/14/2010		SMMA
	033	001	Report of PreConstruction Conferenc	OUT	55	8/3/2010		SMMA
	042	001	Emergency Phone Numbers	OUT	63	7/26/2010		SMMA
01 32 00			Construction Progress Documentation					
	001	002	Start-up Schedule (Rev 2)	OUT	75	7/14/2010		SMMA
	002	001	Milestone Overview Schedule	OUT	75	7/14/2010		SMMA
	005	001	Baseline CPM Schedule	OUT	6	9/21/2010		SMMA
01 32 33			Photographic Documentation					
	002	001	Initial Construction Photographs	OUT	4	9/23/2010		SMMA
	004	001	Monthly Construction Photos Aug 10	OUT	13	9/14/2010		SMMA
	021	001	Aerial Photos - July 2010	OUT	4	9/23/2010		SMMA
01 33 00			Submittal Procedures					
	001	002	Submittal Log	OUT	14	9/13/2010		SMMA
	002	001	Submittal Schedule - Baseline	OUT	6	9/21/2010		SMMA
01 50 00			Temporary Facilities and Controls					
	006	001	Weather Protection & Heating Plan	OUT	14	9/13/2010		SMMA
01 81 13			Sustainable Design Requirements					
	002	001	Project Materials Cost Data	OUT	4	9/23/2010		SMMA
	003	001	MA-CHPS Action Plan - Waste Mgmt Pl	OUT	4	9/23/2010		SMMA
	004	001	Material Attributes Calculations	OUT	4	9/23/2010		SMMA
	005	001	IAQ Management Plan	OUT	4	9/23/2010		SMMA
03 30 00			Cast-in-Place Concrete					
	001	004	MA-CHPS Submittals (Redimix)	OUT	27	8/31/2010		SMMA
	040	001	MA-CHPS Submittals (Rebar)	OUT	47	8/11/2010		SMMA
	041	001	Corrosion inhibitor	OUT	34	8/24/2010		SMMA
05 12 00			Structural Steel Framing					
	015	003	Framing Plan Area C Low Roof	OUT	13	9/14/2010		SMMA
	016	003	Framing Plan Area C Mid Roof	OUT	7	9/20/2010		SMMA
	023.3	001	Piece Drawings Area C (Block 3)	OUT	13	9/14/2010		SMMA
	023.4	001	Piece Drawings Area C (Block 4)	OUT	13	9/14/2010		SMMA
	023.5	001	Piece Drawings Area C (Block 5)	OUT	12	9/15/2010		SMMA
	023.6	001	Piece Drawings Area C (Block 6)	OUT	7	9/20/2010		SMMA
	031	001	Shear Stud Drawings	OUT	20	9/7/2010		SMMA
05 21 00			Steel Joist Framing					
	002	001	Layout Shop Dwgs: High Roof C&D	OUT	20	9/7/2010		SMMA
	003	001	Layout Shop Drawings: Gym Roof	OUT	20	9/7/2010		SMMA

Submittals with SMMA

by Package with days held

Package	Submittal	Rev.	Title	Status	Days Held	Latest Dates Sent	Latest Dates Return	BIC
05 21 00			Steel Joist Framing					
	005	001	Detail Drawings	OUT	20	9/7/2010		SMMA
05 31 00			Steel Decking					
	005	001	Low Roof B & C	OUT	20	9/7/2010		SMMA
	006	001	Low Roof/2nd Fl Deck B & C	OUT	20	9/7/2010		SMMA
	007	001	2nd Floor D	OUT	20	9/7/2010		SMMA
	008	001	Mid Roof B & C	OUT	20	9/7/2010		SMMA
	009	001	High Roof B & C	OUT	20	9/7/2010		SMMA
	010	001	Gym Roof C & D	OUT	20	9/7/2010		SMMA
	011	001	Details	OUT	20	9/7/2010		SMMA
07 21 00			Thermal Insulation					
	006	002	MACHPS - Dow Sq. Edge	OUT	27	8/31/2010		SMMA
08 11 13			Hollow Metal Doors and Frames					
	000	001	Substitution Request	OUT	11	9/16/2010		SMMA
08 62 00			Unit Skylights					
	001	002	Product Data	OUT	0	9/27/2010		SMMA
	002	002	Shop Drawings	OUT	0	9/27/2010		SMMA
	006	002	Warranty Sample	OUT	0	9/27/2010		SMMA
	009	001	MA-CHPS Submittals	OUT	0	9/27/2010		SMMA
10 22 26			Operable Partitions					
	001	001	Product Data	OUT	0	9/27/2010		SMMA
	002	001	Shop Drawings	OUT	0	9/27/2010		SMMA
	003	001	Samples for Initial Selection	OUT	0	9/27/2010		SMMA
	007	001	Setting Drawings	OUT	0	9/27/2010		SMMA
	010	001	Sample of special warranty	OUT	0	9/27/2010		SMMA
11 40 00			Foodservice Equipment					
	001	001	Product Data	OUT	14	9/13/2010		SMMA
	002	001	Layout Shop Drawings	OUT	14	9/13/2010		SMMA
	003	001	Wiring Diagrams	OUT	14	9/13/2010		SMMA
	004	001	Piping Diagrams	OUT	14	9/13/2010		SMMA
	014	001	Item #21 & 61 Shop Drawings	OUT	14	9/13/2010		SMMA
	015	001	MA-CHPS Submittals: Item #21 & 61	OUT	14	9/13/2010		SMMA
	016	001	MA-CHPS Submittals: BSC Cutbook	OUT	14	9/13/2010		SMMA
	017	001	MA-CHPS Submittals: Walkin Cooler	OUT	14	9/13/2010		SMMA
	018	001	MA-CHPS Submittals: Exhaust Hood	OUT	14	9/13/2010		SMMA
	019	001	Product Data: Select Stainless	OUT	7	9/20/2010		SMMA
	020	001	Product Data: Duke	OUT	7	9/20/2010		SMMA
22 11 23			Domestic Water Pumps					
	002	001	Mfg Data: In Line Pumps	OUT	5	9/22/2010		SMMA
	003	001	Pump Shop Drawings:	OUT	5	9/22/2010		SMMA
23 05 23			General-Duty Valves For HVAC Piping					
	001	001	Mfg Data: Brass ball valves.	OUT	14	9/13/2010		SMMA
	002	001	Mfg Data: Bronze ball valves	OUT	14	9/13/2010		SMMA
	003	001	Mfg Data: Single-flange butterfly	OUT	14	9/13/2010		SMMA
	004	001	Mfg Data: Grooved-end butterfly	OUT	14	9/13/2010		SMMA

Submittals with SMMA

by Package with days held

Package	Submittal	Rev.	Title	Status	Days Held	Latest Dates Sent	Latest Dates Return	BIC
23 05 23			General-Duty Valves For HVAC Piping					
	005	001	Mfg Data: Bronze lift check valves	OUT	14	9/13/2010		SMMA
	006	001	Mfg Data: Bronze swing check valves	OUT	14	9/13/2010		SMMA
	007	001	Mfg Data: Bronze gate valves	OUT	14	9/13/2010		SMMA
23 51 00			Breechings, Chimneys, and Stacks					
	001	001	Mfg Data: B-Vent	OUT	18	9/9/2010		SMMA
	002	001	Mfg Data: CGII Design Manual	OUT	18	9/9/2010		SMMA
	003	001	Mfg Data: Corr-Guard	OUT	18	9/9/2010		SMMA
26 05 00			Common Work Results For Electrical					
	001	001	Mfg Data: Access Panels	OUT	0	9/27/2010		SMMA
	002	001	Mfg Data: Conduit Sleeves	OUT	0	9/27/2010		SMMA
	003	001	Mfg Data: Steel Channels	OUT	0	9/27/2010		SMMA
	004	001	Mfg Data: Non Metalic Grout	OUT	0	9/27/2010		SMMA
26 05 26			Grounding and Bonding for Electrica					
	001	001	Ground Clamps	OUT	0	9/27/2010		SMMA
	002	001	Mfg Data: Conductors	OUT	0	9/27/2010		SMMA
	003	001	Mfg Data: Connectors	OUT	0	9/27/2010		SMMA
	004	001	Mfg Data: Grounding electrodes	OUT	0	9/27/2010		SMMA
	008	001	Ground Electrodes	OUT	0	9/27/2010		SMMA
26 05 29			Hangers and Supports for Electrical					
	001	001	Mfg Data:Steel slotted support sys.	OUT	0	9/27/2010		SMMA
	002	001	Mfg Data:Steel slotted support sys.	OUT	0	9/27/2010		SMMA
	006	001	Mfg Data: Concrete anchors.	OUT	0	9/27/2010		SMMA
	007	001	Mfg Data: Vibration mounts.	OUT	0	9/27/2010		SMMA
26 05 33			Raceway and Boxes for Electrical Sy					
	001	001	Mfg Data: Metal condult and tubing	OUT	0	9/27/2010		SMMA
	002	001	Mfg Data: Metal conduit and tubing	OUT	0	9/27/2010		SMMA
	003	001	Mfg Data: Nonmetallic condult and t	OUT	0	9/27/2010		SMMA
	004	001	Mfg Data: Fittings	OUT	0	9/27/2010		SMMA
	005	001	Mfg Data: Metal wireways	OUT	0	9/27/2010		SMMA
	006	001	Mfg Data: Surface raceways	OUT	0	9/27/2010		SMMA
	007	001	Mfg Data: Pull and junction boxes	OUT	0	9/27/2010		SMMA
	008	001	Mfg Data: Outlet and switch boxes	OUT	0	9/27/2010		SMMA
	010	001	Mfg Data: Sleeves for raceways	OUT	0	9/27/2010		SMMA
	014	001	Mfg Data: Pull and junction boxes	OUT	0	9/27/2010		SMMA
	015	001	Mfg Data: Pull and junction boxes	OUT	0	9/27/2010		SMMA
	016	001	Mfg Data: Pull and junction boxes	OUT	0	9/27/2010		SMMA
	017	001	Mfg Data: Pull and junction boxes	OUT	0	9/27/2010		SMMA
	018	001	Mfg Data: Sleeves for raceways	OUT	0	9/27/2010		SMMA
31 20 00			Earth Moving					
	009.2	001	Gravel Fill (Onsite processed)	OUT	3	9/24/2010		SMMA

Submittals with SMMA

by Package with days held

Job No: 21010

Project No: 09020.00 - Stow

Date: 9/27/2010

Package	Submittal	Rev.	Title	Status	Days Held	Latest Dates Sent	Latest Dates Return	BIC
31 20 00			Earth Moving					
	013.2	001	Gravel Fill (1 1/2" Dense Graded)	OUT	3	9/24/2010		SMMA
	013.3	001	Granular Fill (Onsite processed)	OUT	3	9/24/2010		SMMA
33 31 00			Sanitary Utility Sewerage System					
	008	002	14,000 Gallon Recirculation Trap	OUT	10	9/17/2010		SMMA
33 31 10			Sanitary Sewerage Pump Station					
	002	001	Pump System Mfg Data	OUT	14	9/13/2010		SMMA
	003	001	Pump System Layout Shop Drawing	OUT	14	9/13/2010		SMMA
	004	001	Wiring Diagrams	OUT	14	9/13/2010		SMMA
	008	001	Risers & Accessories	OUT	10	9/17/2010		SMMA

C M S

RFI / Response LOG

Stow Center Elementary School

RFI#	Subject / Description	RFI Date	Returned
001	Grade beam reinforcing	6/15/2010	6/16/2010
002	30" drain line note	6/21/2010	6/25/2010
003	Enclosure fence windscreen	6/21/2010	6/23/2010
004	Roof drain piping	6/22/2010	6/25/2010
005	Part B canopy foundation	6/29/2010	7/15/2010
006	Survey information	7/16/2010	7/22/2010
007	Materials attributes calculations	7/19/2010	7/23/2010
008	Primary electric duct-bank conduit	7/23/2010	7/26/2010
009	Electric service pole	7/27/2010	8/27/2010
010	Electric panel at existing building	7/28/2010	8/6/2010
011	Sturo RFI#1 - Col's on line W	7/28/2010	8/2/2010
012	Sturo RFI#2 - Typ. Bracing gusset	7/28/2010	8/2/2010
013	Addendum #1 Footing Change	7/29/2010	8/20/2010
014	Pole riser conduits	7/30/2010	8/2/2010
015	Pier dimensions	8/2/2010	8/3/2010
016	Storm drain headwall	8/3/2010	8/5/2010
017	Slab on grade base course	8/6/2010	8/6/2010
018	Footing subgrade preparation	8/6/2010	8/6/2010
019	Phase 1A Asbestos quanitities	8/6/2010	8/27/2010
020	Sturo RFI3 davit locations & dims	8/6/2010	9/2/2010
021	Site grading information	8/13/2010	8/27/2010
022	Parts A + B roof details	8/12/2010	8/13/2010
022.2	Parts A + B roof details	8/19/2010	8/24/2010

023	0.40 W/C Concrete	8/17/2010	8/18/2010
023.2	0.40 W/C Concrete	8/19/2010	8/20/2010
024	Building layout discrepancies	8/17/2010	8/18/2010
025	Wood flooring systems	8/17/2010	8/18/2010
026	Basketball backstops supports	8/18/2010	8/20/2010
027	Lobby skylight size	8/19/2010	8/24/2010
028	Part A existing door openings	8/19/2010	8/20/2010
029	Waterproofing dimension	8/20/2010	9/2/2010
030	Dim and size	8/22/2010	8/31/2010
031	Hole at brace	8/22/2010	8/27/2010
032	Screen wall	8/22/2010	8/31/2010
033	Column	8/22/2010	8/31/2010
034	Column prep	8/22/2010	8/27/2010
034.1	Column prep	8/22/2010	8/27/2010
034.2	Column prep	8/30/2010	9/3/2010
035	Stair D178	8/22/2010	8/31/2010
036	Skylight frame	8/22/2010	8/31/2010
037	Edge of slab	8/22/2010	8/31/2010
038	Frame SF14	8/22/2010	8/31/2010
039	Curtain wall	8/22/2010	8/31/2010
040	C-D corner	8/25/2010	9/2/2010
041	masonry ties	8/26/2010	8/27/2010
042	det. 3/s2.03	8/26/2010	9/3/2010
043	dim at 24 & 30	8/26/2010	9/2/2010
044	Bldg D connections	8/26/2010	9/2/2010
045	Applied fireproofing scope	8/26/2010	8/31/2010
046	Platform floor system	8/27/2010	9/2/2010
047	Climbing wall @ gym	8/27/2010	9/2/2010
048	Dim at F-line	8/28/2010	9/2/2010
049	Fire tank access manholes	8/30/2010	9/3/2010

050	Operable window color	8/30/2010	8/31/2010
051	Sloped glazing mfg	8/30/2010	8/31/2010
052	Onsite reuse of materials	8/31/2010	9/2/2010
053	Wood doors glazing	9/1/2010	9/2/2010
054	Composite wall panels	9/1/2010	9/3/2010
055	Pumping concrete	9/1/2010	
056	Ftg subgrade @ fire pump pit	9/3/2010	9/7/2010
057	Operable vents in cur.	9/7/2010	9/9/2010
058	CW6 material	9/7/2010	9/9/2010
059	Window opg clarification	9/7/2010	9/9/2010
060	Storefront face dimes	9/7/2010	9/8/2010
061	Stair C122 fire rating	9/7/2010	
062	Sloped glazing	9/7/2010	9/20/2010
063	R.S.F. Cincotta	9/7/2010	9/9/2010
064	Titan roofing bond letters	9/8/2010	
065	Kitchen equipment customer consent	9/9/2010	
066	Detectable warning panels	9/10/2010	9/16/2010
067	Watertight seals	9/10/2010	9/16/2010
068	Electronic scoreboards	9/10/2010	9/13/2010
069	Vented Deck	9/14/2010	9/17/2010
070	Spandrel glass	9/14/2010	9/16/2010
071	Roof Davit bracket	9/15/2010	9/17/2010
072	Elevation discrepancies	9/15/2010	9/17/2010
073	Elevations at 14/N	9/15/2010	9/17/2010
074	Screen wall	9/15/2010	9/20/2010
075	Gas service pit	9/16/2010	9/16/2010
075.2	Gas service pit	9/20/2010	
076	Tube steel elev.	9/16/2010	9/17/2010
077	El. Chan @ CW	9/17/2010	9/17/2010
078	El. @ Grid l, M&F	9/17/2010	9/21/2010
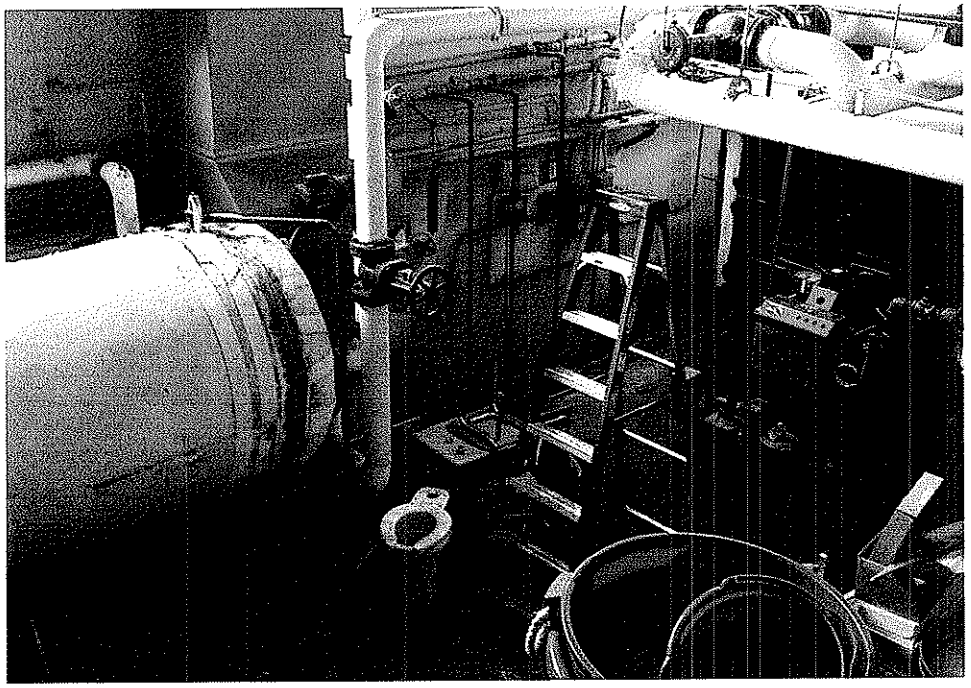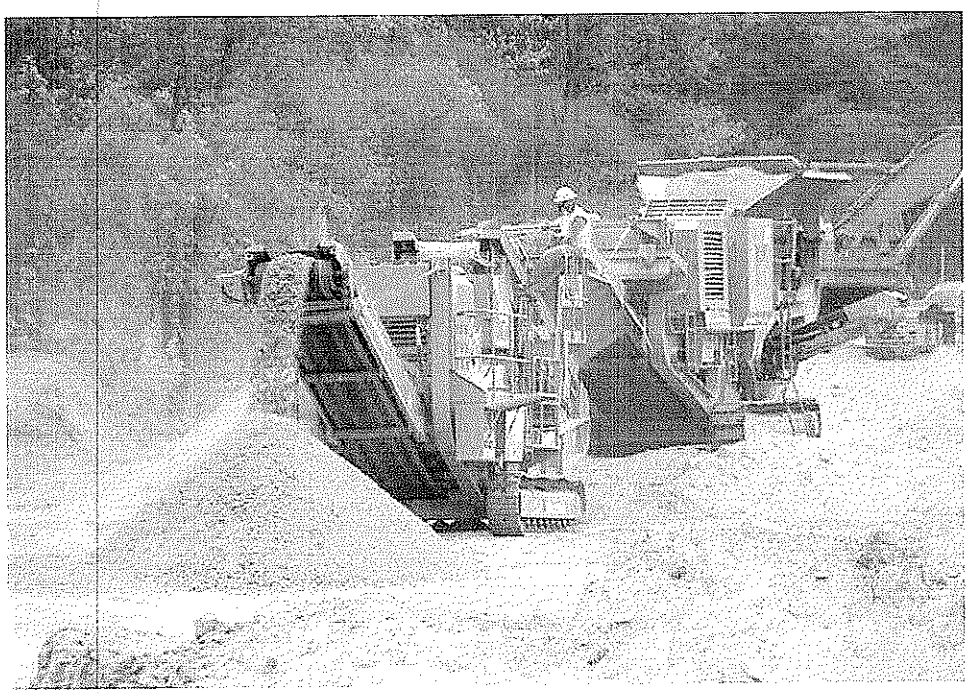
079	Longspan Joists @ Gym	9/17/2010	
080	Exposed structural steel finish	9/17/2010	9/23/2010
081	Pump Station Dims	9/17/2010	9/21/2010
082	W30x90 Elevation	9/17/2010	
083	W27x55 Elevation	9/17/2010	
084	Bent Plate Elevation	9/17/2010	
085	Bent Plate Elevation	9/17/2010	
086	Bent Plate Elevation	9/17/2010	
087	Glazing color match	9/20/2010	9/21/2010
088	CW #6 material	9/20/2010	
089	Maintenance building location	9/22/2010	9/23/2010
090	Entrance sign details	9/27/2010	
091	Outrigger at 30.1 sturo RFI 41	9/27/2010	
092	Exterior soffit expan joint detail	9/27/2010	
093	Screen wall connection Sturo RFI 44	9/27/2010	
094	Joint shop drawings	9/28/2010	
095	Sloped glazing	9/28/2010	
096	Elevator scope clairification	9/30/2010	
097	Motorized shades scope clairf.	9/28/2010	
098	Sturo RFI 42 dimensions for W8x10	9/28/2010
